





## **Pennies for Progress**

Pennies 2

Prepared for Council Meeting on  
May 20, 2019

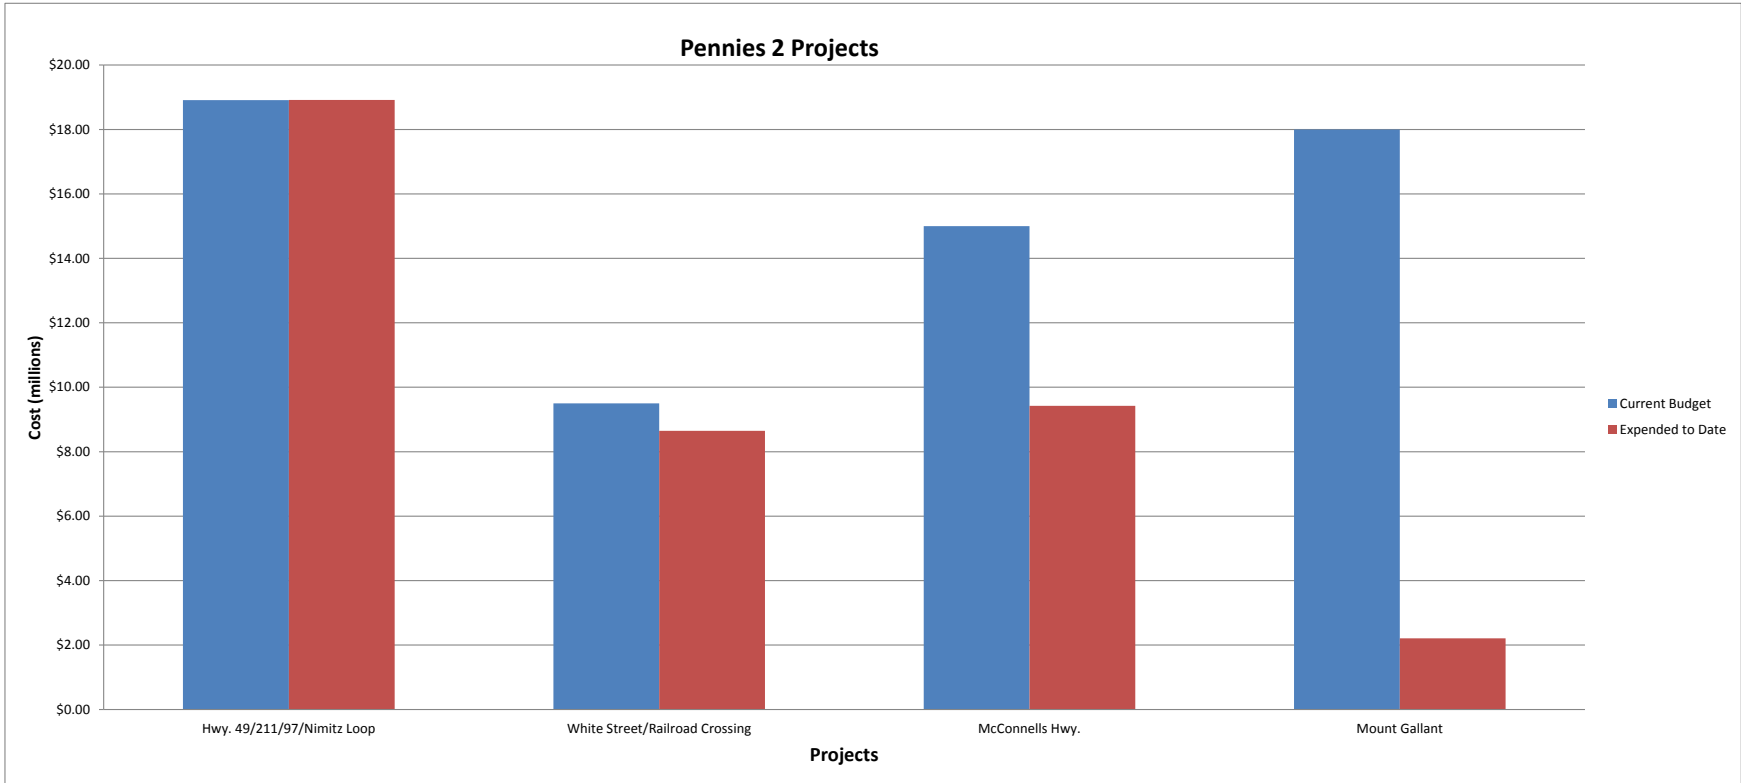


Project	Current Budget	Expended to Date	Status
Hwy. 49/211/97/Nimitz Loop	\$18.91	\$18.91	Under construction
White Street/Railroad Crossing	\$9.50	\$8.65	Complete
McConnells Hwy.	\$15.00	\$9.42	Under construction
Mount Gallant	\$18.00	\$2.21	Finalizing plans/utility coordination

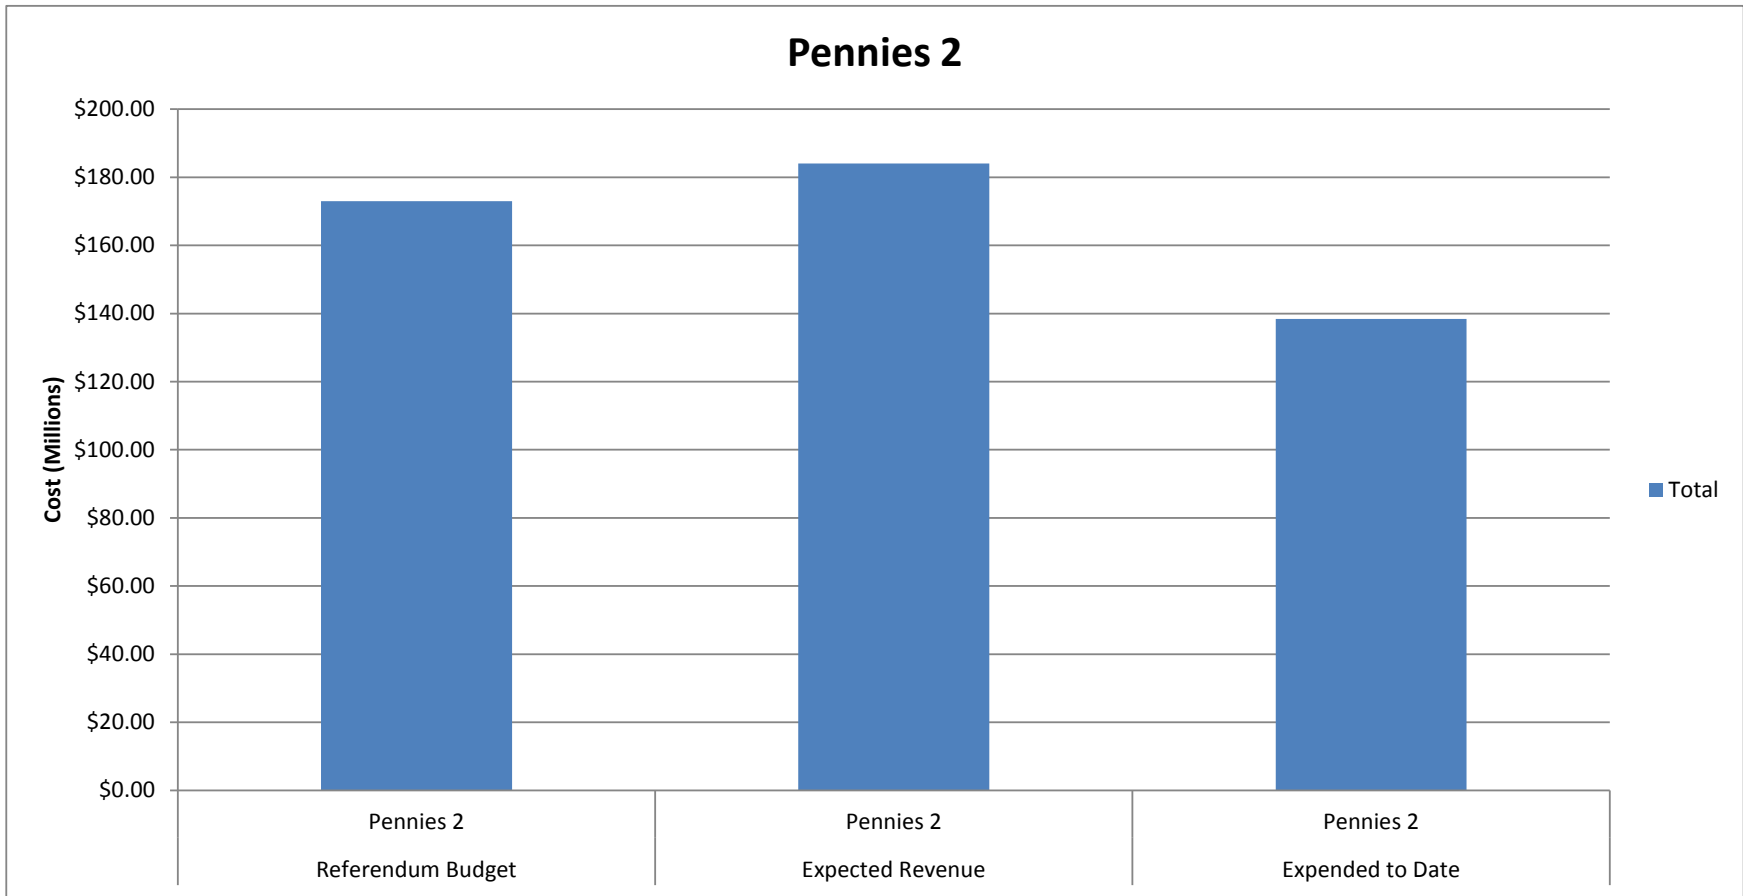

		Total
Referendum Budget	Pennies 2	\$173.00
Expected Revenue	Pennies 2	\$184.00
Expended to Date	Pennies 2	\$138.39

\* Dollars are in millions


## Hwy. 97 / 211 / 97 / Nimitz Loop

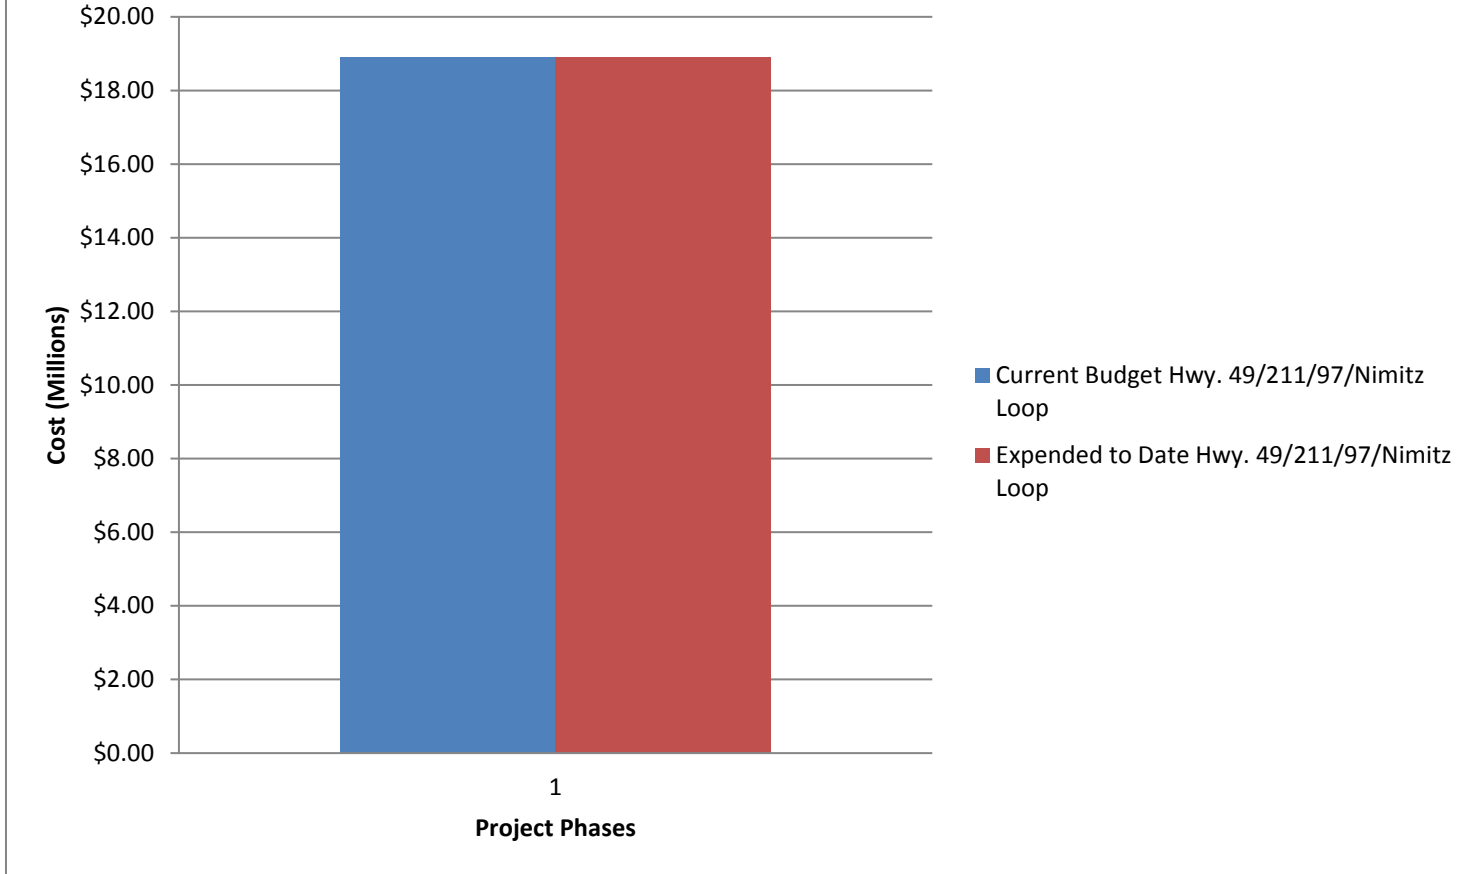

Project Status: Under construction  
Expenses are updated through: May 10, 2019

\* Managed by SCDOT. Funds have already been submitted to SCDOT.


## White Street / Railroad Crossing

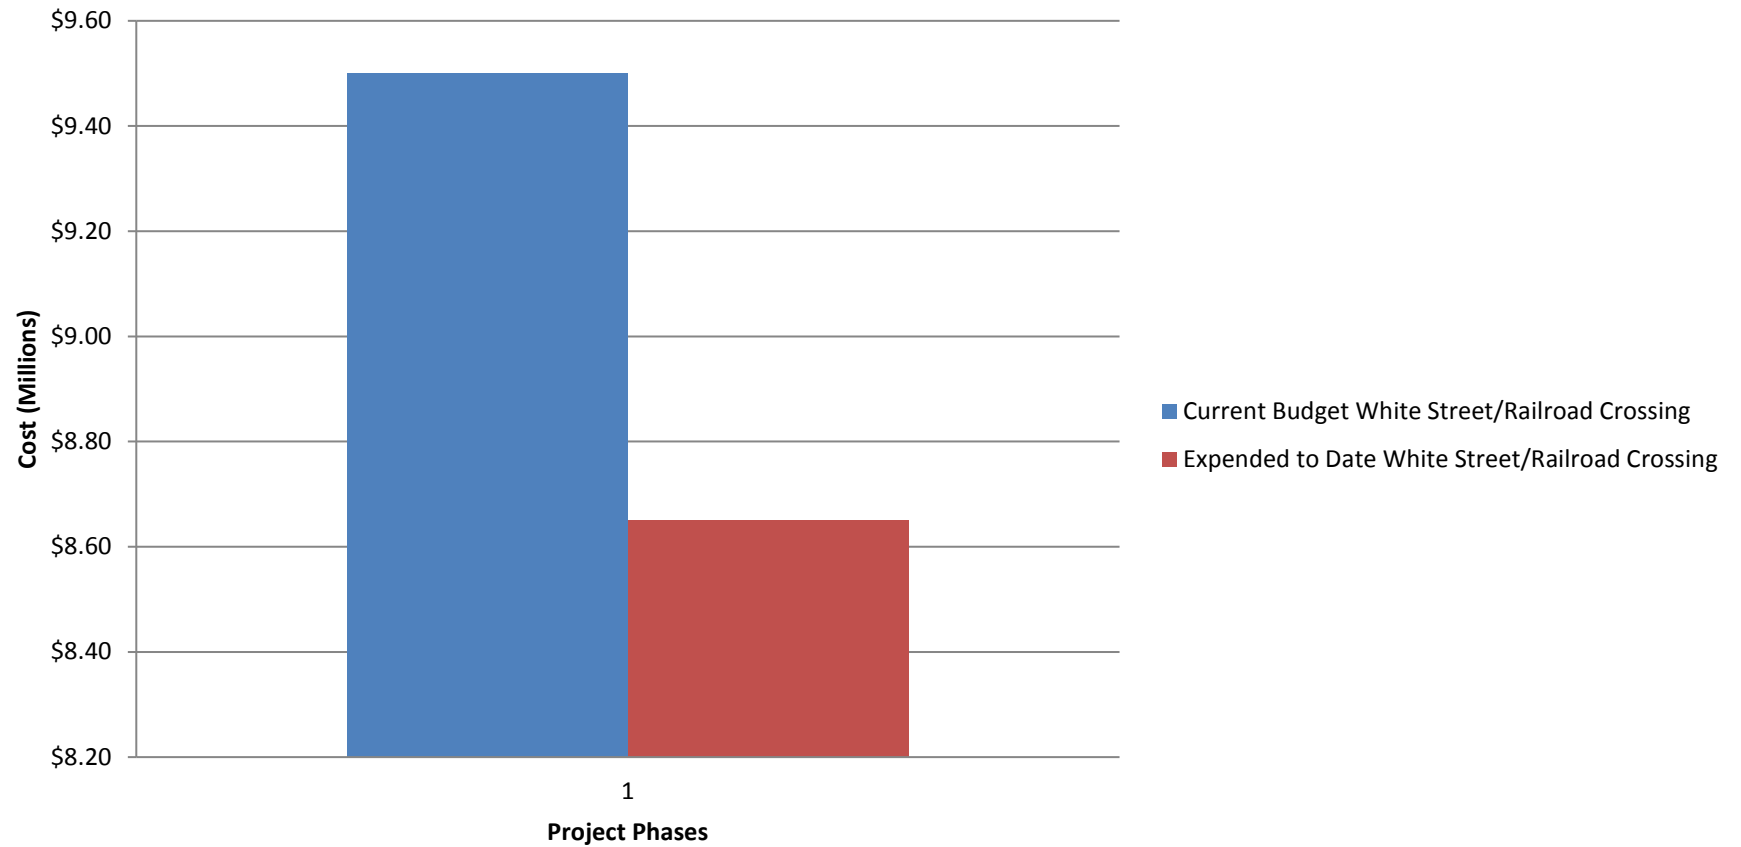

Project Status: Complete


Expenses are updated through: May 10, 2019

## McConnells Highway Highway 901 to Eastview Road

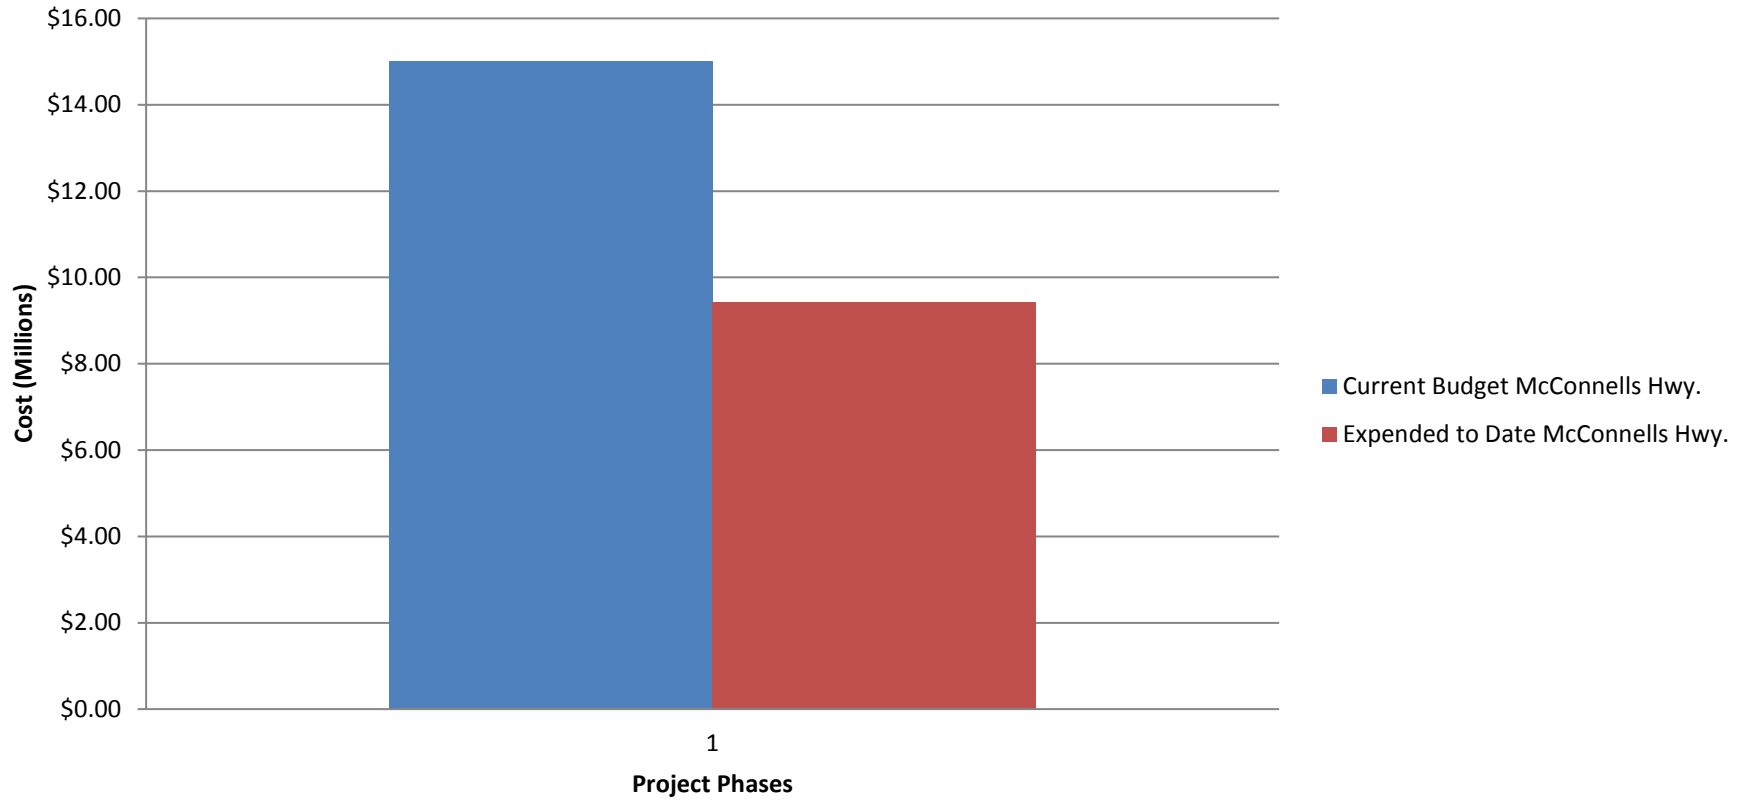

Project Status: Under construction  
Expenses are updated through: May 10, 2019

## Mount Gallant Anderson Road to Dave Lyle Blvd

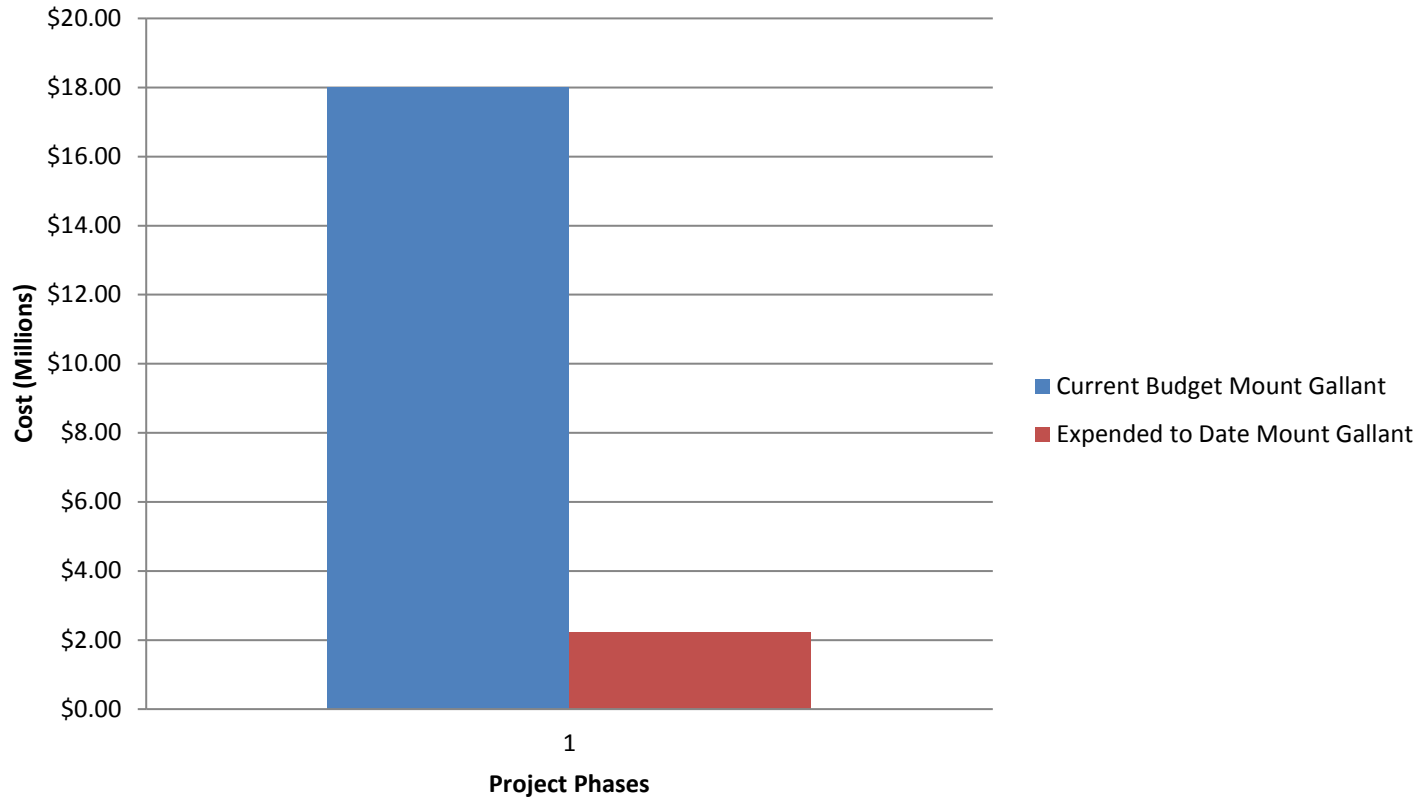

Project Status: Finalizing plans/utility coordination

Expenses are updated through: May 10, 2019




## **Pennies for Progress**


Pennies 3

Prepared for Council Meeting on  
May 20, 2019



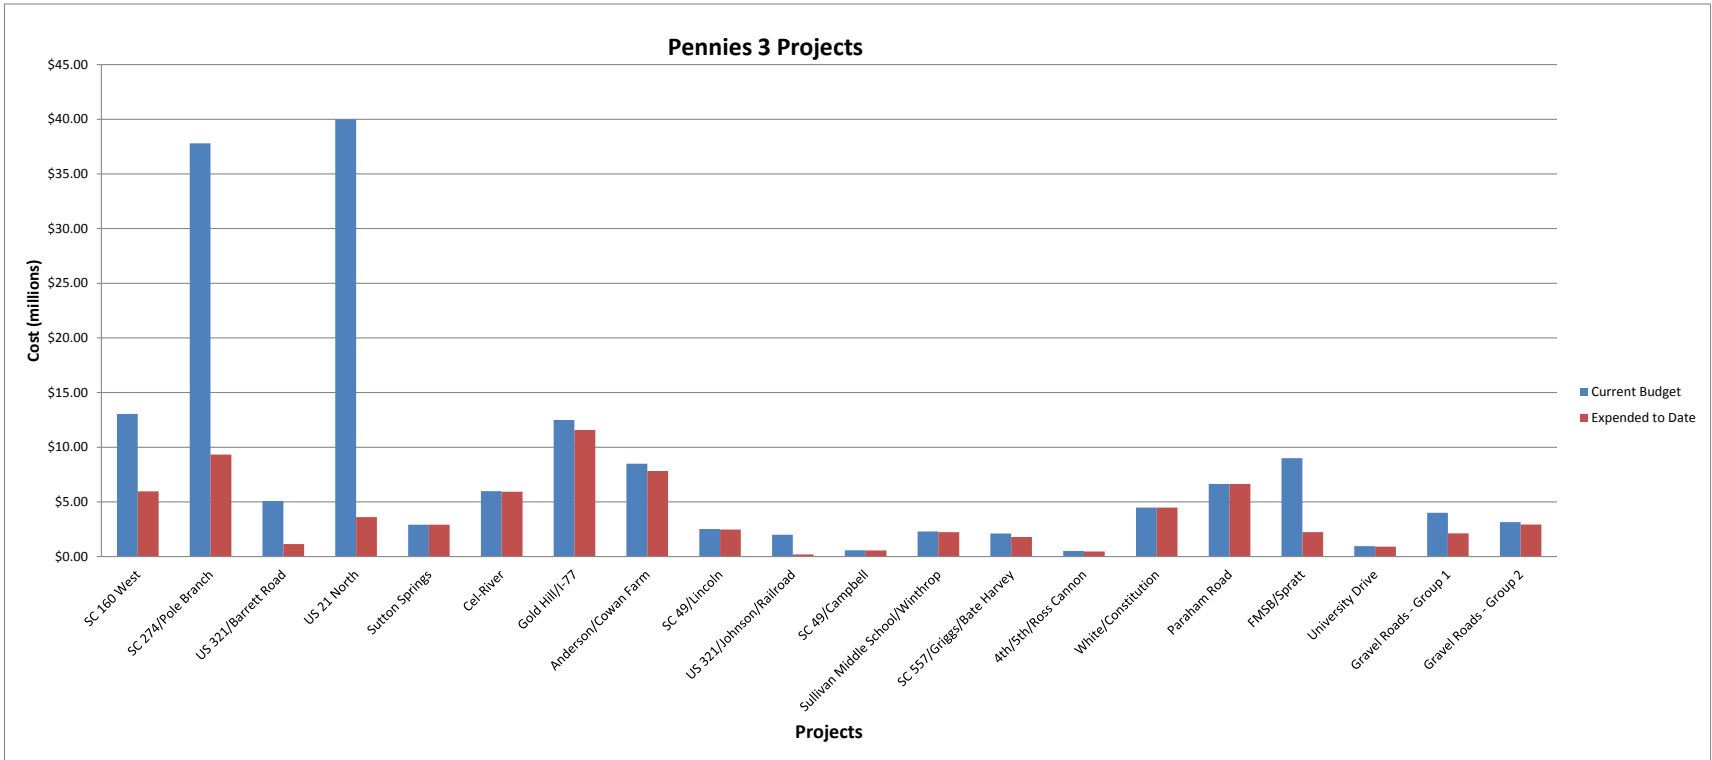

Project	Current Budget	Expended to Date	Status
SC 160 West	\$13.05	\$5.97	Under construction
SC 274/Pole Branch	\$37.80	\$9.33	Under construction
US 321/Barrett Road	\$5.08	\$1.14	Under construction
US 21 North	\$40.00	\$3.61	Acquiring Right-of-Way
Sutton Springs	\$2.91	\$2.91	Complete
Cel-River	\$5.98	\$5.93	Complete
Gold Hill/I-77	\$12.50	\$11.57	Bids Received
Anderson/Cowan Farm	\$8.50	\$7.83	Under construction
SC 49/Lincoln	\$2.53	\$2.46	Complete
US 321/Johnson/Railroad	\$2.00	\$0.20	Acquiring Right-of-Way
SC 49/Campbell	\$0.58	\$0.56	Complete
Sullivan Middle School/Winthrop	\$2.30	\$2.24	Under construction
SC 557/Griggs/Bate Harvey	\$2.12	\$1.79	Complete
4th/5th/Ross Cannon	\$0.50	\$0.46	Complete
White/Constitution	\$4.48	\$4.48	Complete
Paraham Road	\$6.65	\$6.65	Complete
FMSB/Spratt	\$9.00	\$2.23	Final Plans
University Drive	\$0.95	\$0.91	Complete
Gravel Roads - Group 1	\$4.00	\$2.12	Ongoing
Gravel Roads - Group 2	\$3.15	\$2.93	Ongoing

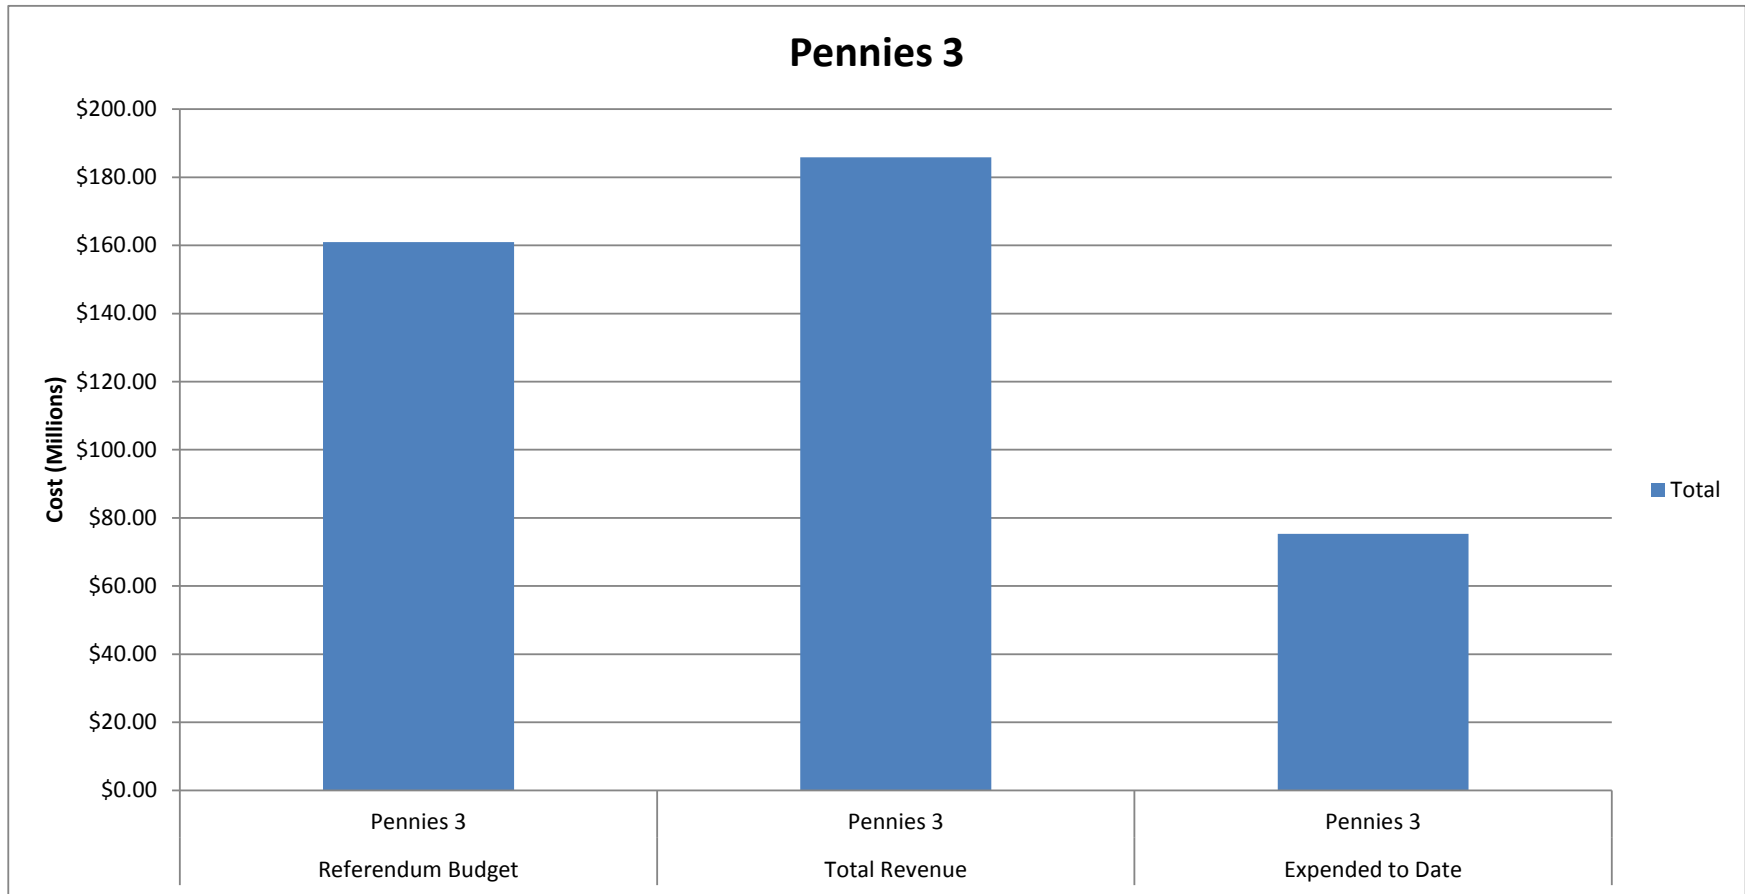


		Total
Referendum Budget	Pennies 3	\$161.00
Total Revenue	Pennies 3	\$185.88
Expended to Date	Pennies 3	\$75.34

\* Dollars are in millions

# SC 160 West


## Gold Hill Road to NC State Line

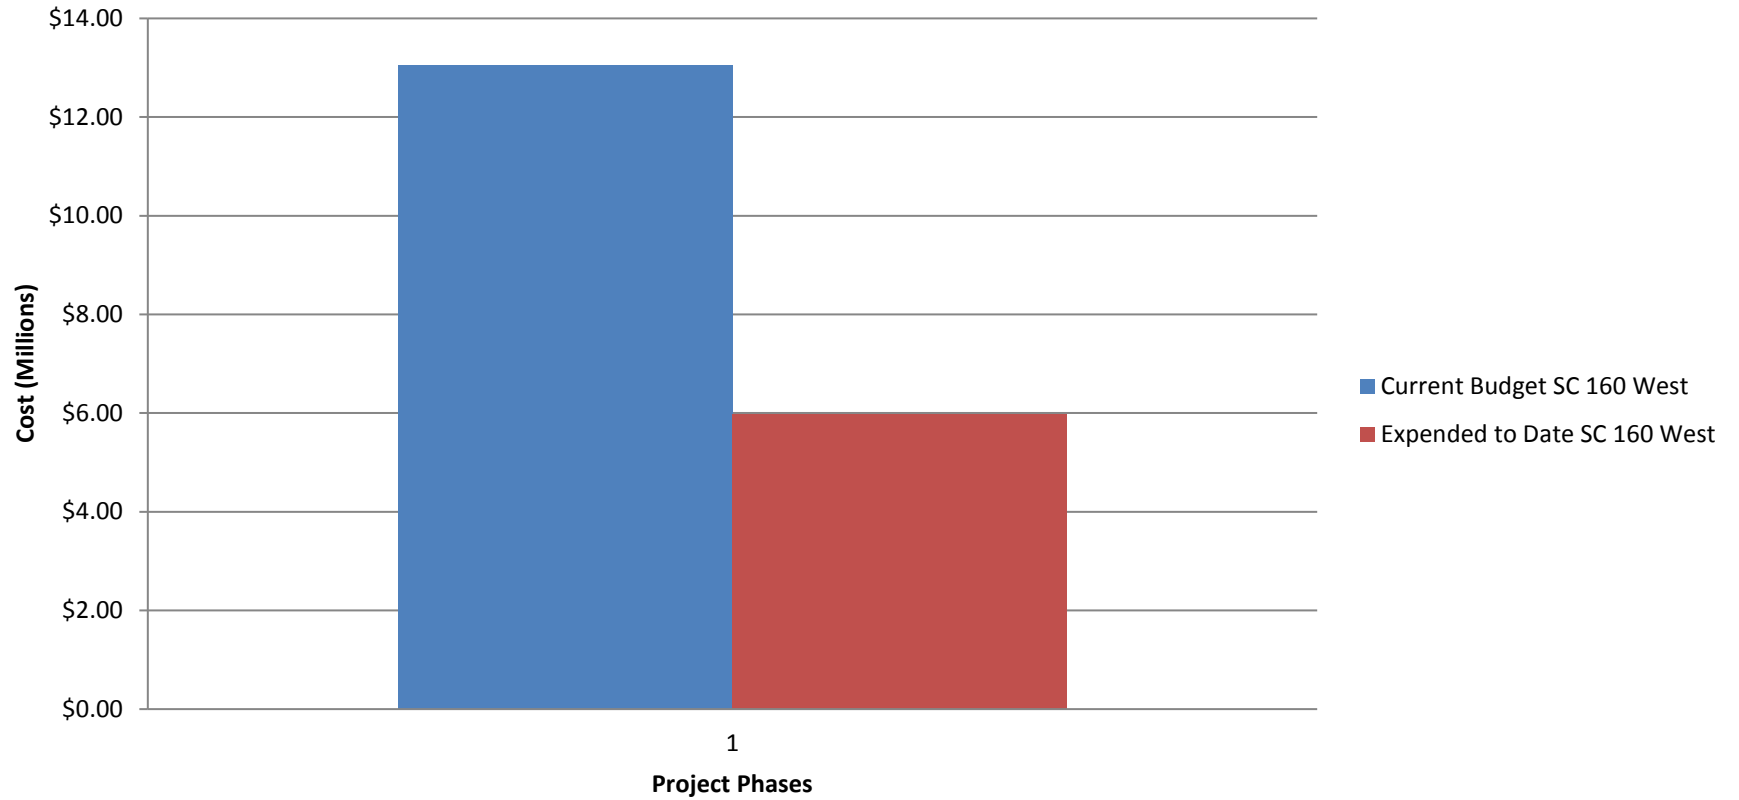

Project Status: Under construction  
Expenses are updated through: May 10, 2019


# 274 Pole Branch

Hwy 274: Highway 49 to Pole Branch Road  
Pole Branch: Highway 274 to NC State Line

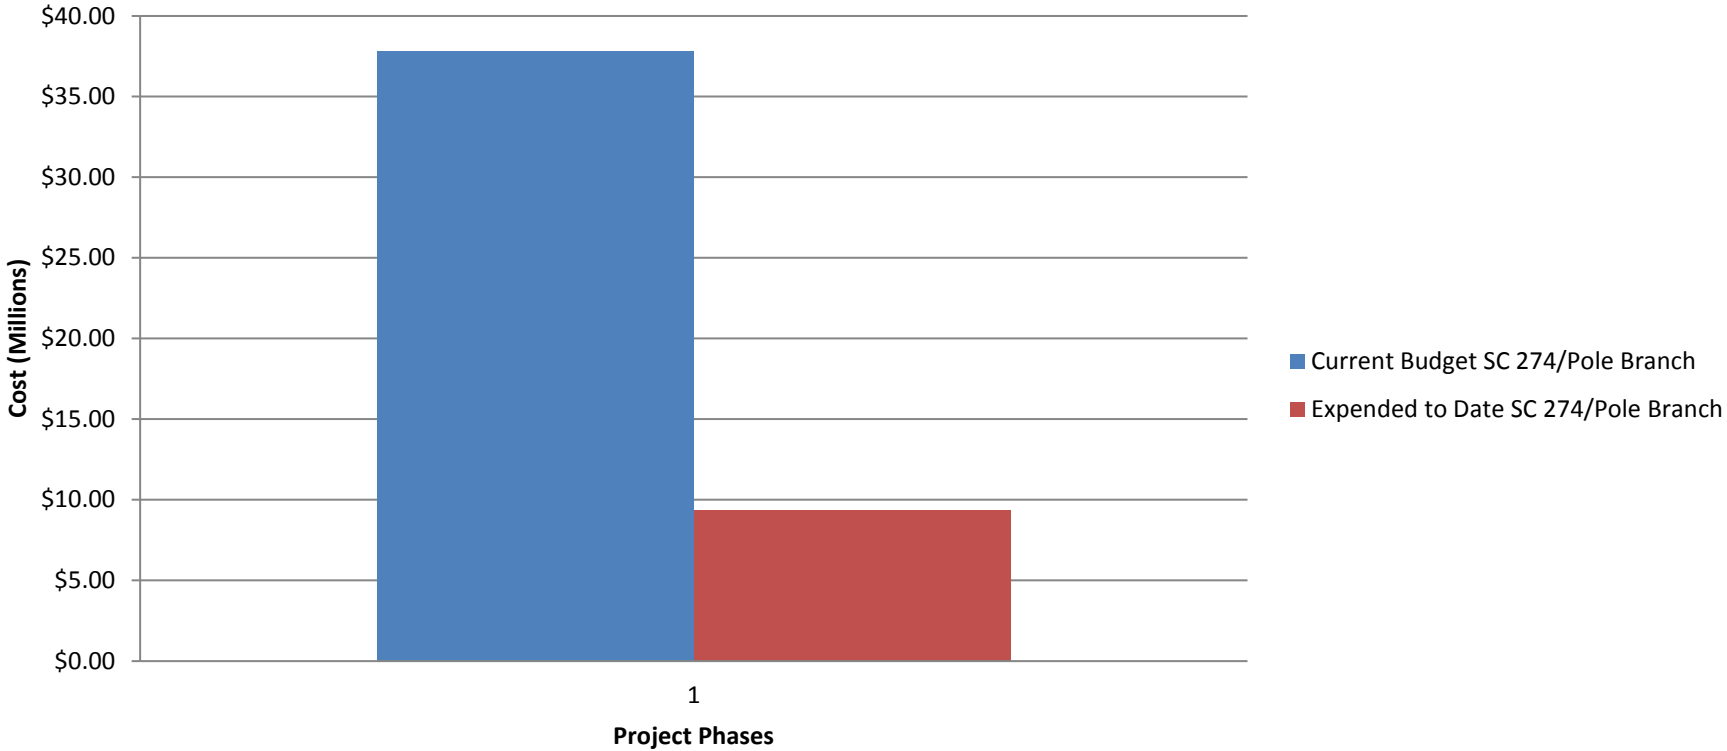

Project Status: Under construction  
Expenses are updated through: May 10, 2019


## US 321 - Barrett Connector Road

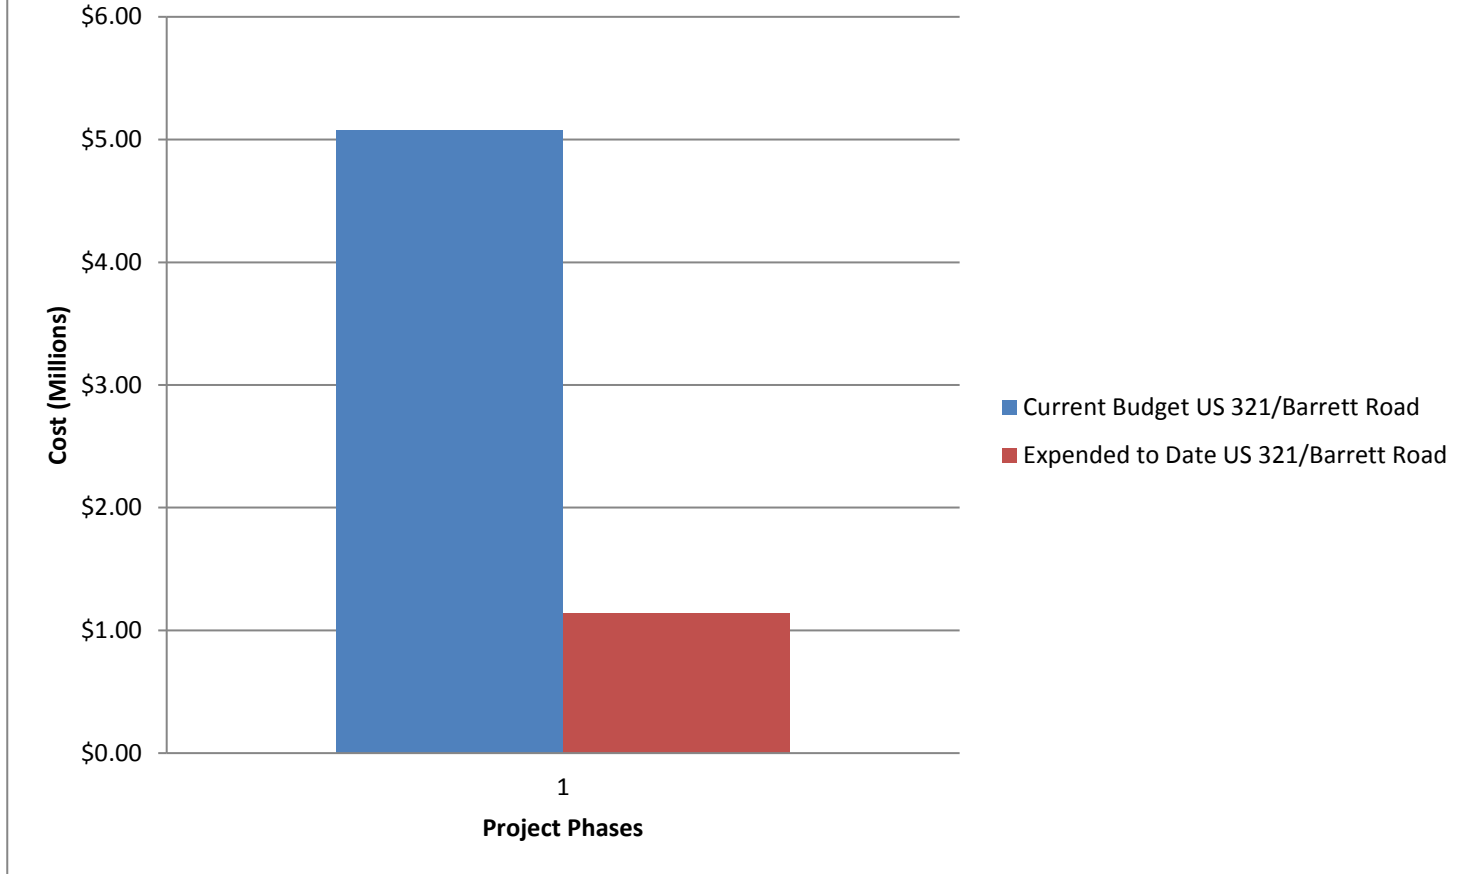

Project Status: Under construction


Expenses are updated through: May 10, 2019

**US 21 North/Highway 51**  
**US 21: Springfield Parkway to Springhill Farm Road**  
**Hwy 51: US 21 to NC State Line**

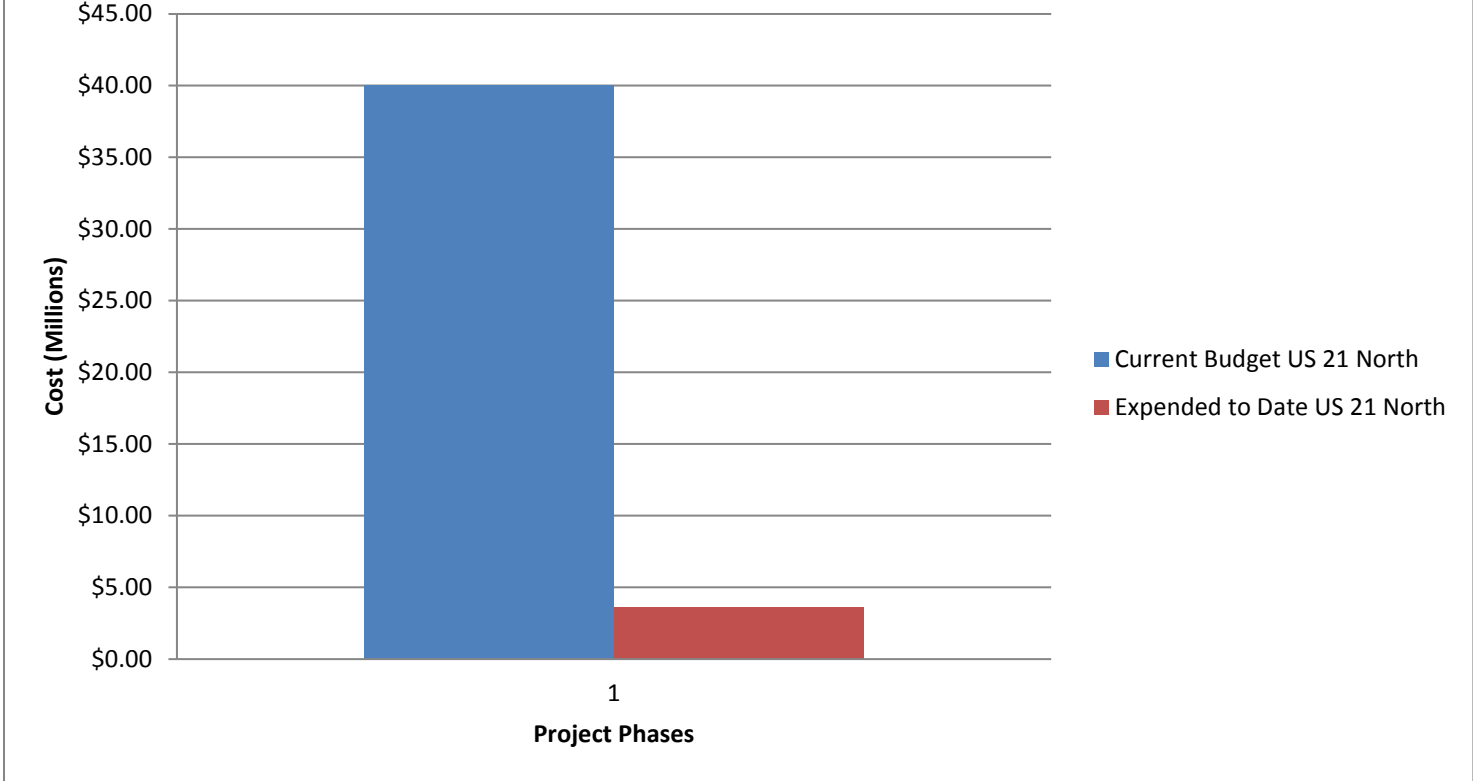

Project Status: Acquiring Right-of-Way  
Expenses are updated through: May 10, 2019

# Sutton Springs

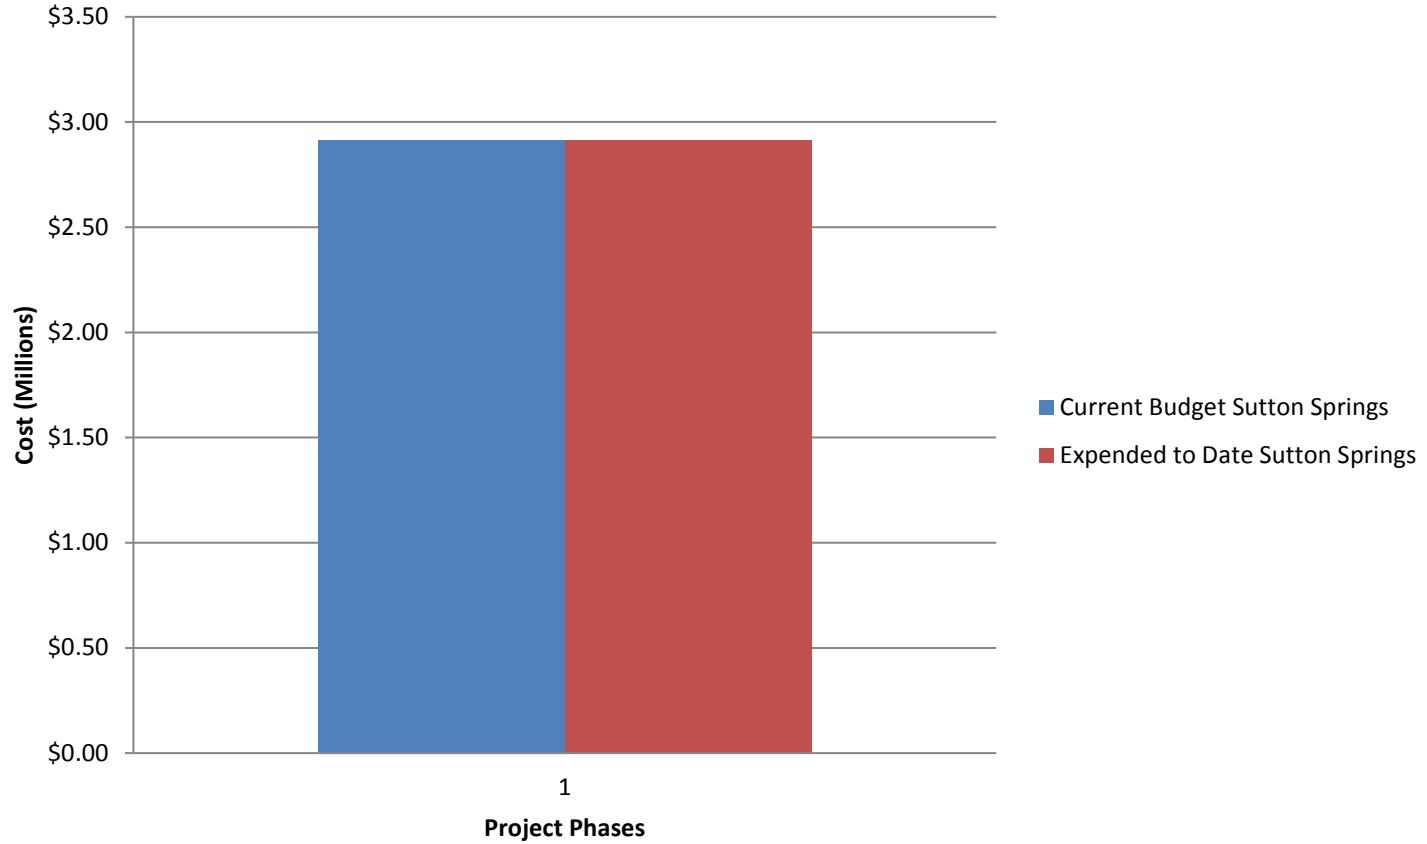


Project Status: Complete

Expenses are updated through: May 10, 2019

# Cel-River


## Cherry Road to Cherry Street

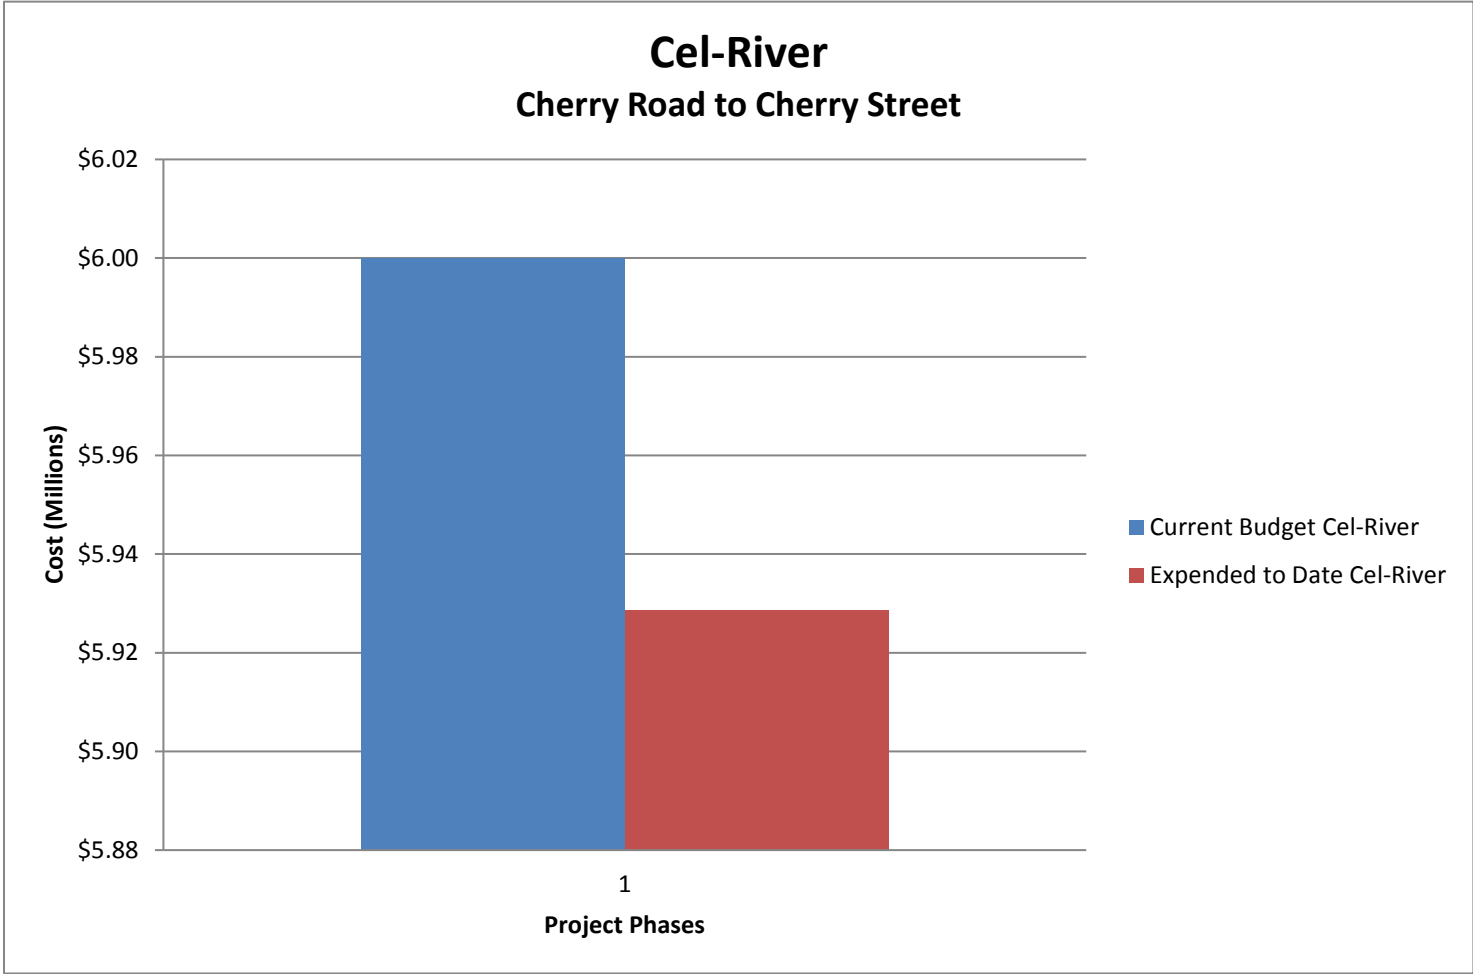

Project Status: Complete

Expenses are updated through: May 10, 2019




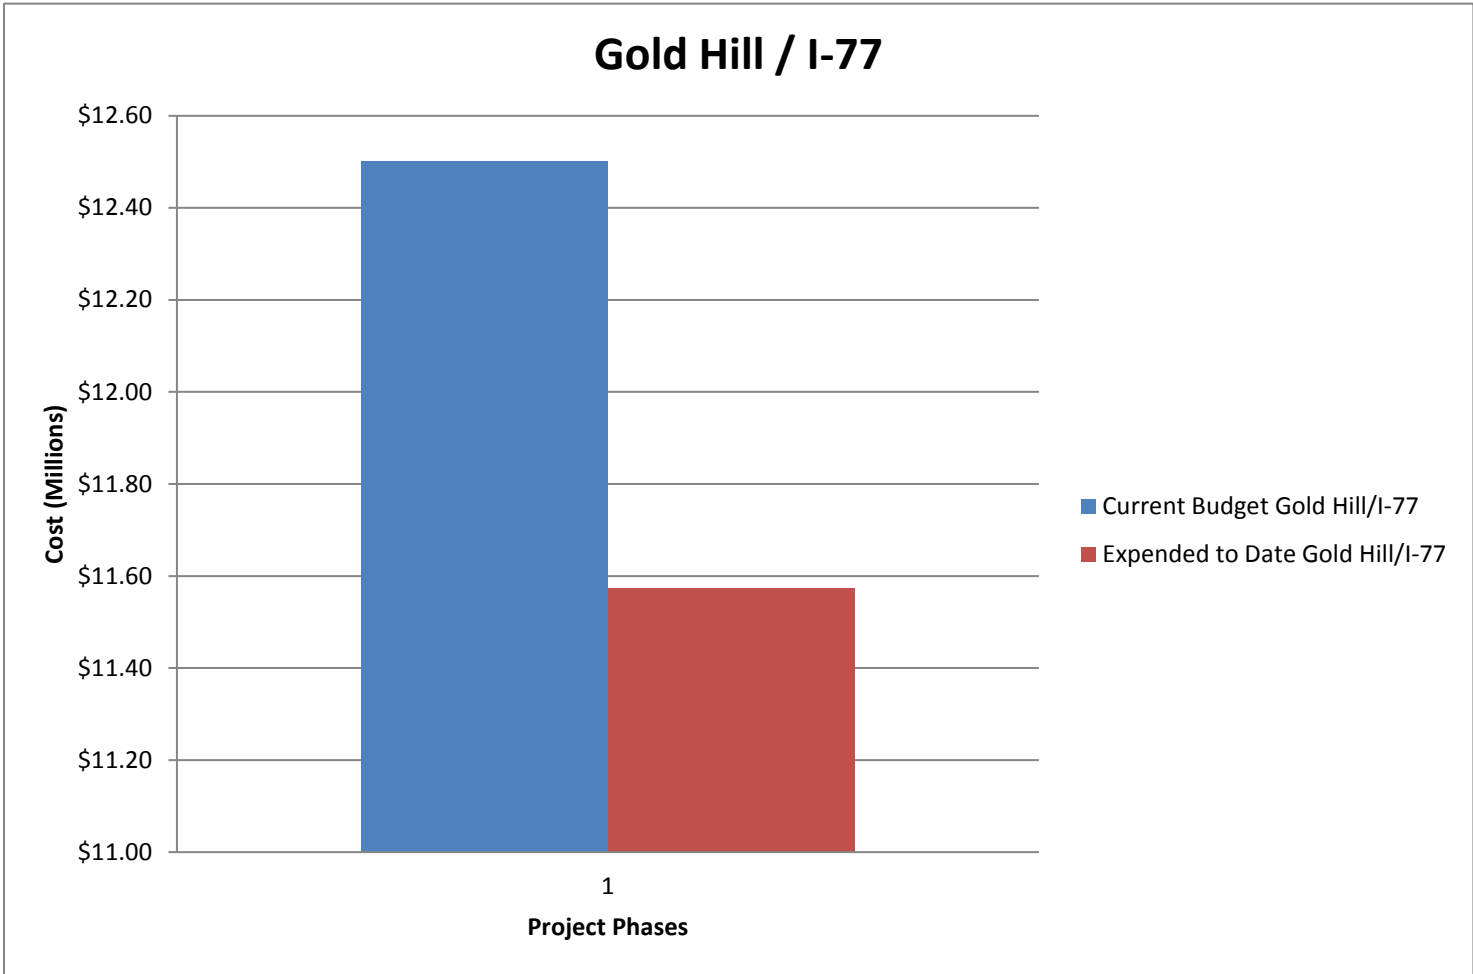

Project Status: Bids Received  
Expenses are updated through: May 10, 2019

\* Managed by SCDOT. Funds have already been submitted to SCDOT.


## Anderson / Cowan Farm

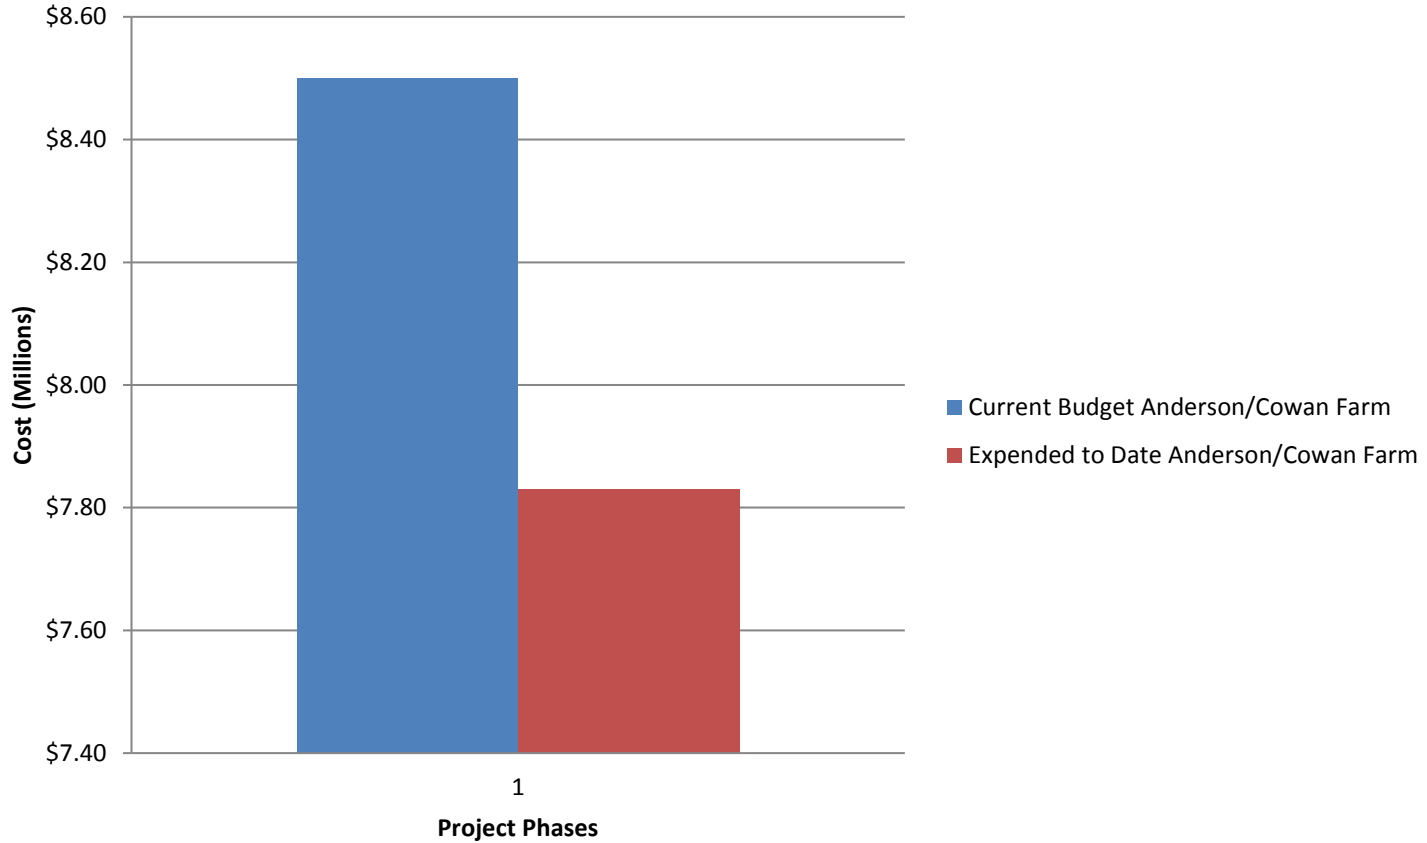

Project Status: Under construction  
Expenses are updated through: May 10, 2019

\* Managed by SCDOT. Funds have already  
been submitted to SCDOT.


## SC 49 / Lincoln

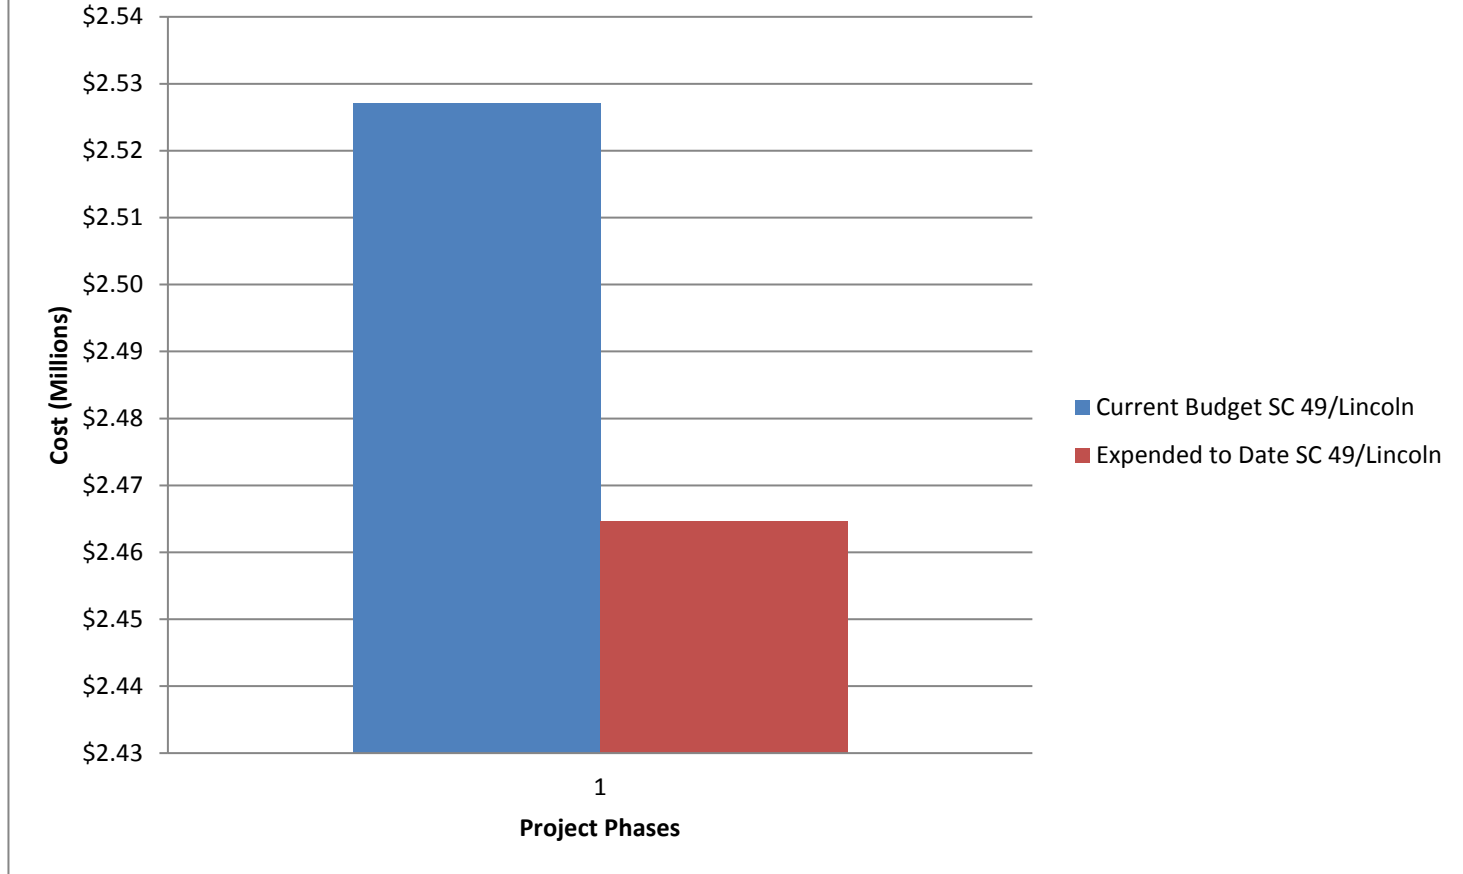

Project Status: Complete


Expenses are updated through: May 10, 2019

# US 321 / Johnson / Railroad

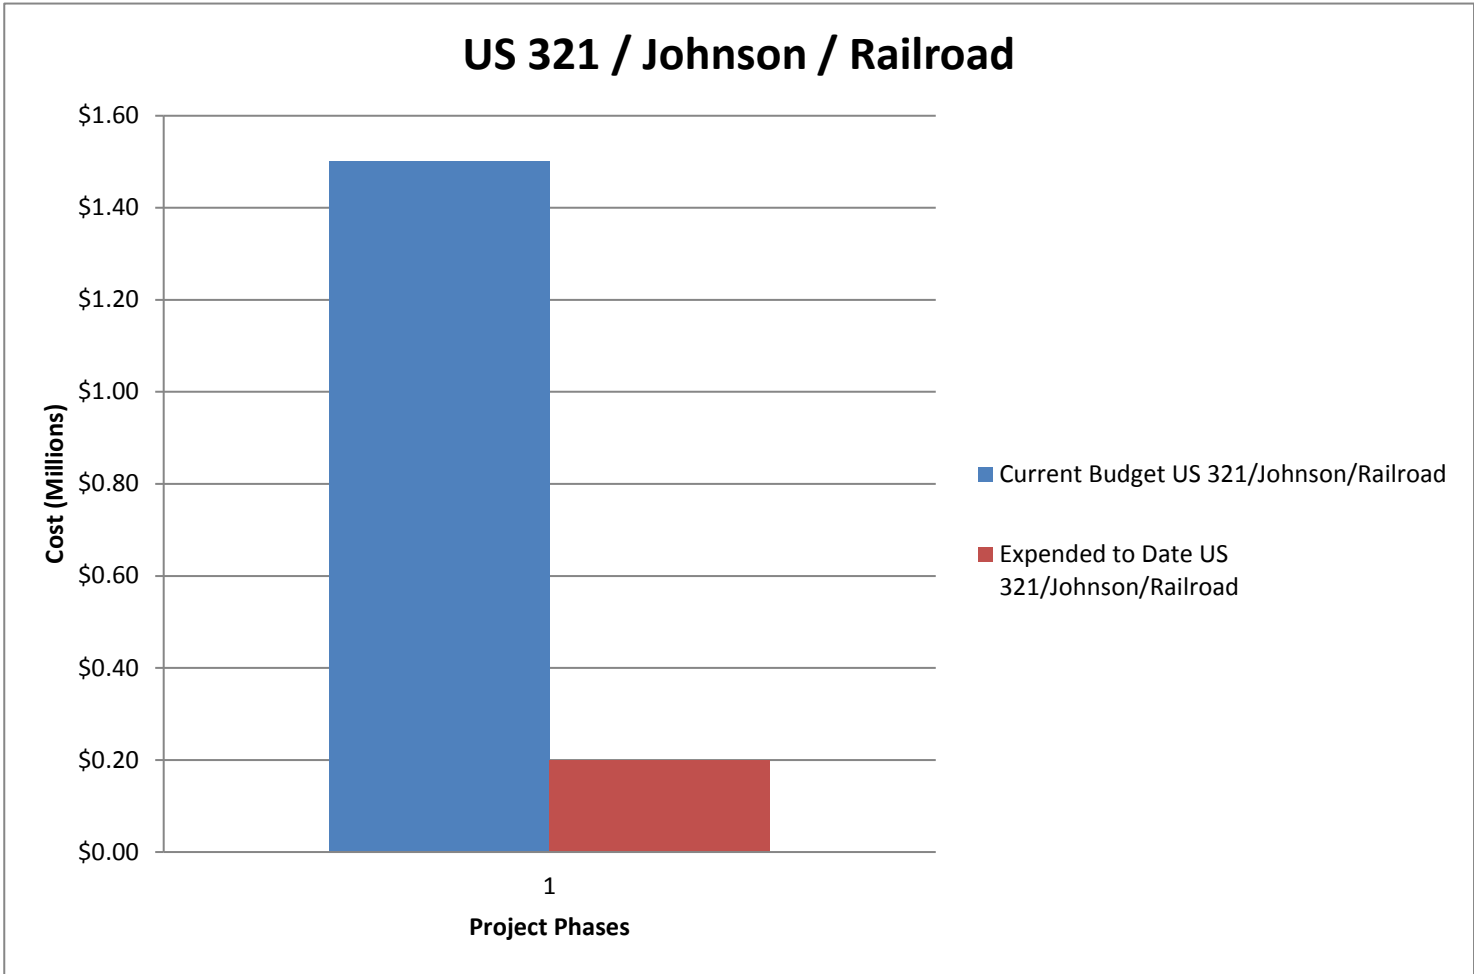

Project Status: Acquiring Right-of-Way  
Expenses are updated through: May 10, 2019

## SC 49 / Campbell

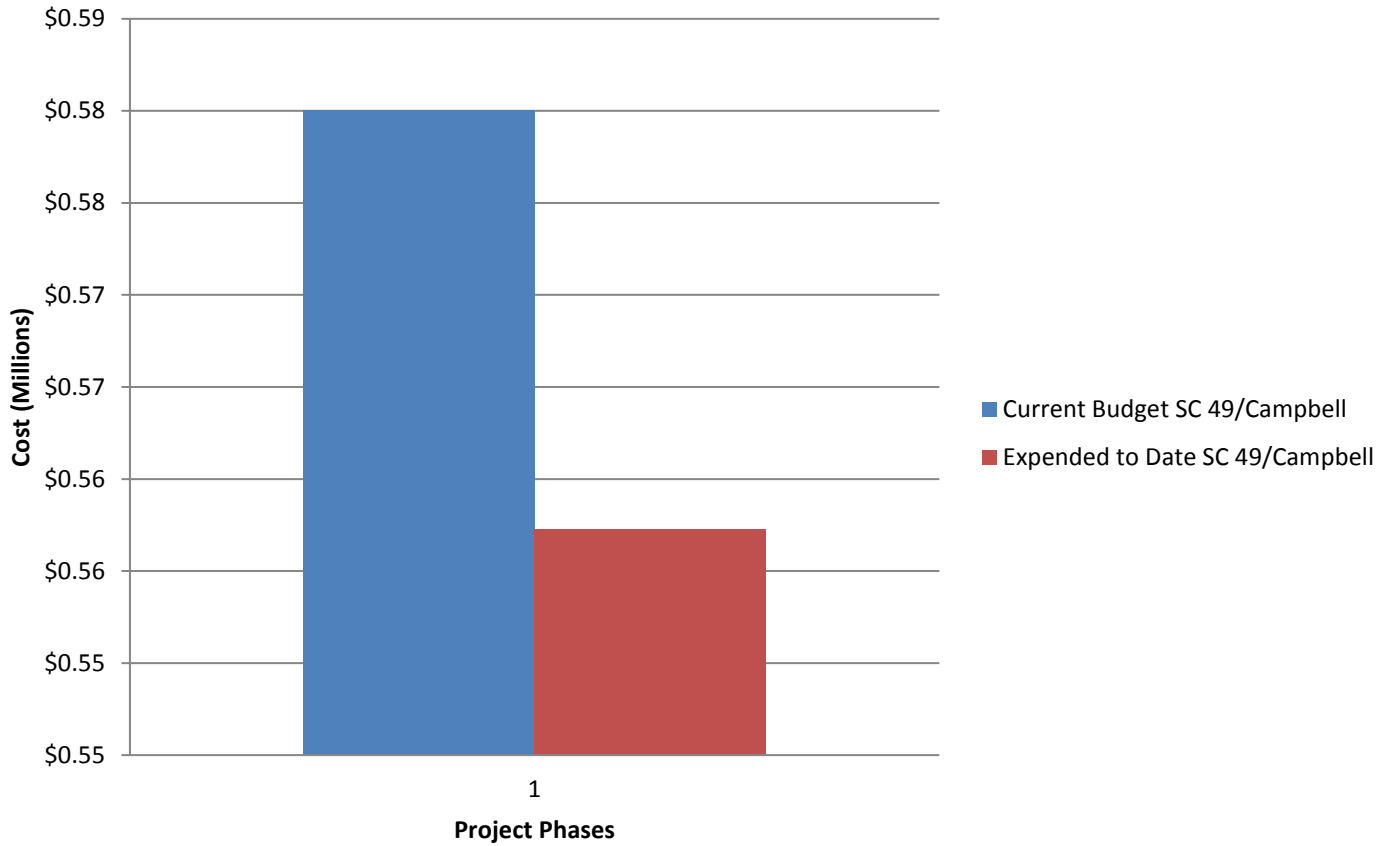


Project Status: Complete

Expenses are updated through:

May 10, 2019


## Sullivan Middle School / Winthrop

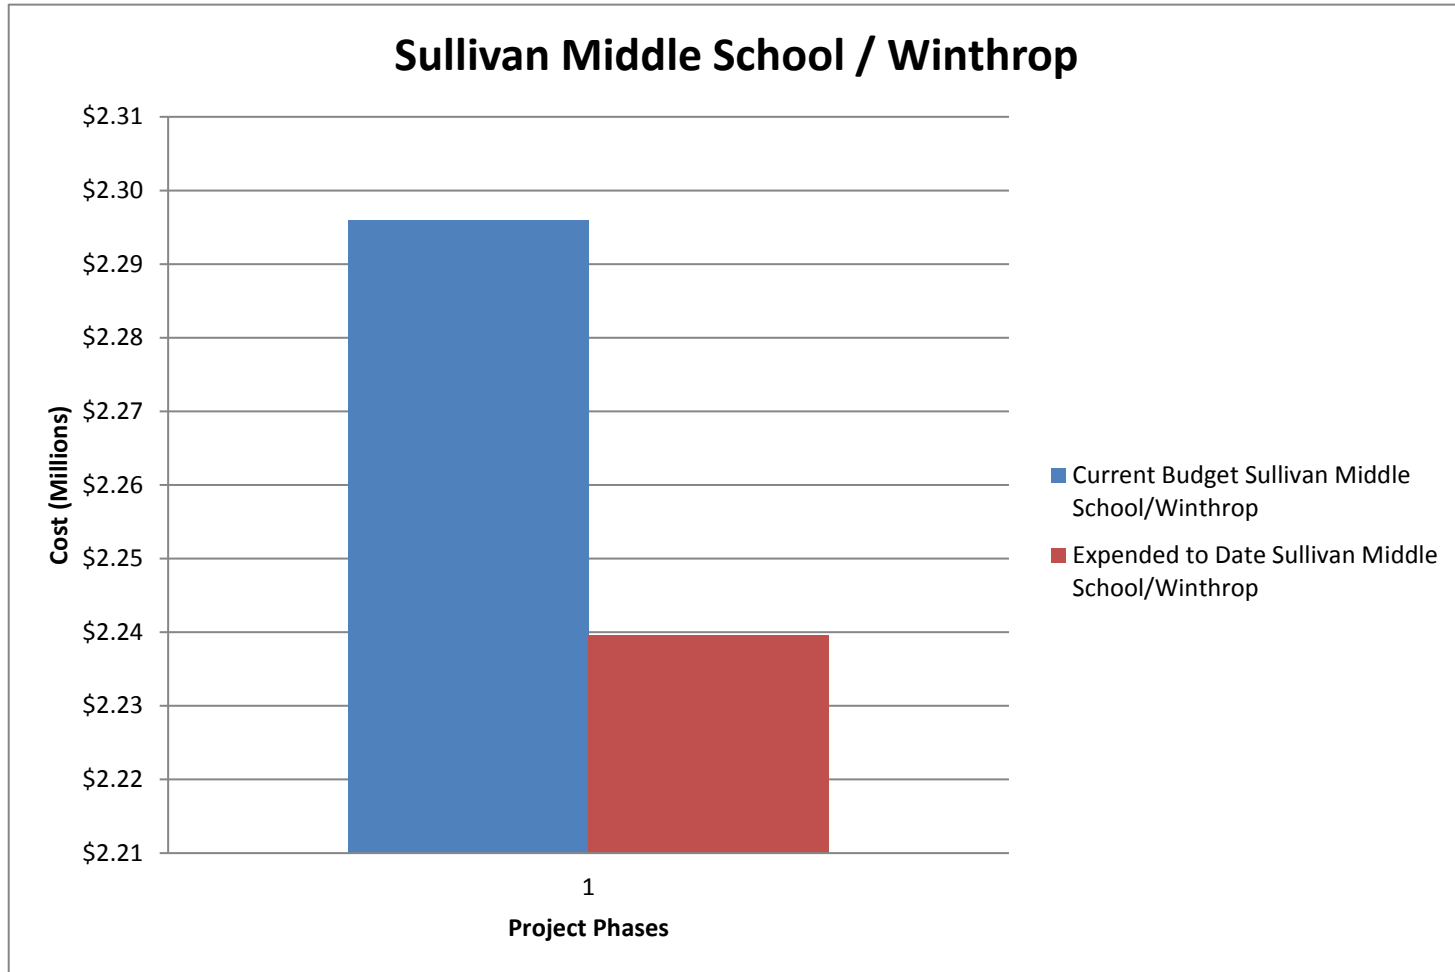

Project Status: Under construction  
Expenses are updated through: May 10, 2019

\* Managed by SCDOT. Funds have already been submitted to SCDOT.


## SC 557 / Griggs / Bate Harvey

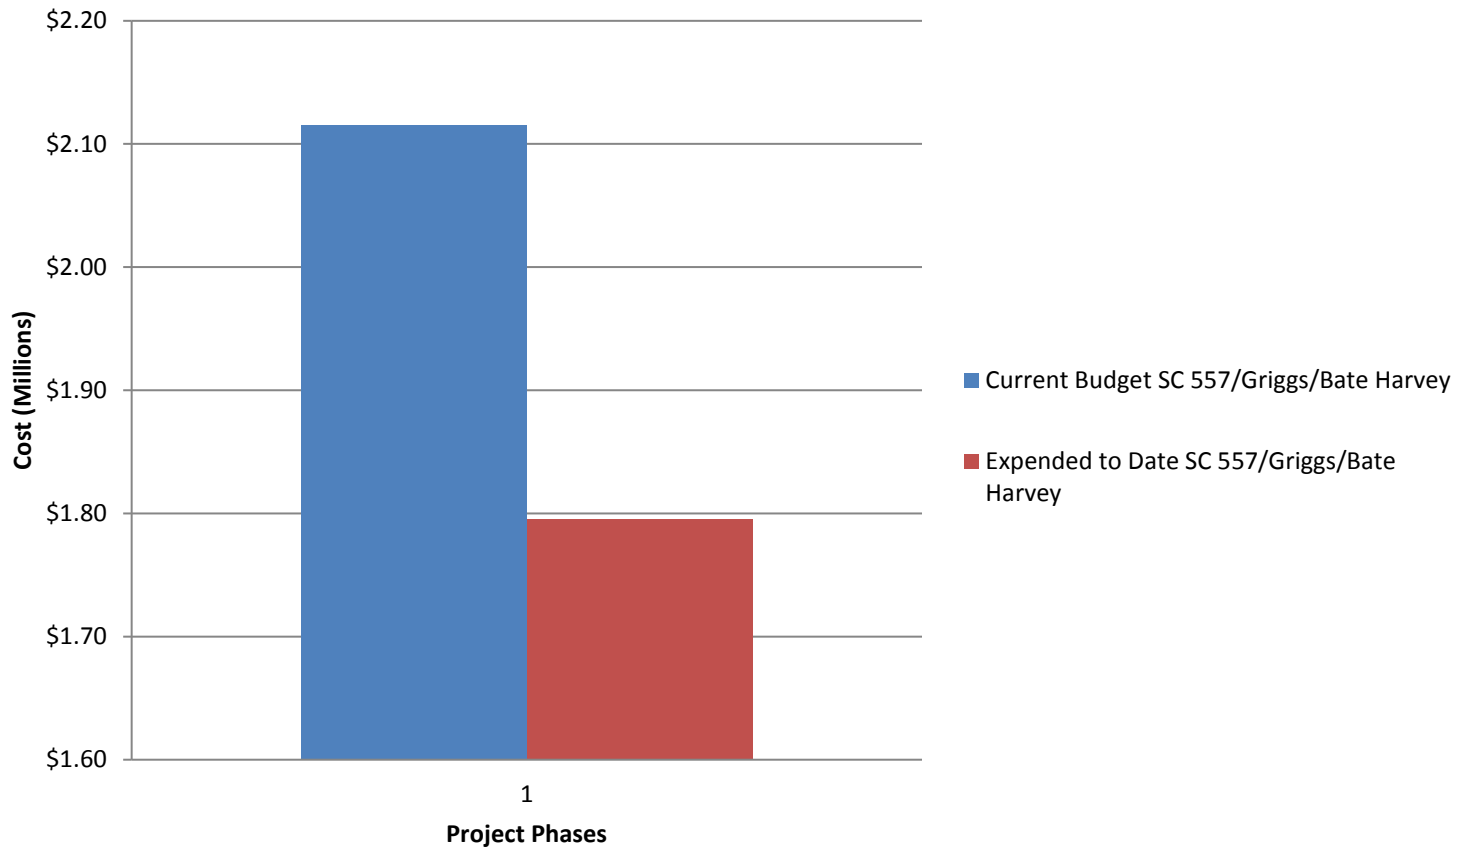

Project Status: Complete

Expenses are updated through: May 10, 2019

## 4th / 5th / Ross Cannon

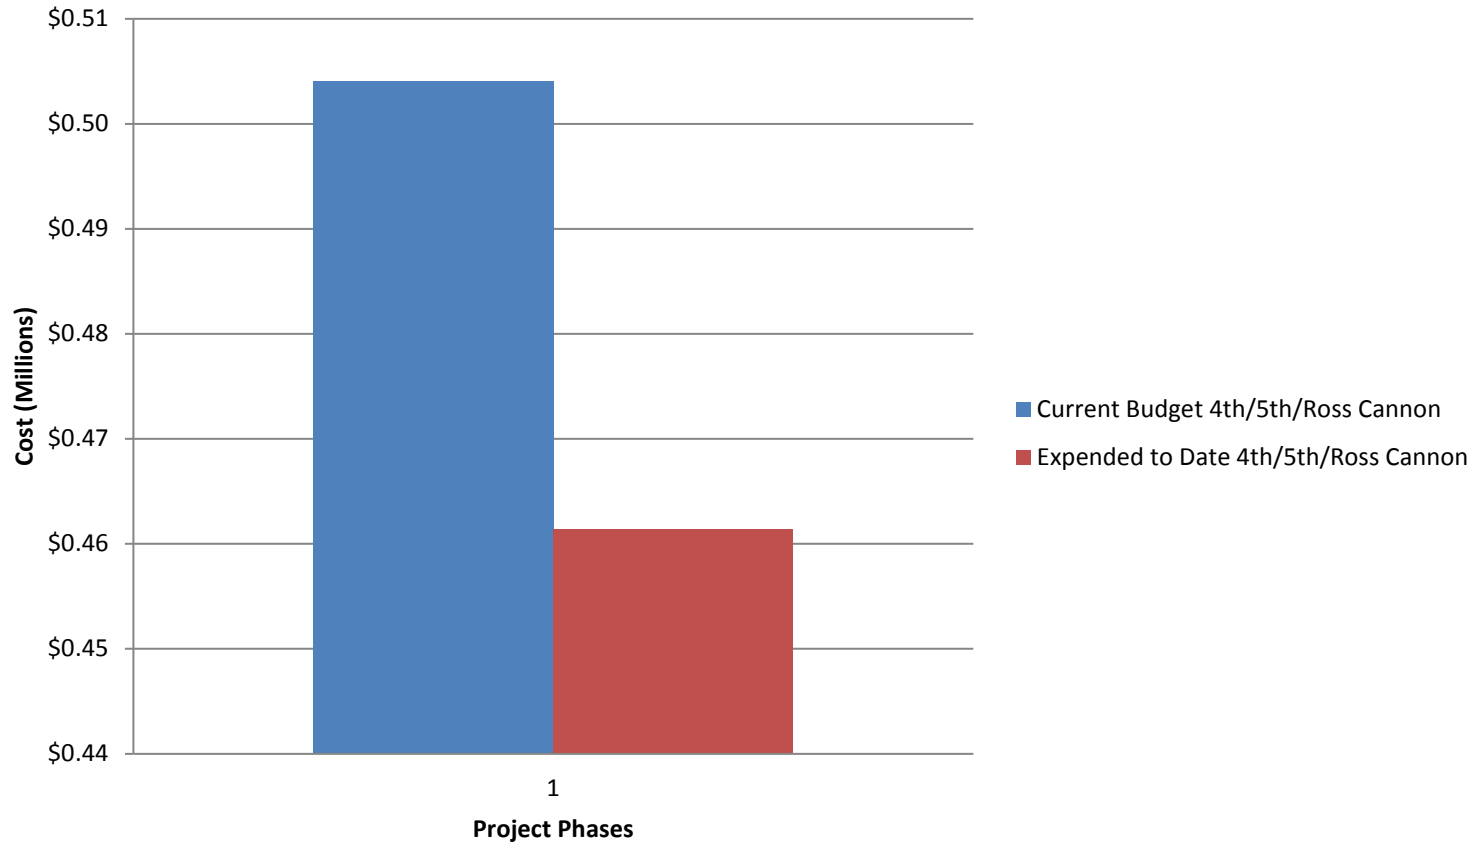


Project Status: Complete

Expenses are updated through: May 10, 2019




## White / Constitution

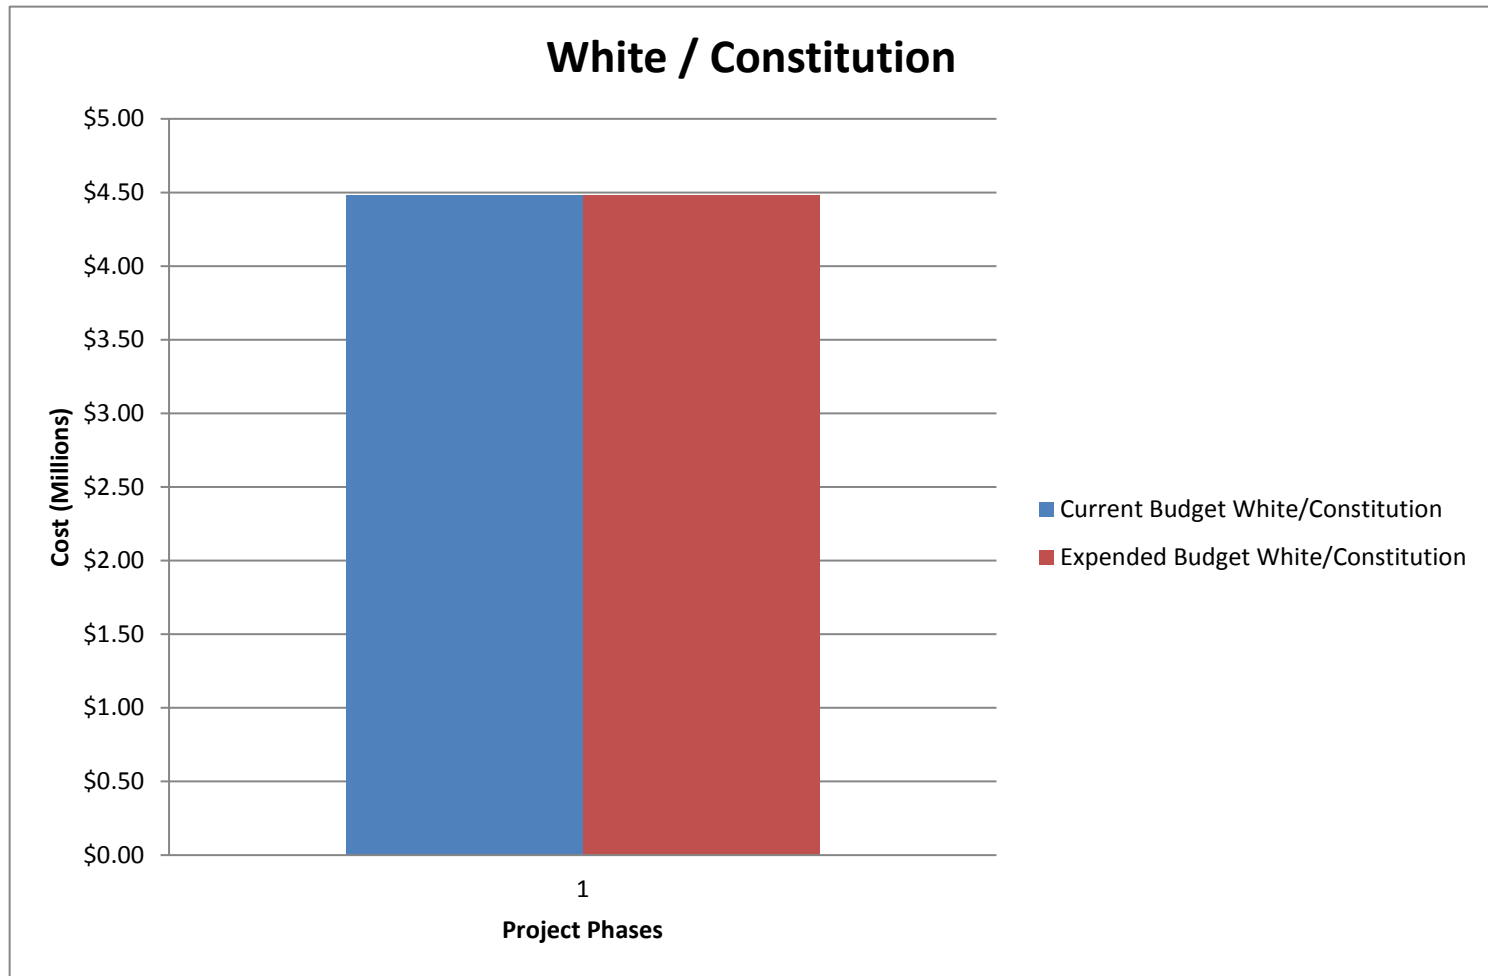

Project Status: Complete


Expenses are updated through: May 10, 2019

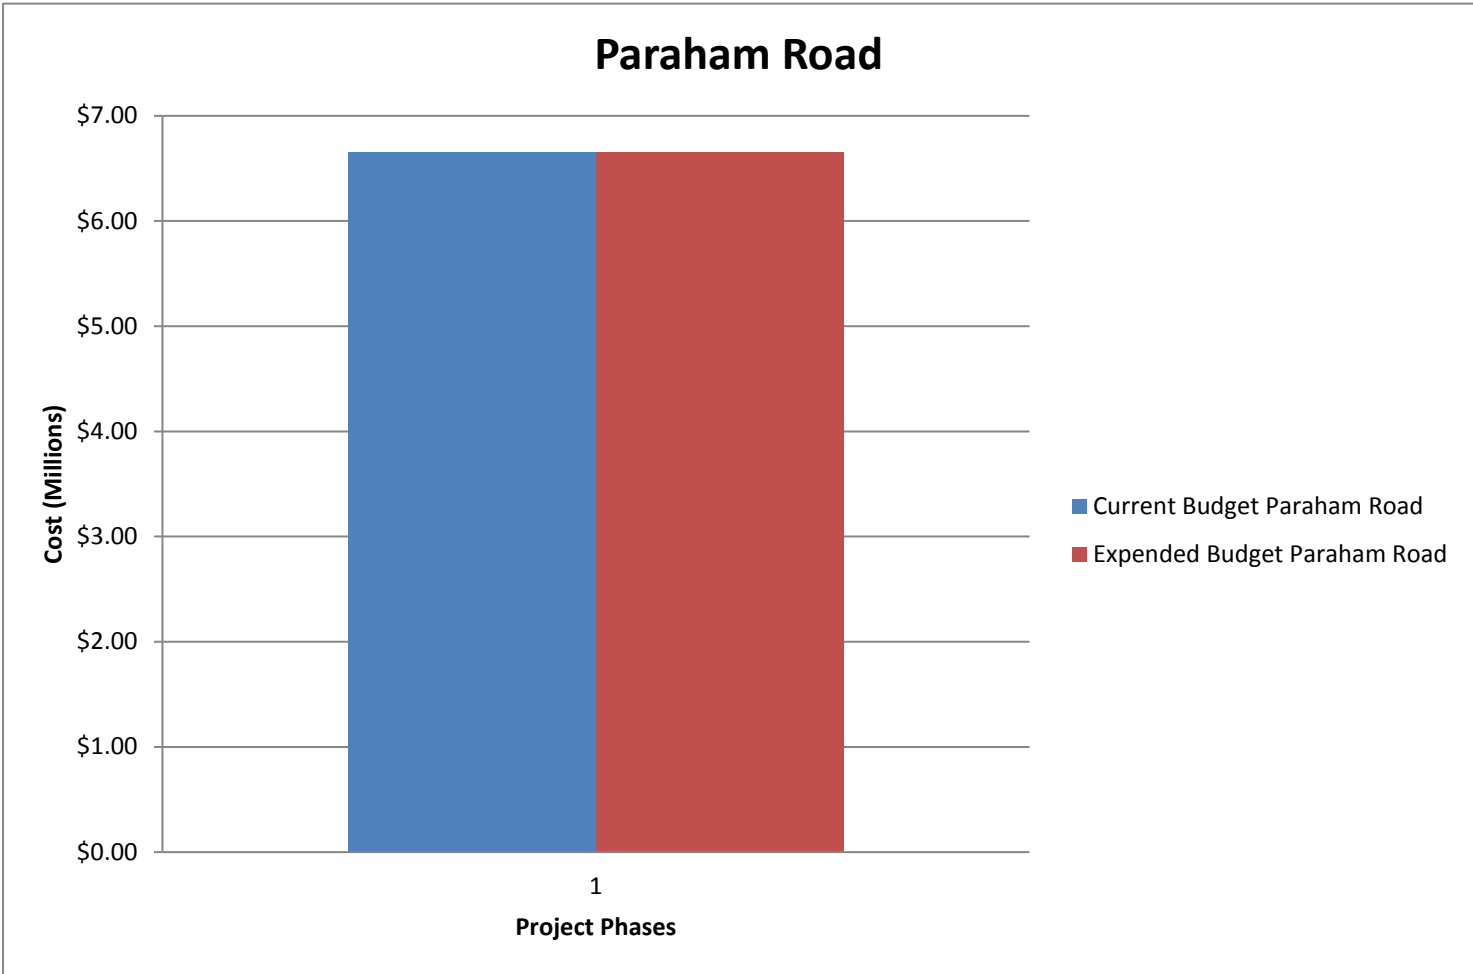

Project Status: Complete


Expenses are updated through: May 10, 2019

# FMSB / Spratt

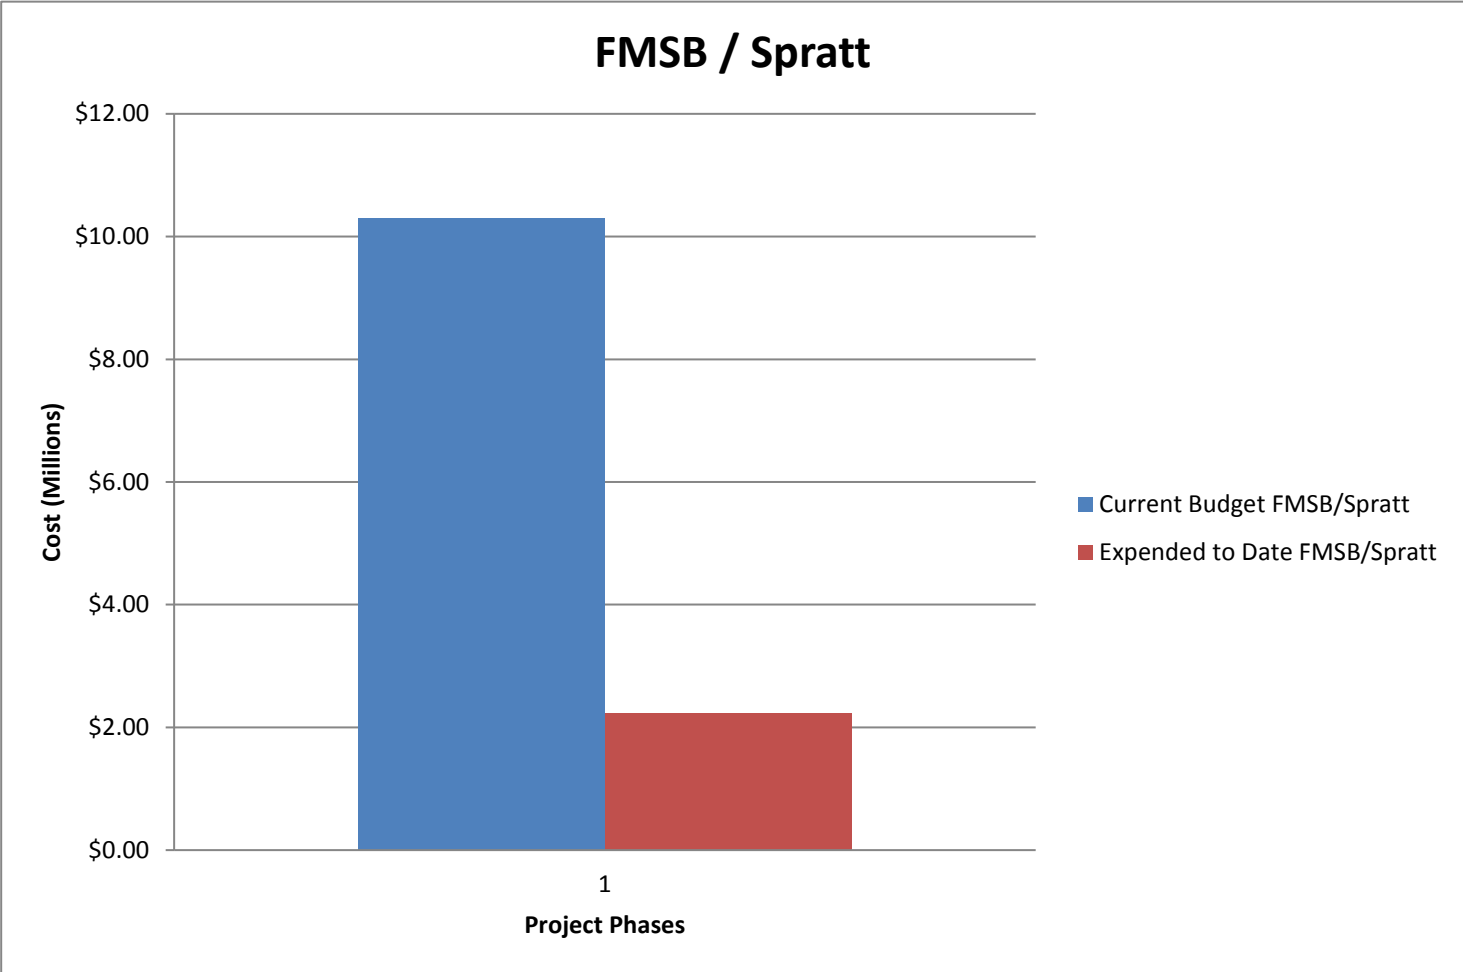


Project Status: Final Plans  
Expenses are updated through: May 10, 2019


# University Drive

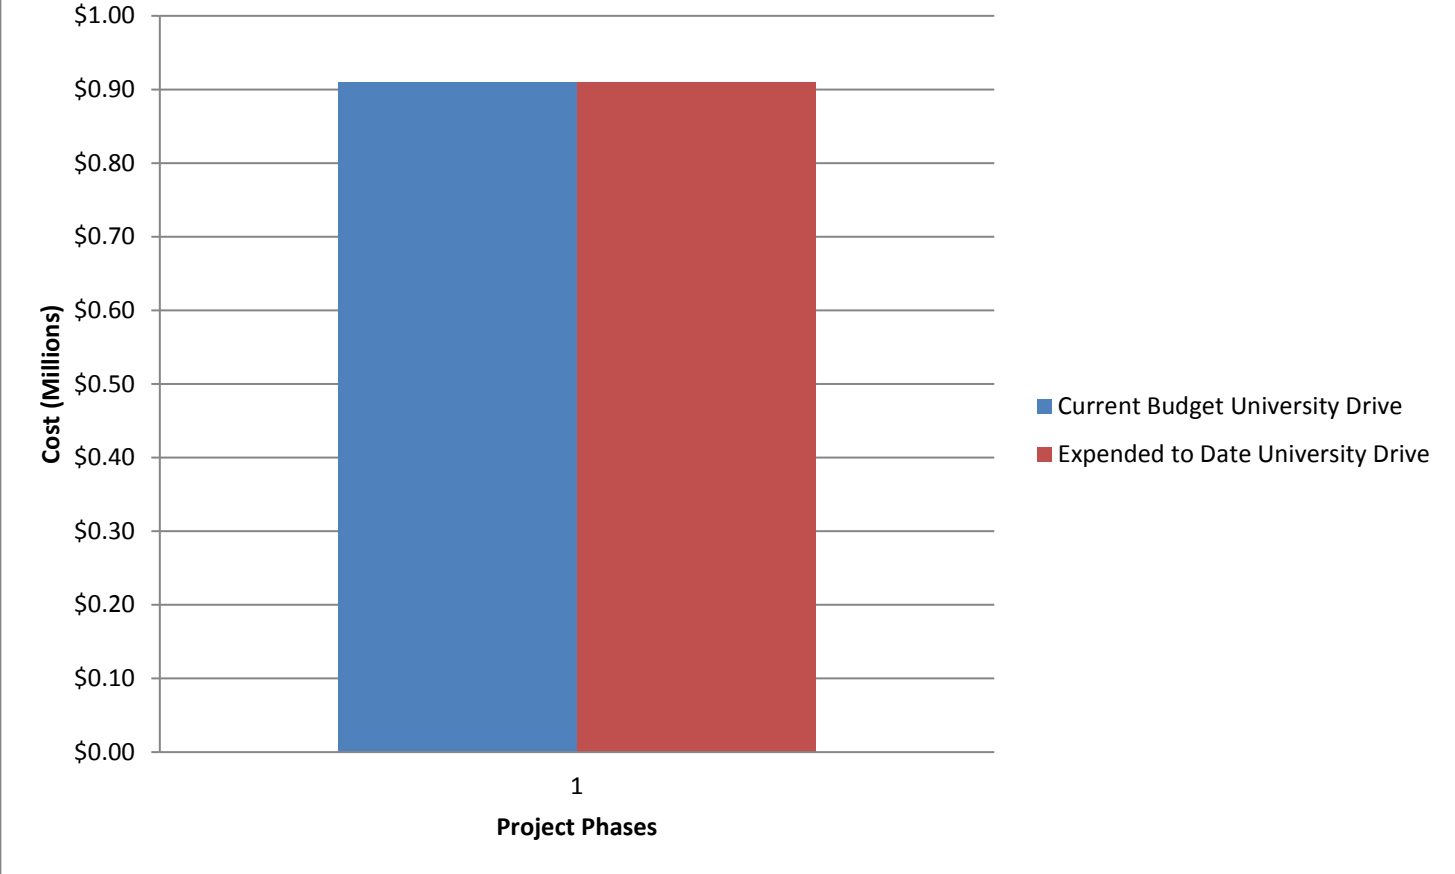

Project Status: Complete  
Expenses are updated through: May 10, 2019

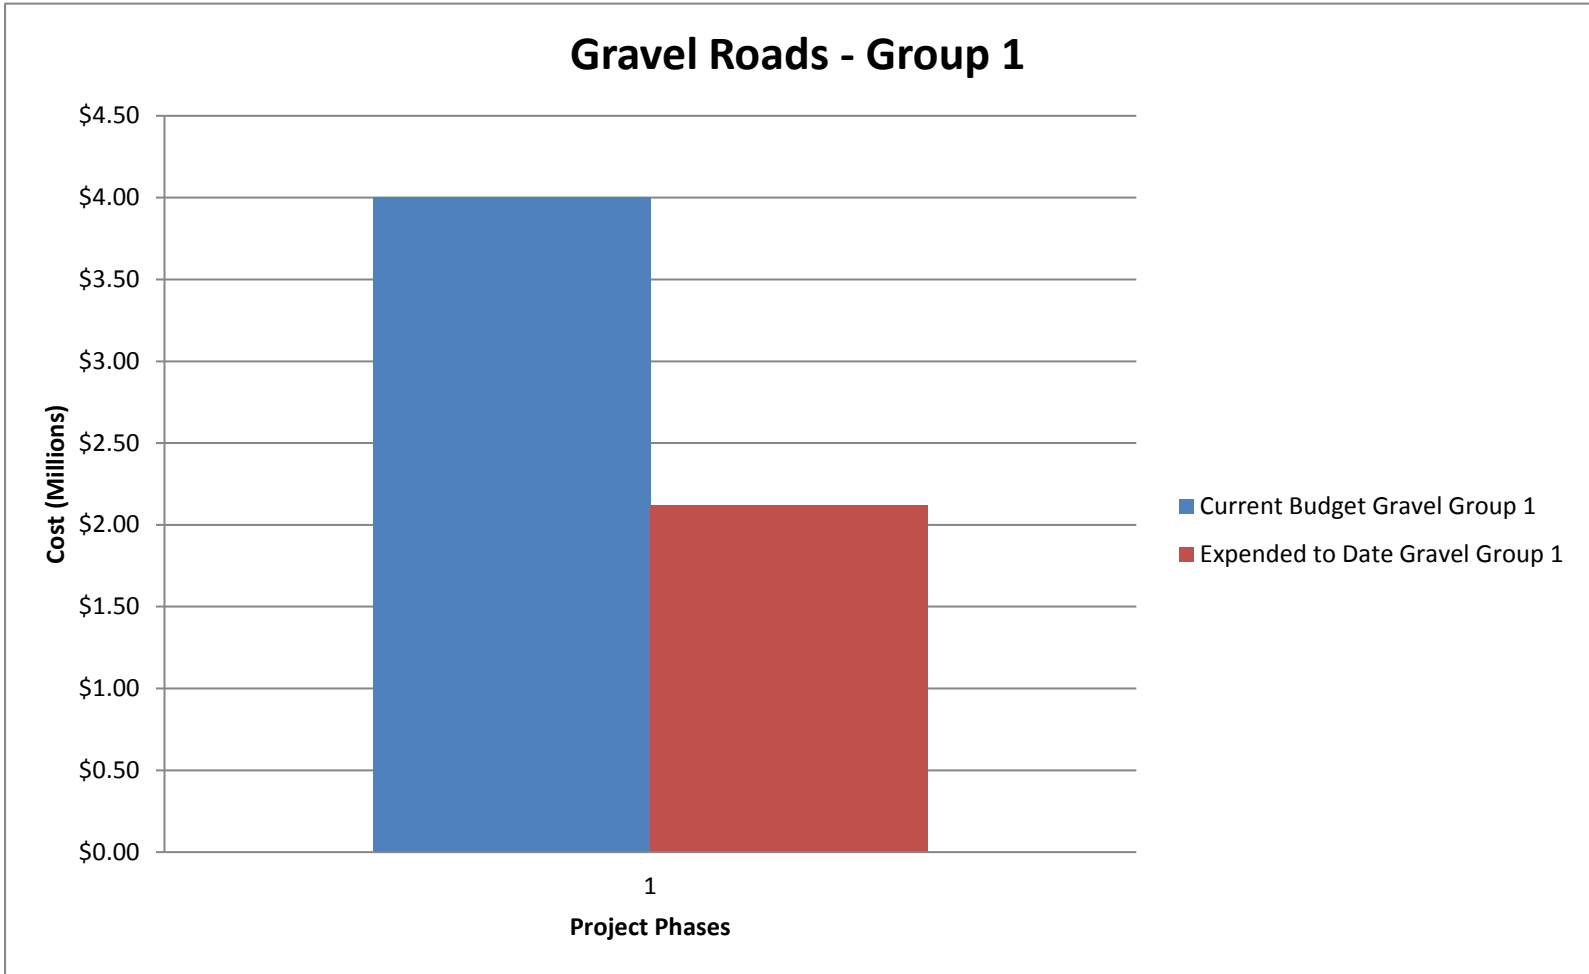

Project Status: Ongoing  
Expenses are updated through: May 10, 2019

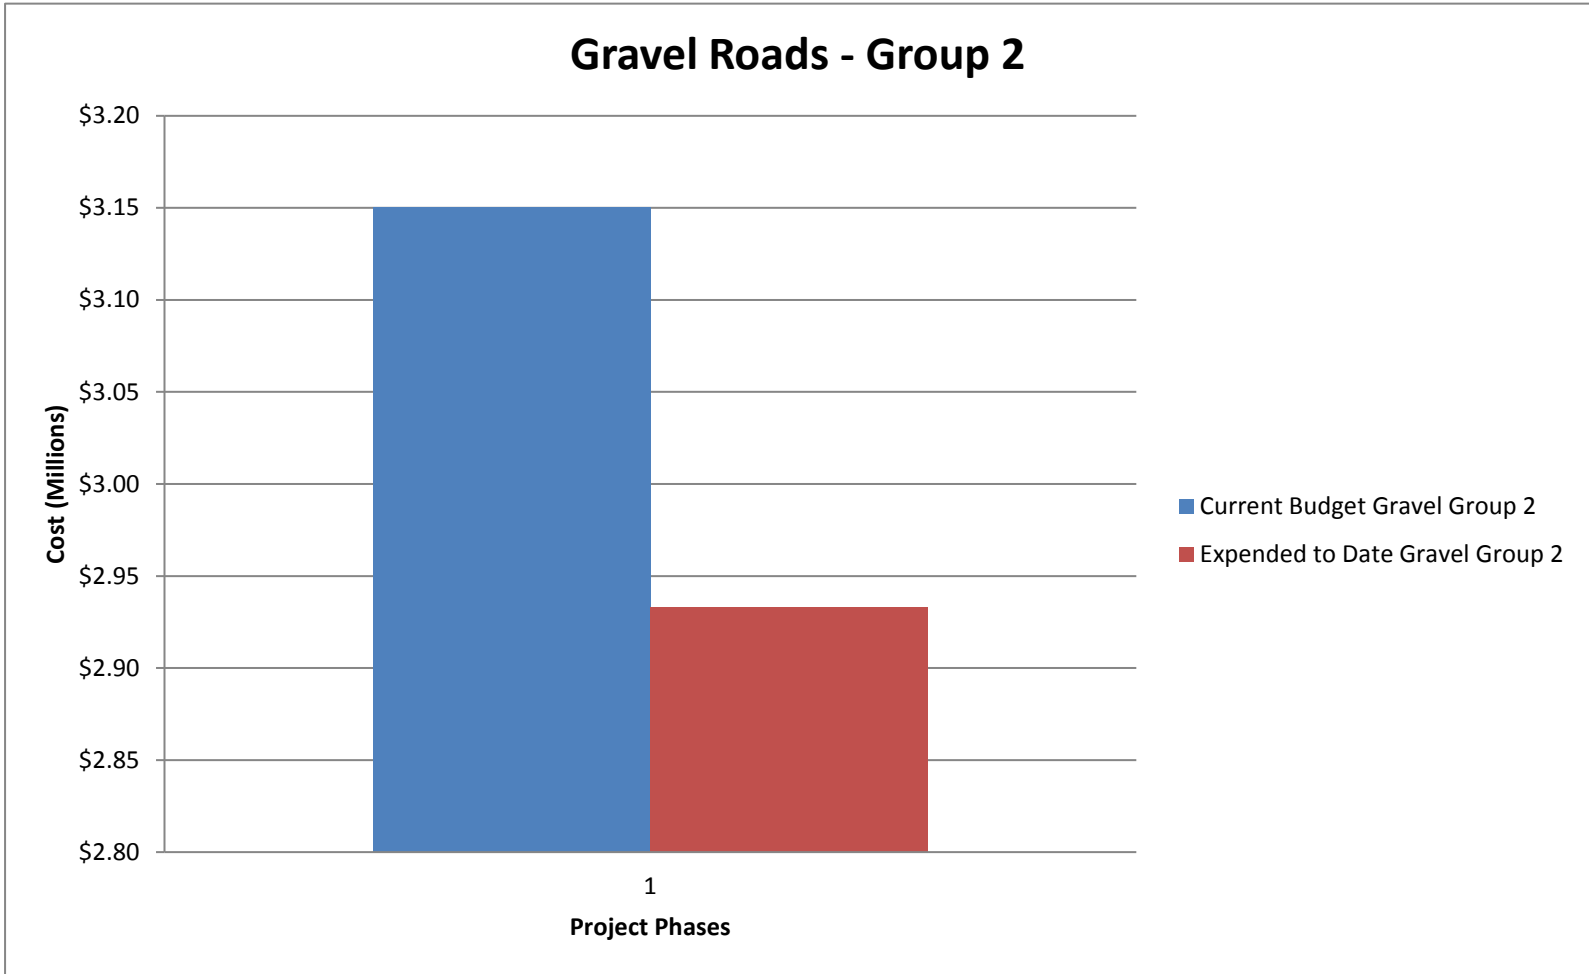


Project Status: Ongoing  
Expenses are updated through: May 10, 2019



## **Pennies for Progress**

Pennies 4

Prepared for Council Meeting on  
May 20, 2019

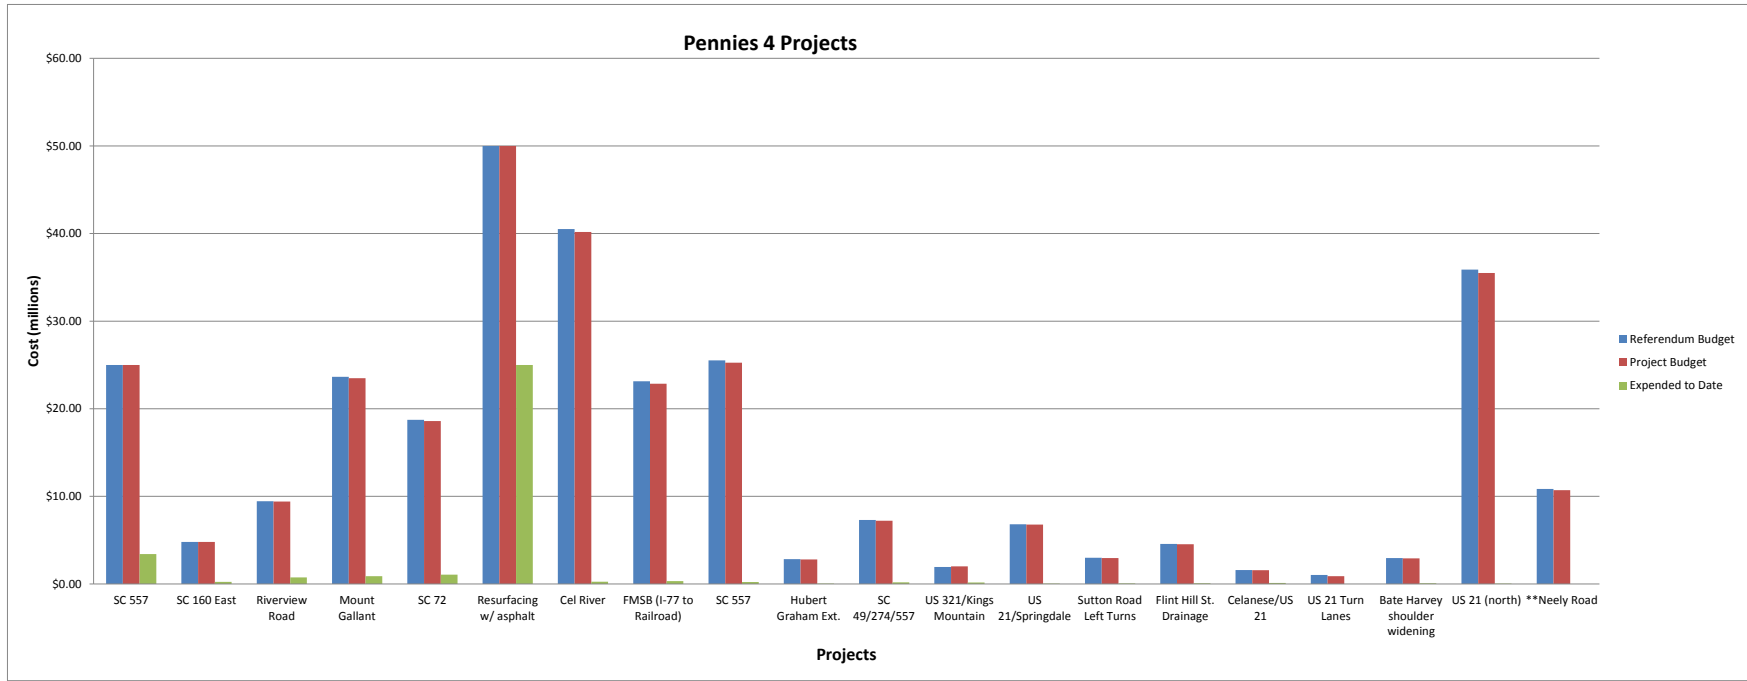



Project	Referendum Budget	Program Management	Project Budget	Expended to Date	Status
SC 557	\$25.00	\$0.00	\$25.00	\$3.41	Acquiring Right-of-Way
SC 160 East	\$4.80	\$0.00	\$4.80	\$0.23	Acquiring Right-of-Way
Riverview Road	\$9.45	\$0.05	\$9.40	\$0.75	Acquiring Right-of-Way
Mount Gallant	\$23.65	\$0.16	\$23.49	\$0.89	30% plans
SC 72	\$18.74	\$0.14	\$18.60	\$1.07	Acquiring Right-of-Way
Resurfacing w/ asphalt	\$50.00	\$0.00	\$50.00	\$25.00	Ongoing
Cel River	\$40.51	\$0.34	\$40.17	\$0.26	30% plans
FMSB (I-77 to Railroad)	\$23.13	\$0.27	\$22.86	\$0.33	Preliminary design
SC 557	\$25.52	\$0.26	\$25.26	\$0.22	Preliminary design
Hubert Graham Ext.	\$2.83	\$0.04	\$2.79	\$0.05	30% plans
SC 49/274/557	\$7.30	\$0.08	\$7.22	\$0.18	30% plans
US 321/Kings Mountain	\$1.94	\$0.02	\$2.01	\$0.17	Acquiring Right-of-Way
US 21/Springdale	\$6.82	\$0.04	\$6.78	\$0.04	Preliminary design
Sutton Road Left Turns	\$3.00	\$0.05	\$2.95	\$0.07	30% plans
Flint Hill St. Drainage	\$4.57	\$0.03	\$4.54	\$0.08	Preliminary design
Celanese/US 21	\$1.59	\$0.02	\$1.57	\$0.11	30% plans
US 21 Turn Lanes	\$1.03	\$0.01	\$0.88	\$0.00	Bids Received by SCDOT
Bate Harvey shoulder widening	\$2.95	\$0.03	\$2.92	\$0.07	70% plans
US 21 (north)	\$35.88	\$0.38	\$35.50	\$0.05	Preliminary design
**Neely Road	\$10.85	\$0.14	\$10.71	\$0.00	On hold

Project budget is Referendum budget subtracting the Program Management allocation



# Pennies 4

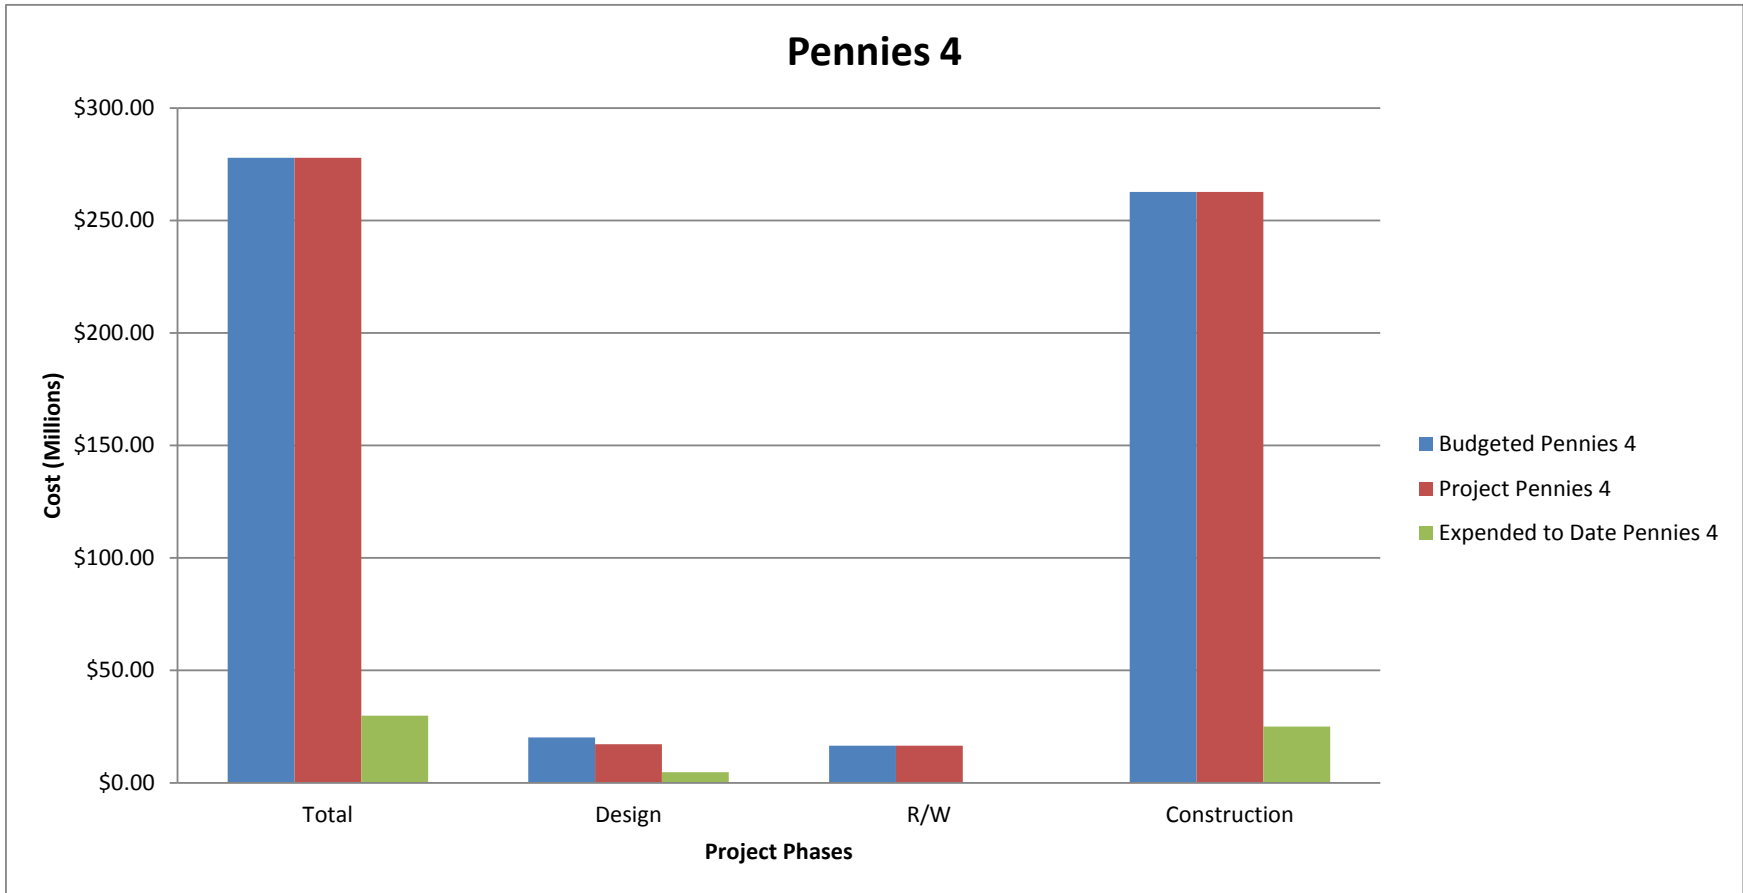

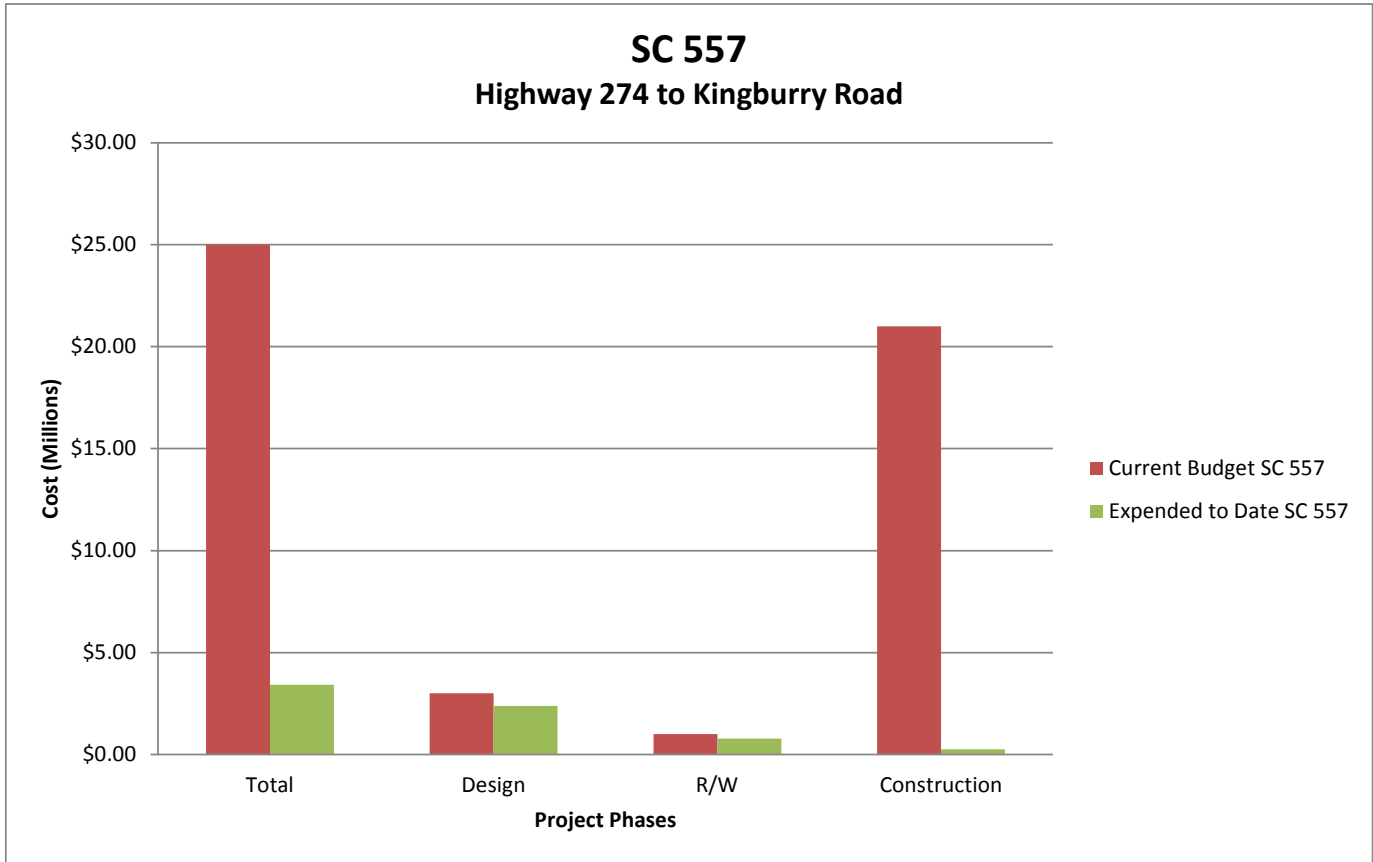


Project Status: Acquiring Right-of-Way  
 Expenses are updated through: May 10, 2019

	<u>Budget</u>	<u>Spent to Date</u>
Pennies 2	\$20.00	\$2.46
Pennies 3	\$1.50	\$0.95
Pennies 4	\$3.50	\$0.00
<b>Total</b>	<b>\$25.00</b>	<b>\$3.41</b>

\* Staff Anticipates there will be additional funding available from other Pennies 2 projects, thus reducing the amount needed from Pennies 4 from \$8.0 million to \$3.5 million.


## SC 160 East FMSB to Lancaster County Line

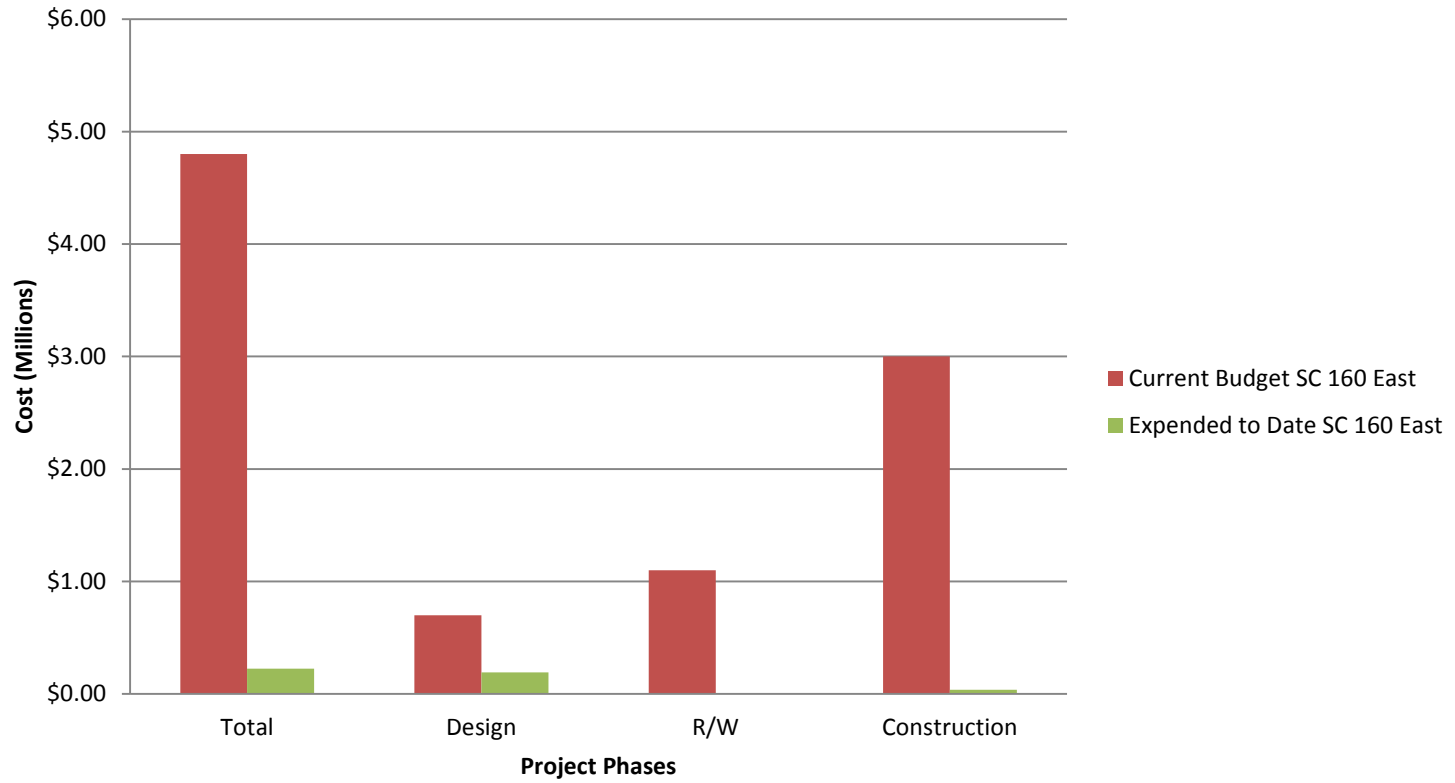

Project Status:           Acquiring Right-of-Way  
 Expenses are updated through:           May 10, 2019

	<u>Budget</u>	<u>Spent to Date</u>
Pennies 3	\$1.50	\$0.23
Pennies 4	\$3.30	\$0.00
<b>Total</b>	<b>\$4.80</b>	<b>\$0.23</b>


## Riverview Road Celanese Road to Eden Terrace Road

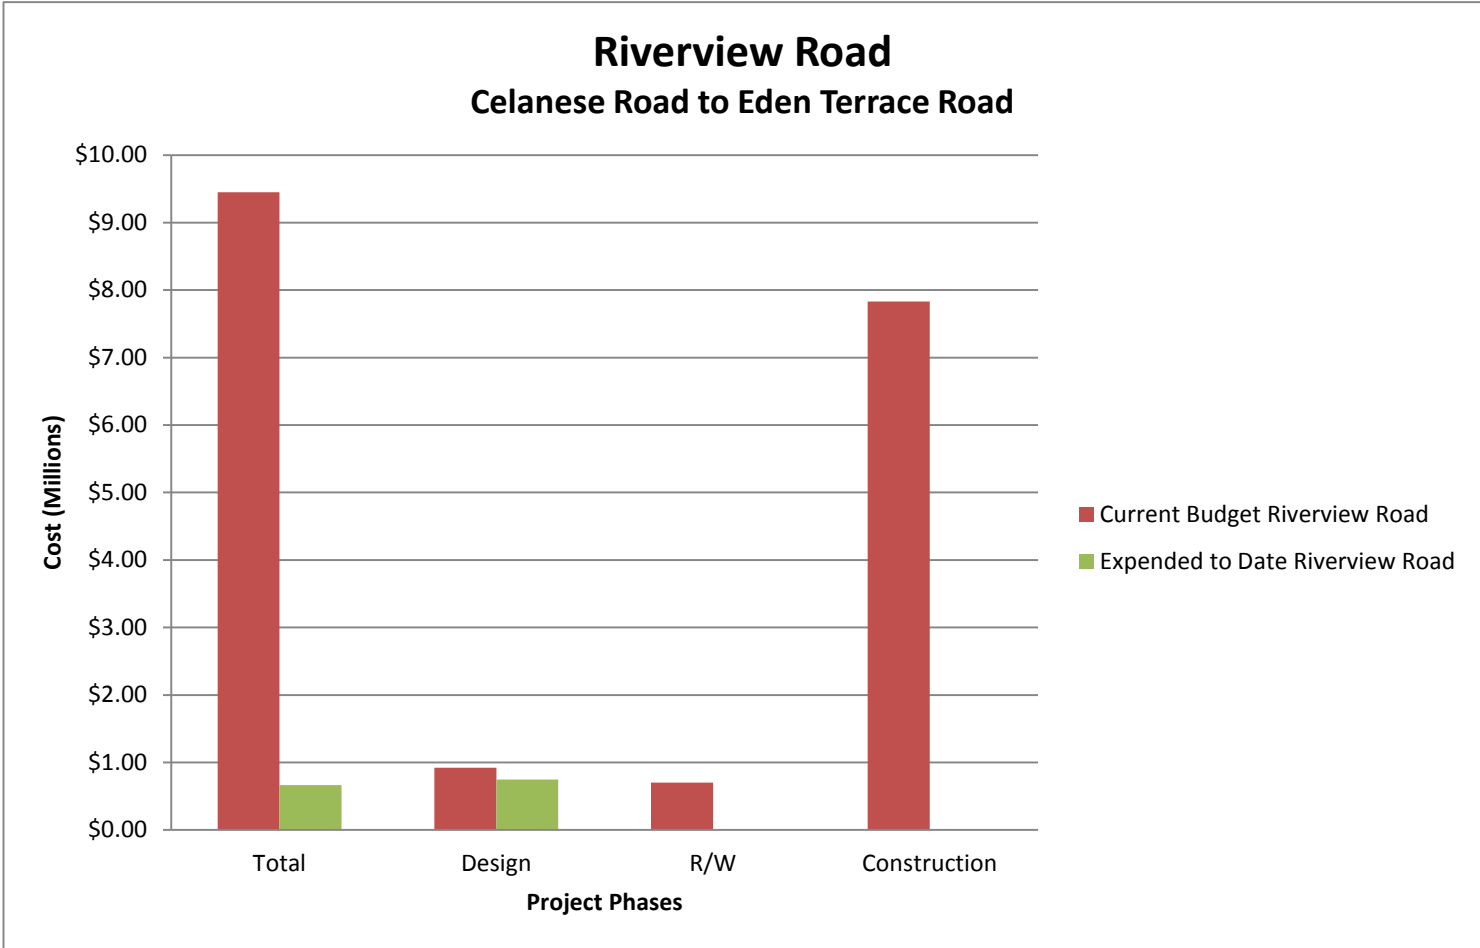

Project Status:           Acquiring Right-of-Way  
 Expenses are updated through:           May 10, 2019

	<u>Budget</u>	<u>Spent to Date</u>
Pennies 3	\$3.49	\$0.75
Pennies 4	\$6.01	\$0.00
<b>Total</b>	<b>\$9.50</b>	<b>\$0.75</b>


## Mt Gallant Celanese Road to Twin Lakes Road

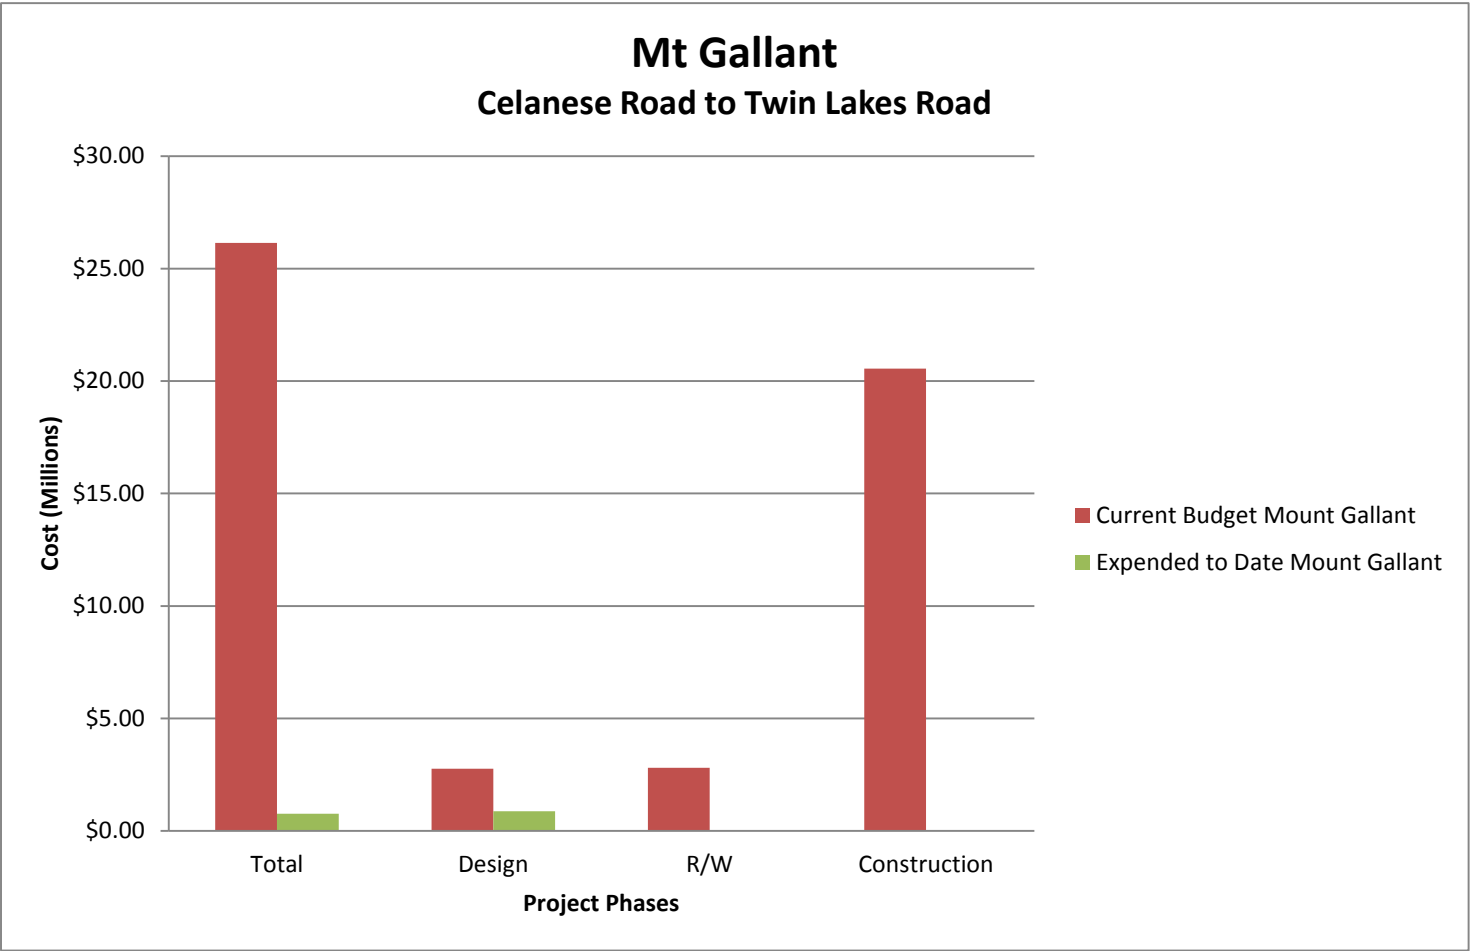

Project Status: 30% plans  
 Expenses are updated through: May 10, 2019

	<u>Budget</u>	<u>Spent to Date</u>
Pennies 3	\$2.49	\$0.89
Pennies 4	\$23.81	\$0.00
<b>Total</b>	<b>\$26.30</b>	<b>\$0.89</b>


## SC 72 Highway 901 to Rambo Road

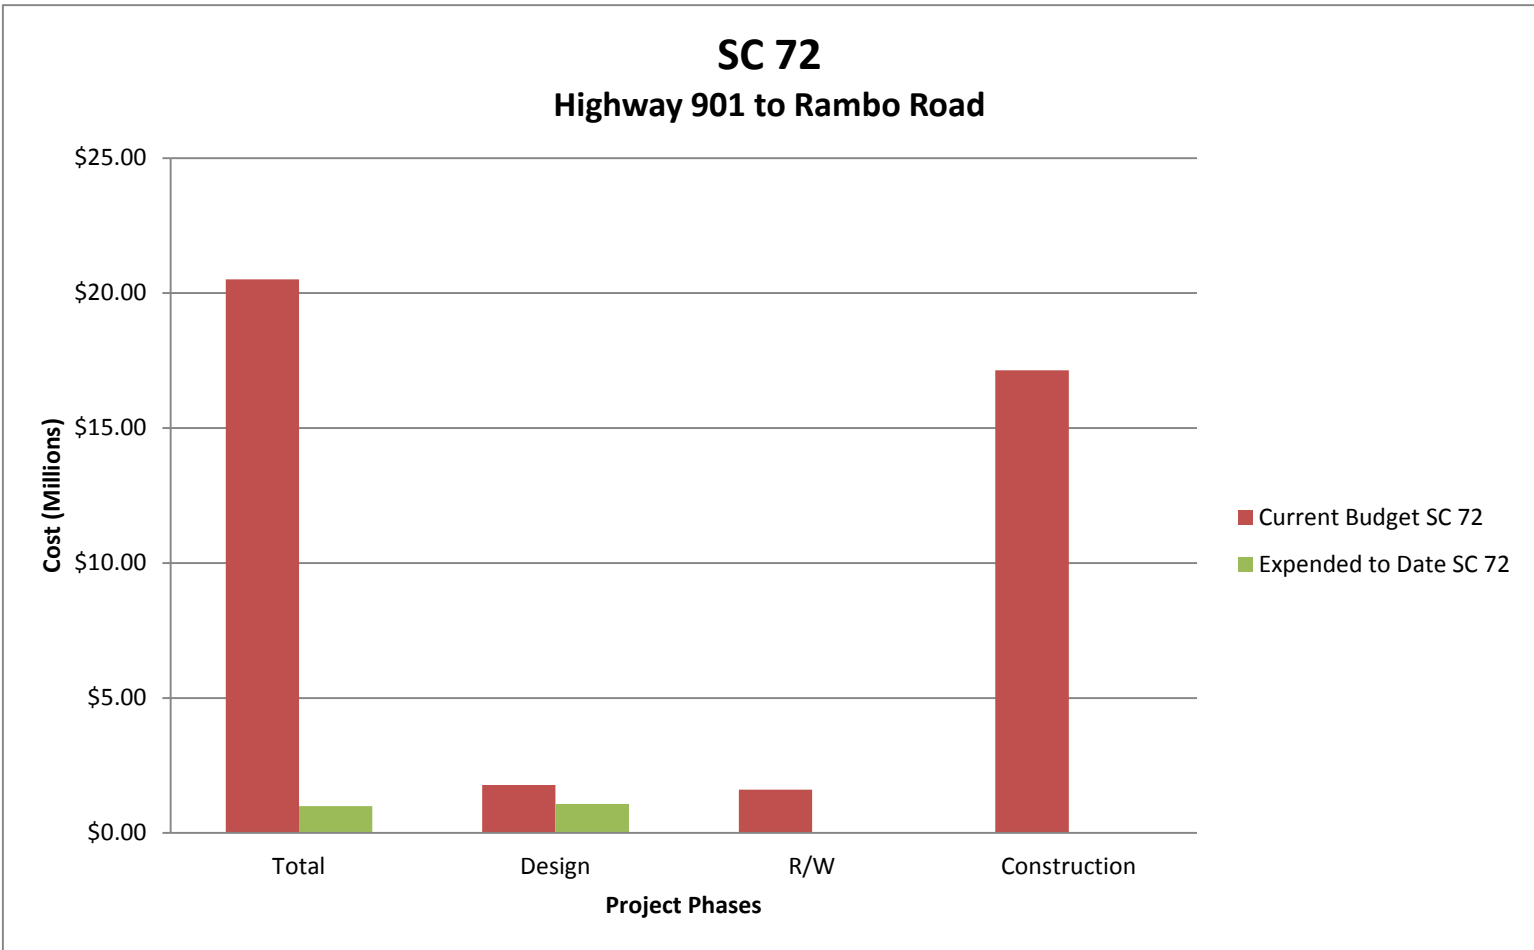

Project Status: Acquiring Right-of-Way  
 Expenses are updated through: May 10, 2019

	<u>Budget</u>	<u>Spent to Date</u>
Pennies 3	\$1.77	\$1.07
Pennies 4	\$18.88	\$0.00
<b>Total</b>	<b>\$20.65</b>	<b>\$1.07</b>


## Resurfacing w/ Asphalt

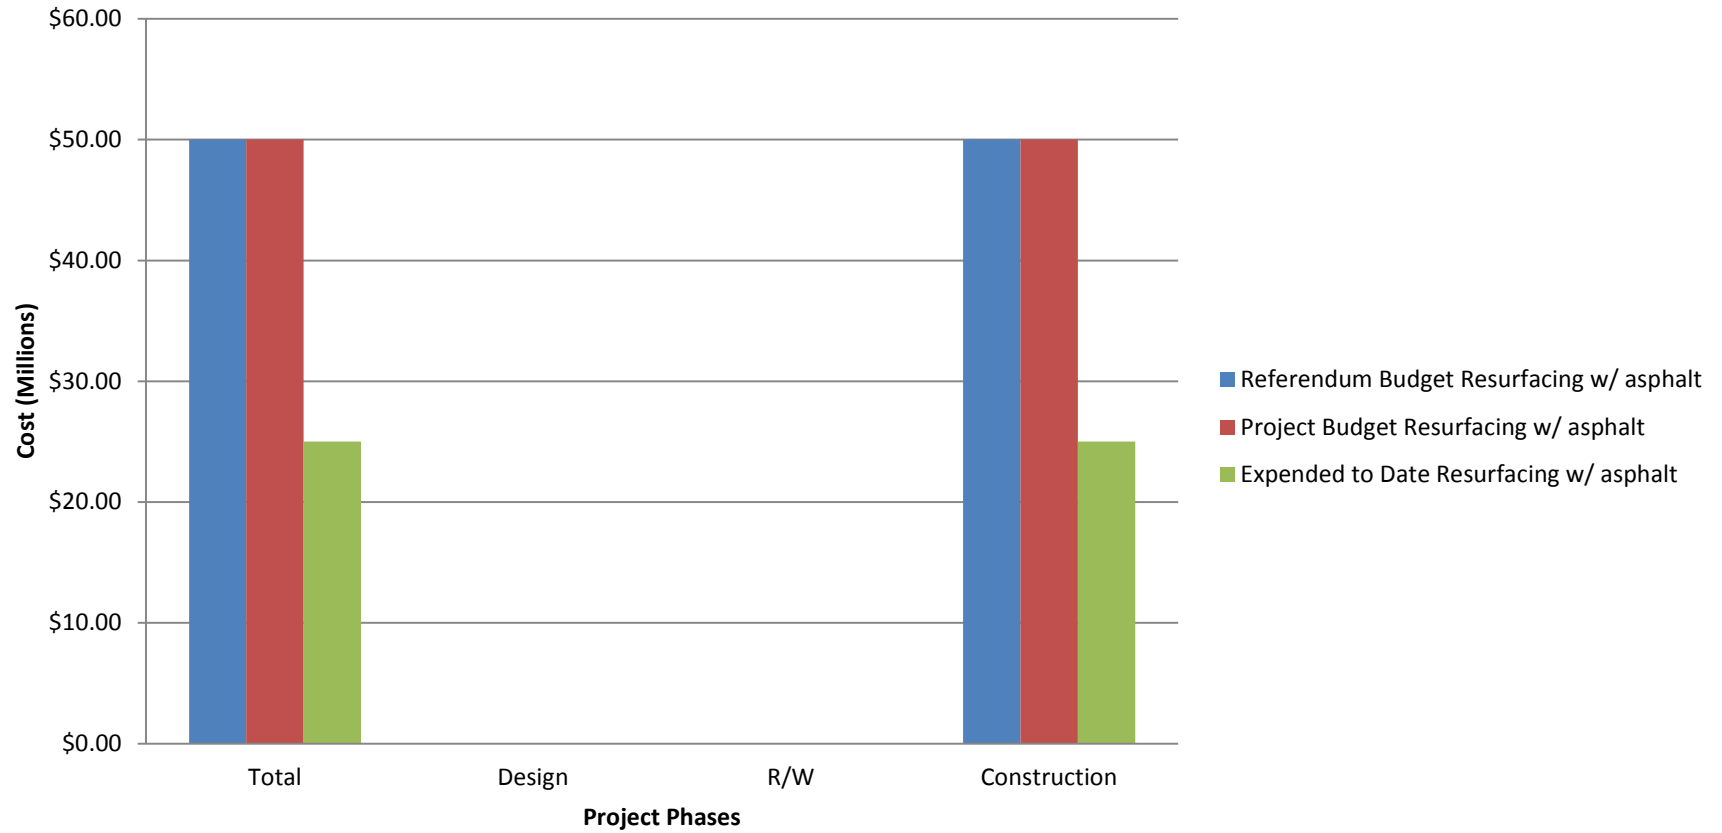

Project Status: Ongoing

Expenses are updated through: May 10, 2019

## Cel River Cherry Street to Dave Lyle Blvd

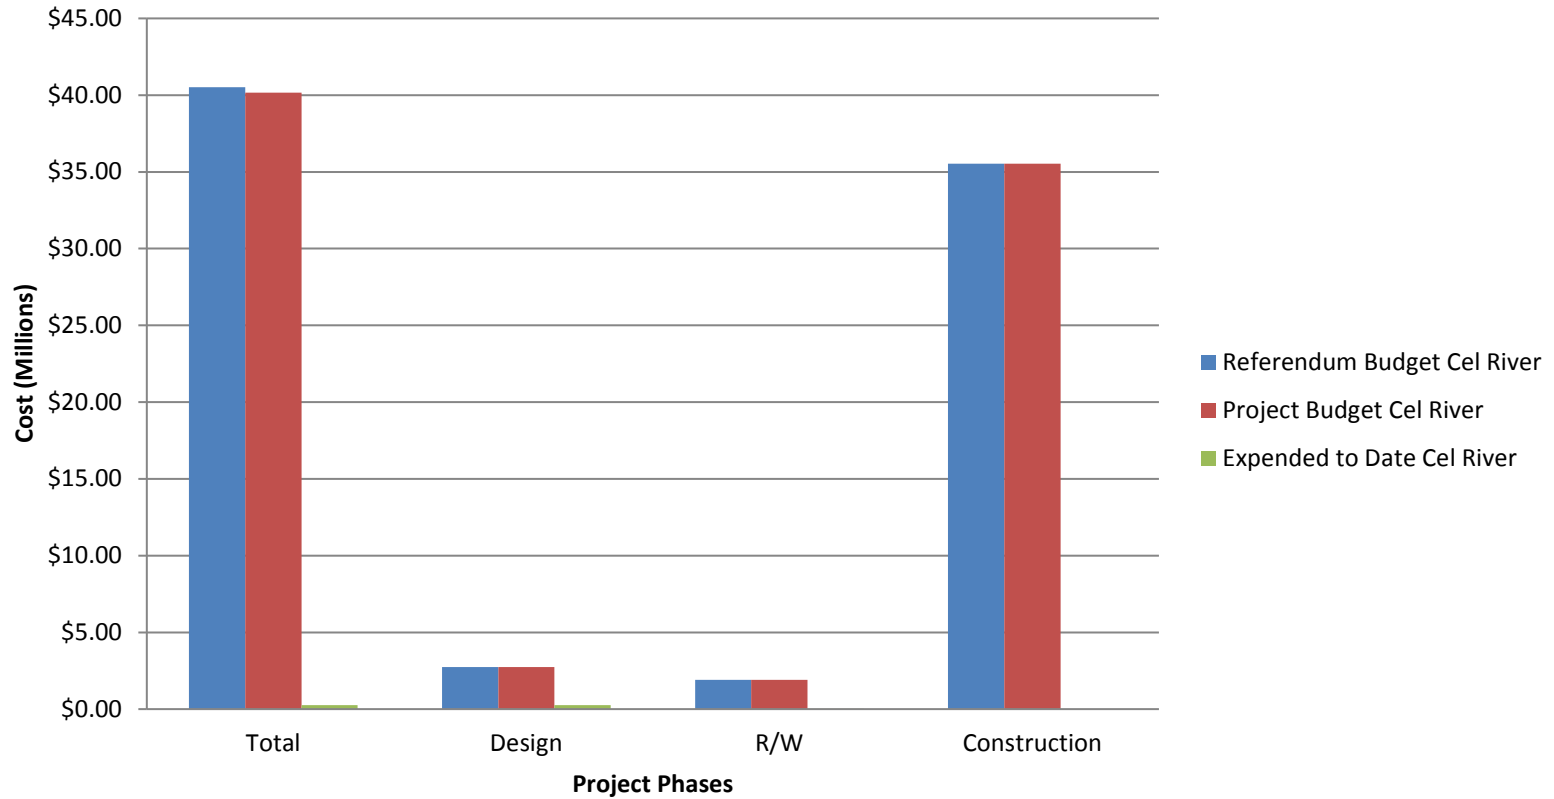


Project Status: 30% plans  
Expenses are updated through:

May 10, 2019




## FMSB I-77 to Railroad Bridge

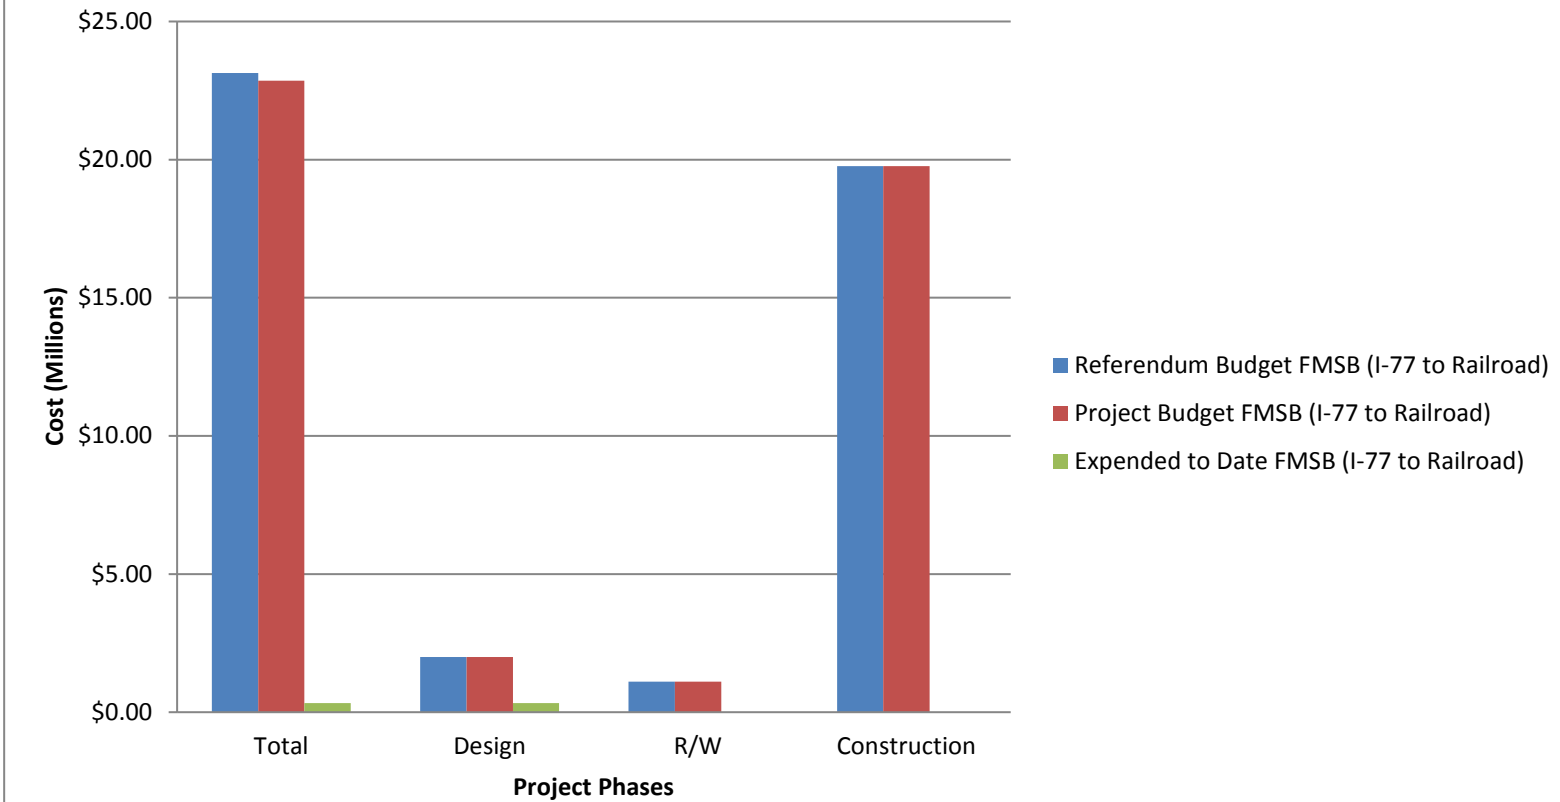


Project Status: Preliminary design  
Expenses are updated through: May 10, 2019

# SC 557 Kingsburry Road to Highway 55

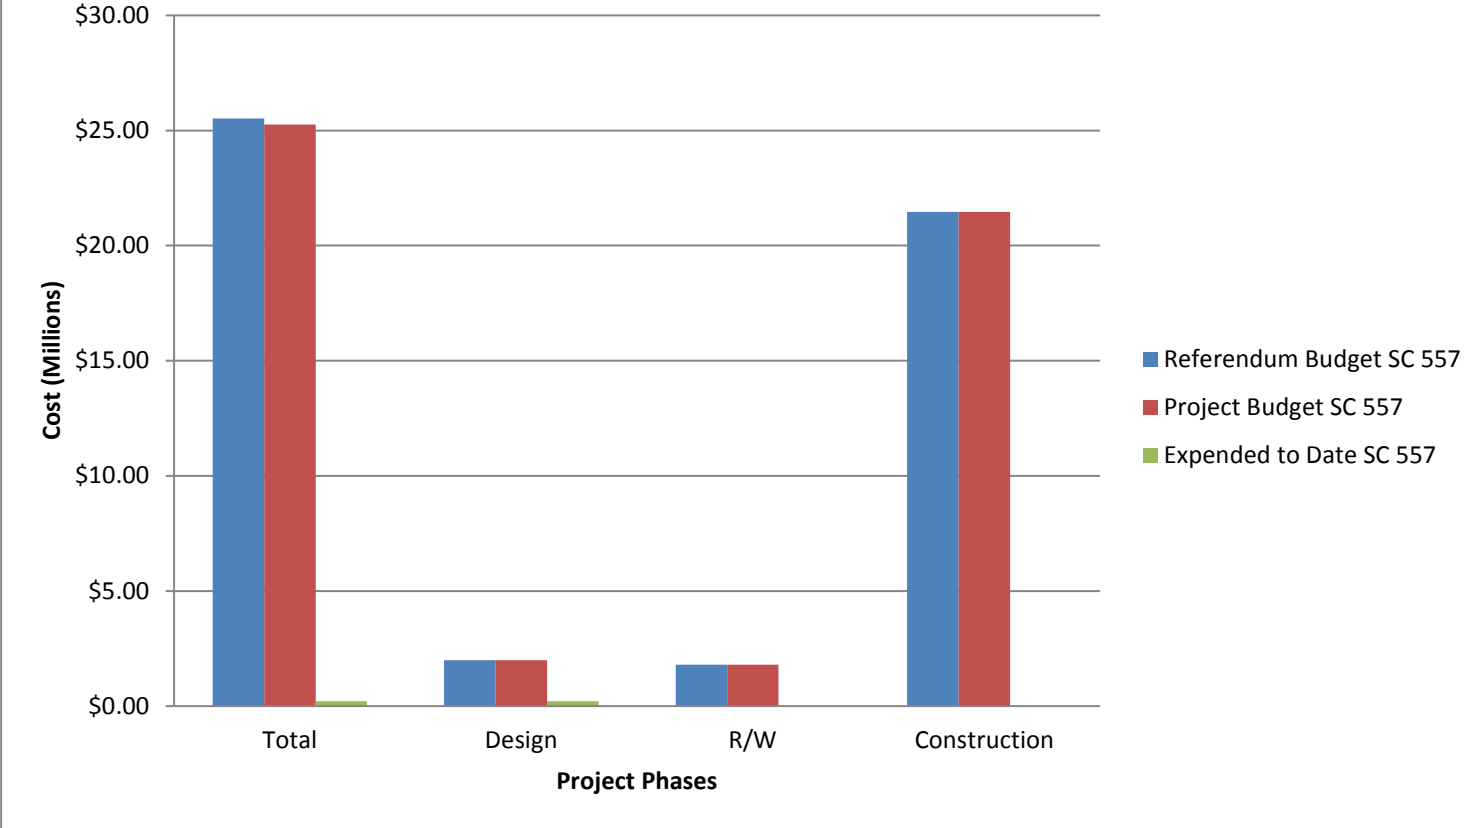

Project Status: Preliminary design  
Expenses are updated through: May 10, 2019


## Hubert Graham Ext. Windhaven Development to Dry Run Road

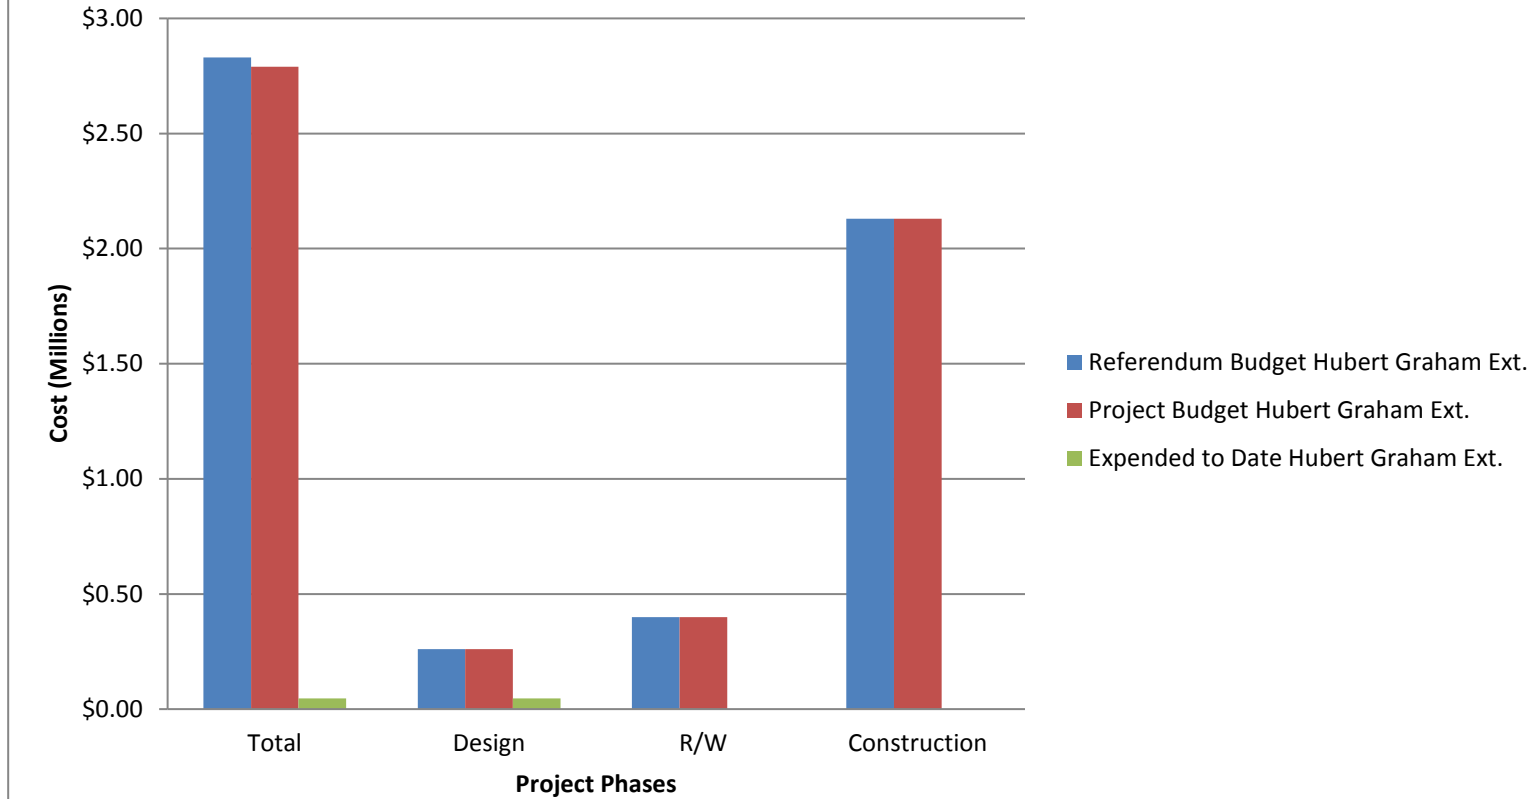

Project Status: 30% plans


Expenses are updated through: May 10, 2019

# SC 49 / 274 / 557

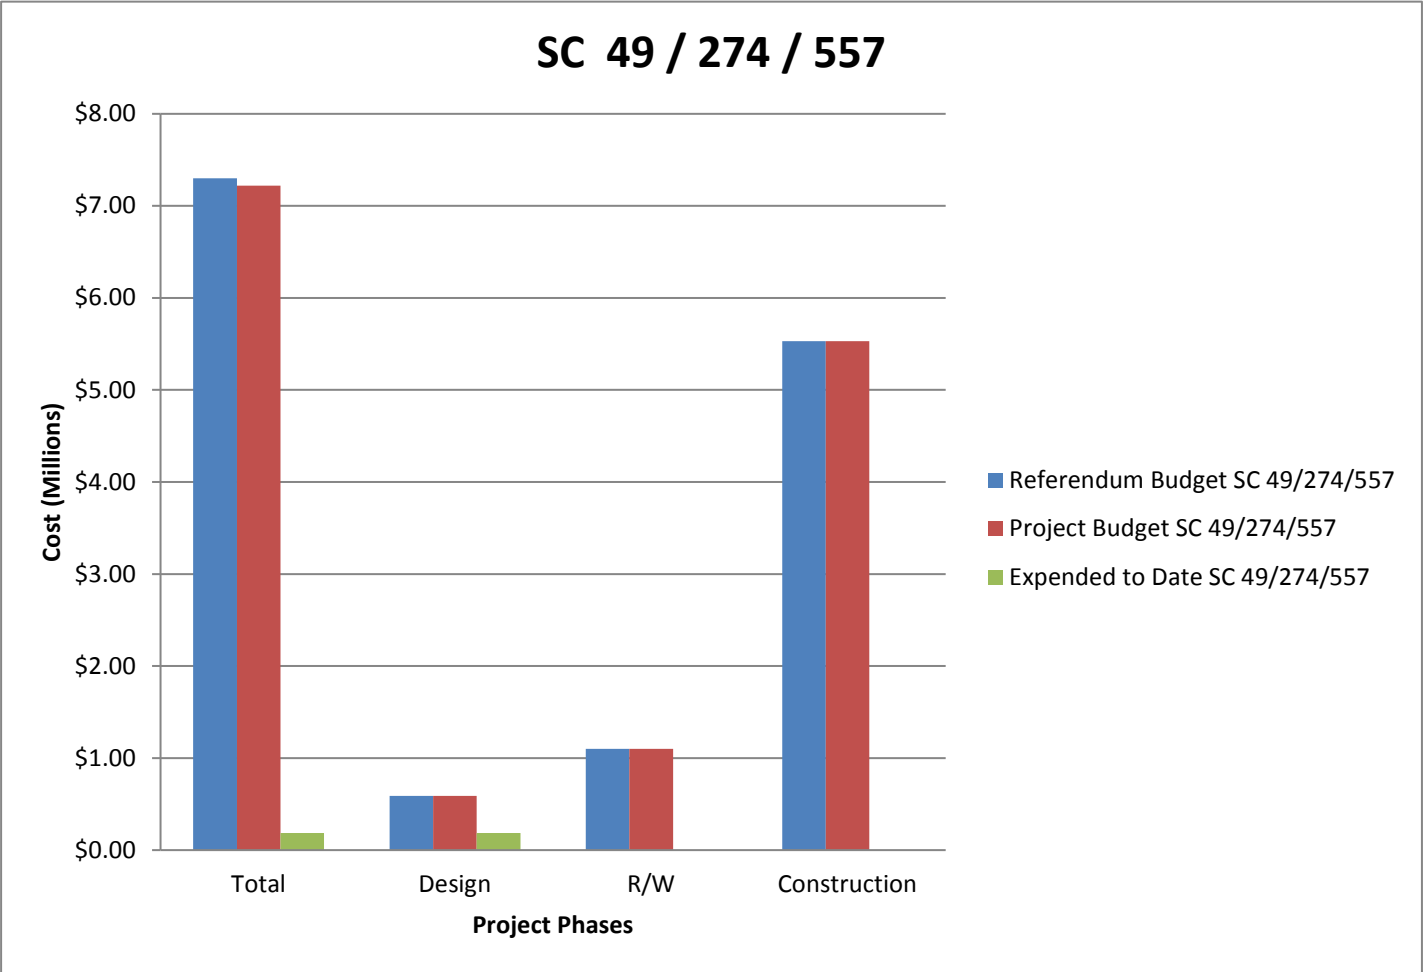


Project Status: 30% plans  
Expenses are updated through: May 10, 2019

# US 321 / Kings Mountain

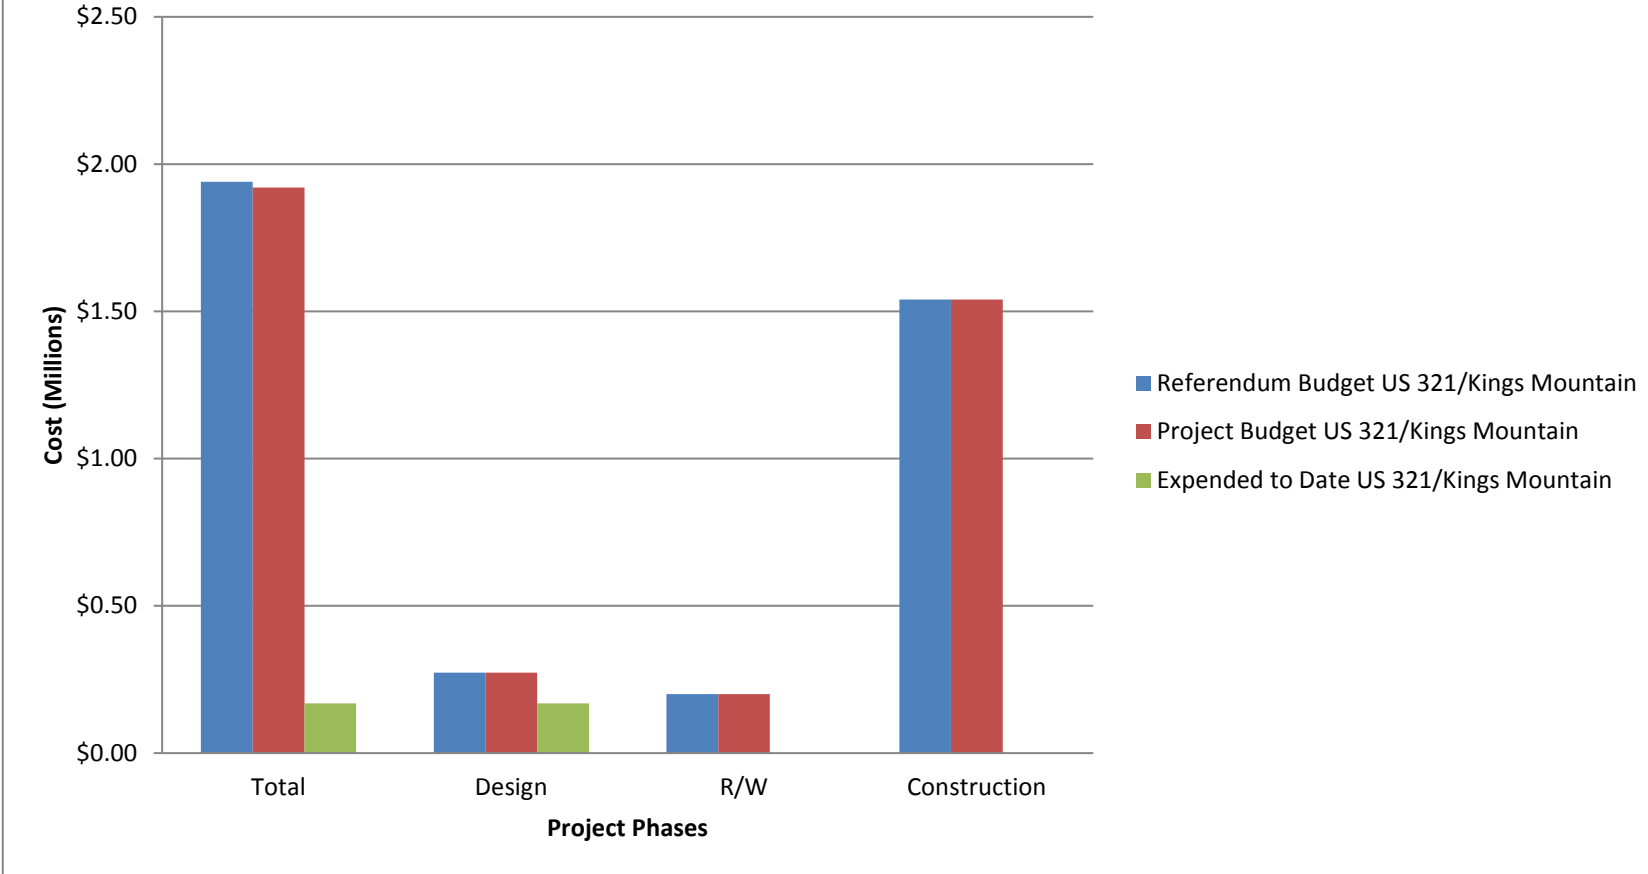

Project Status: Acquiring Right-of-Way  
Expenses are updated through: May 10, 2019


## US 21 / Springdale

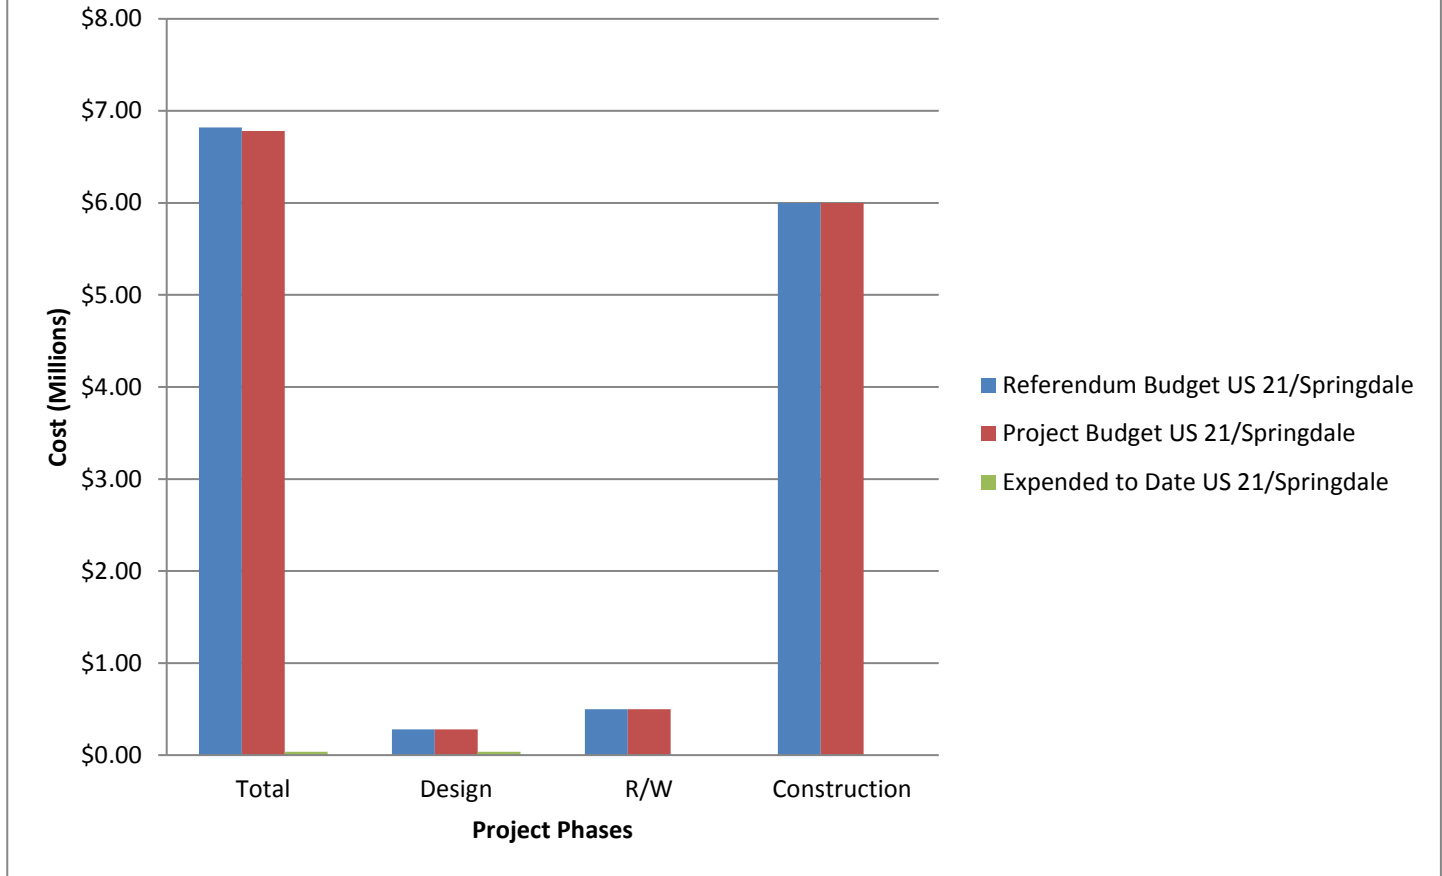

Project Status: Preliminary design  
Expenses are updated through: May 10, 2019

## Sutton Road Left Turns


### New Gray Rock Road, Sam Smith Road, Harris Road

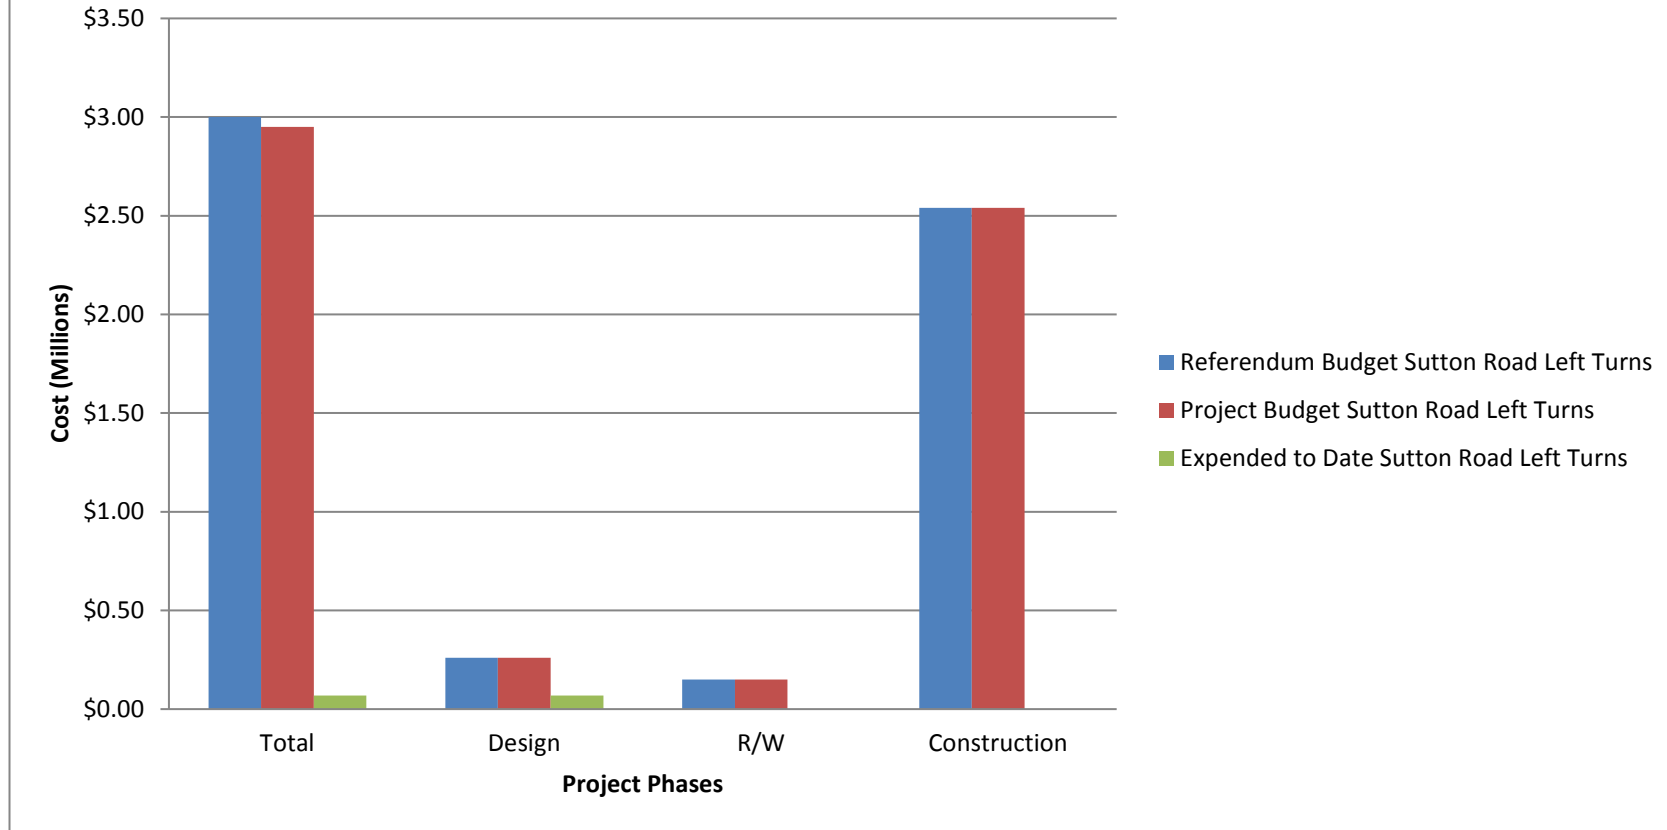

Project Status: 30% plans  
Expenses are updated through: May 10, 2019

# Flint Hill Street Community Drainage


## Frank Street, Oates Street, Haynes Street, Russell Street

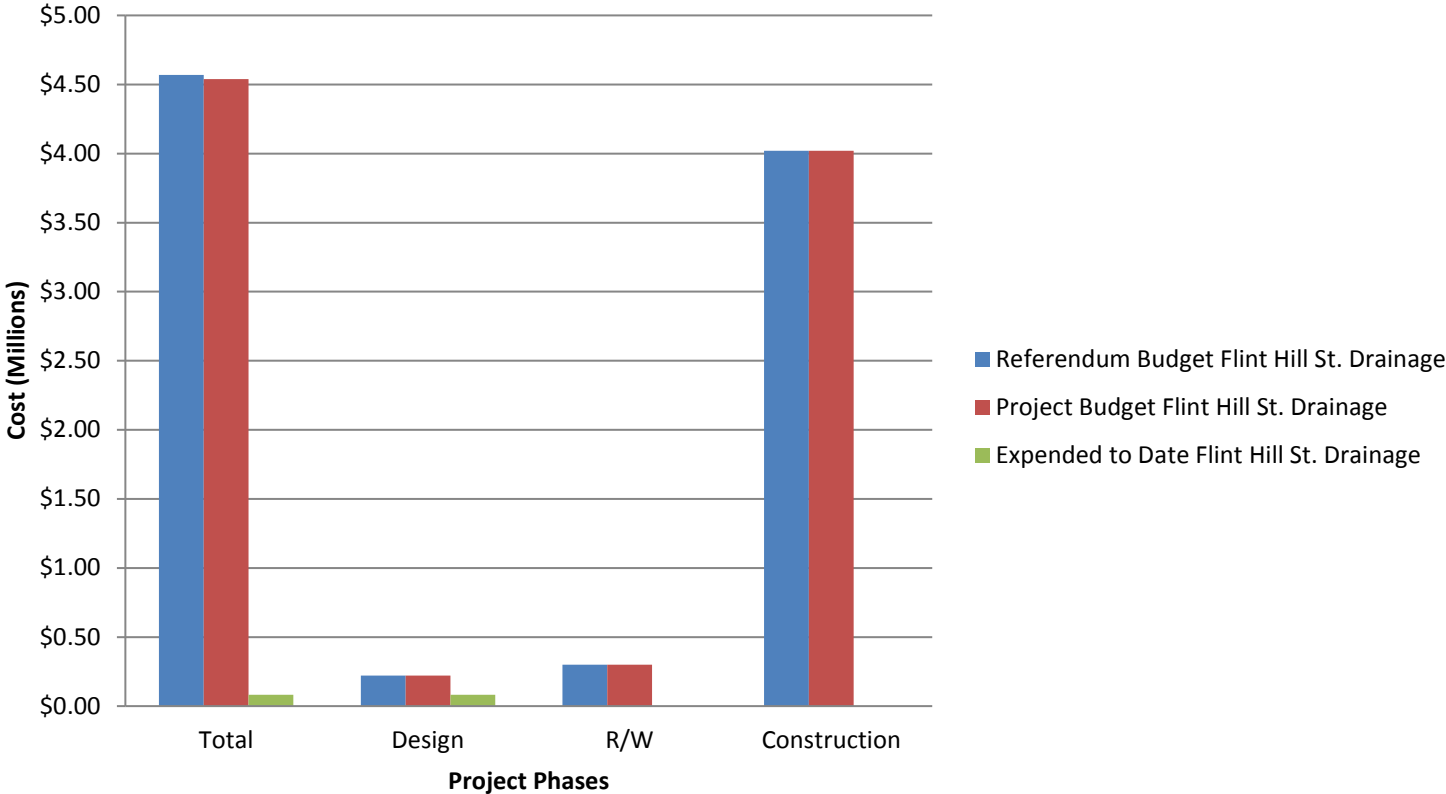

Project Status: Preliminary design  
Expenses are updated through: May 10, 2019




## Celanese / US 21

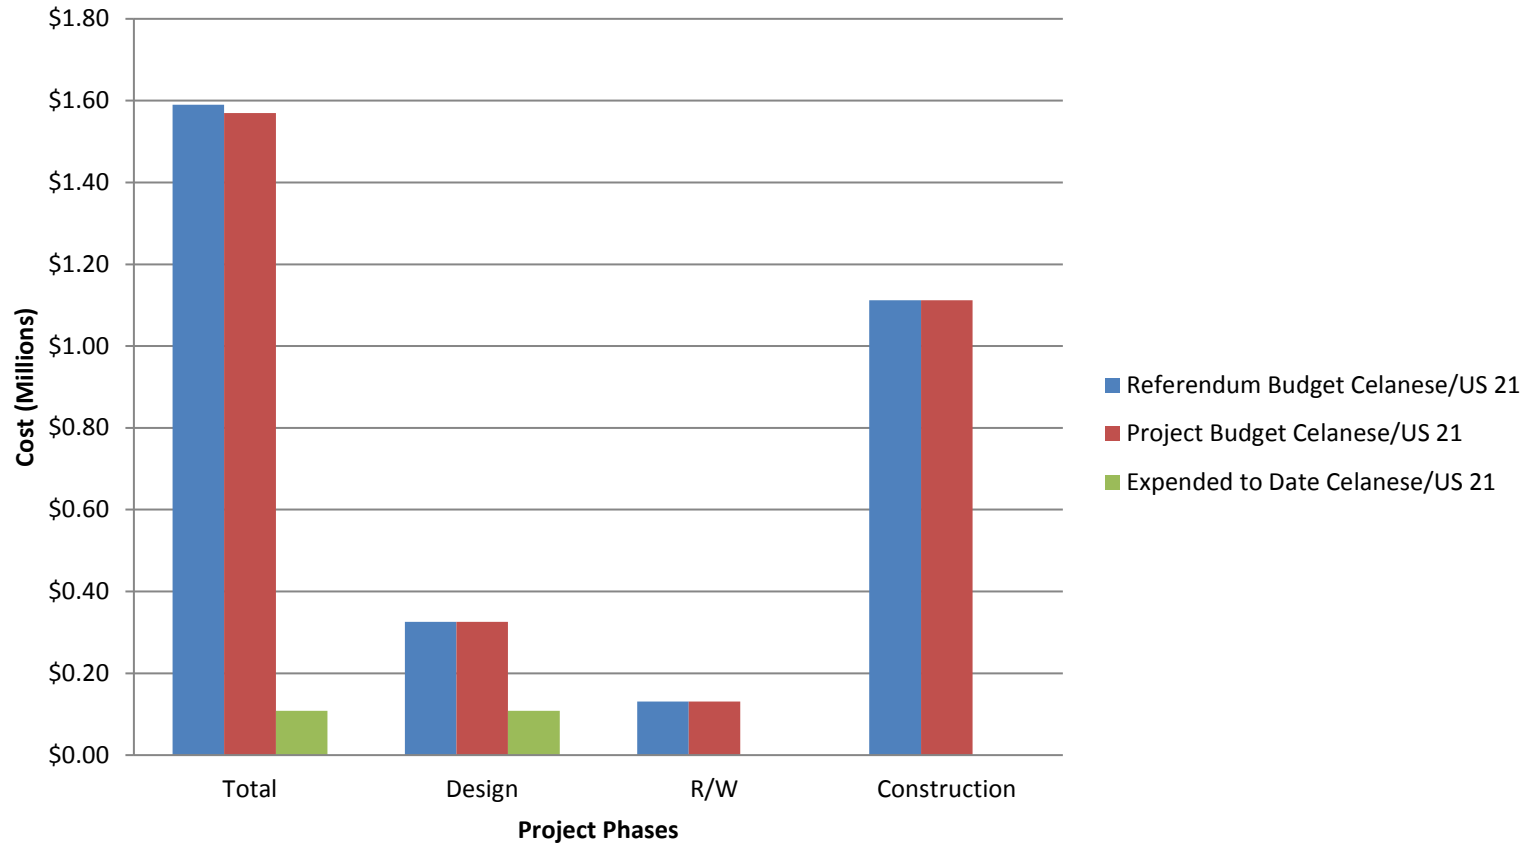

Project Status: 30% plans  
Expenses are updated through: May 10, 2019

## US 21 Turn Lanes


**Catawba Baptist Church, Hopewell Presbyterian Church, Benson Road,  
Cannon Drive, McAllister Road**

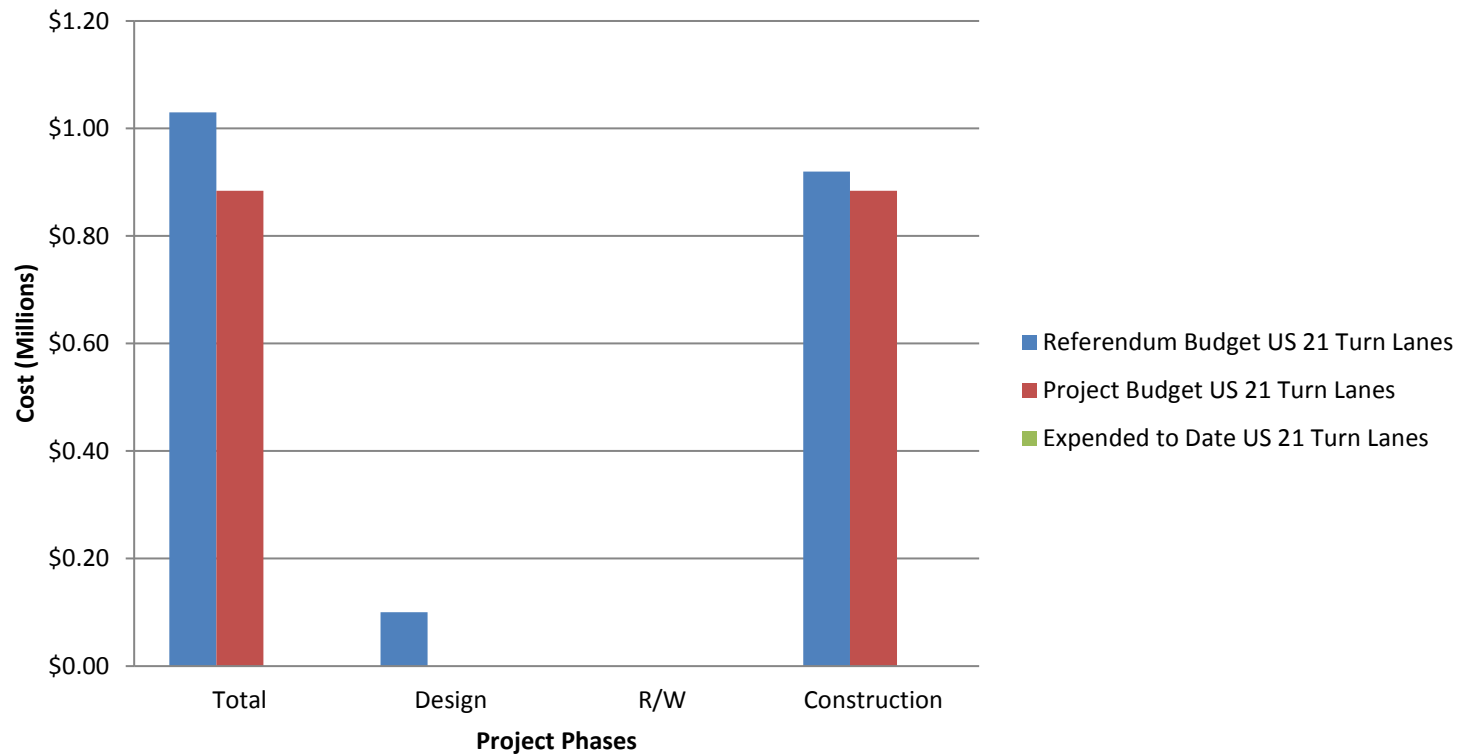

Project Status: Bids Received by SCDOT  
Expenses are updated through: May 10, 2019

Project Budget reduced due to SCDOT designing in-house, and bids being received.


## Bate Harvey Shoulder Widening Highway 557 to Green Pond Road

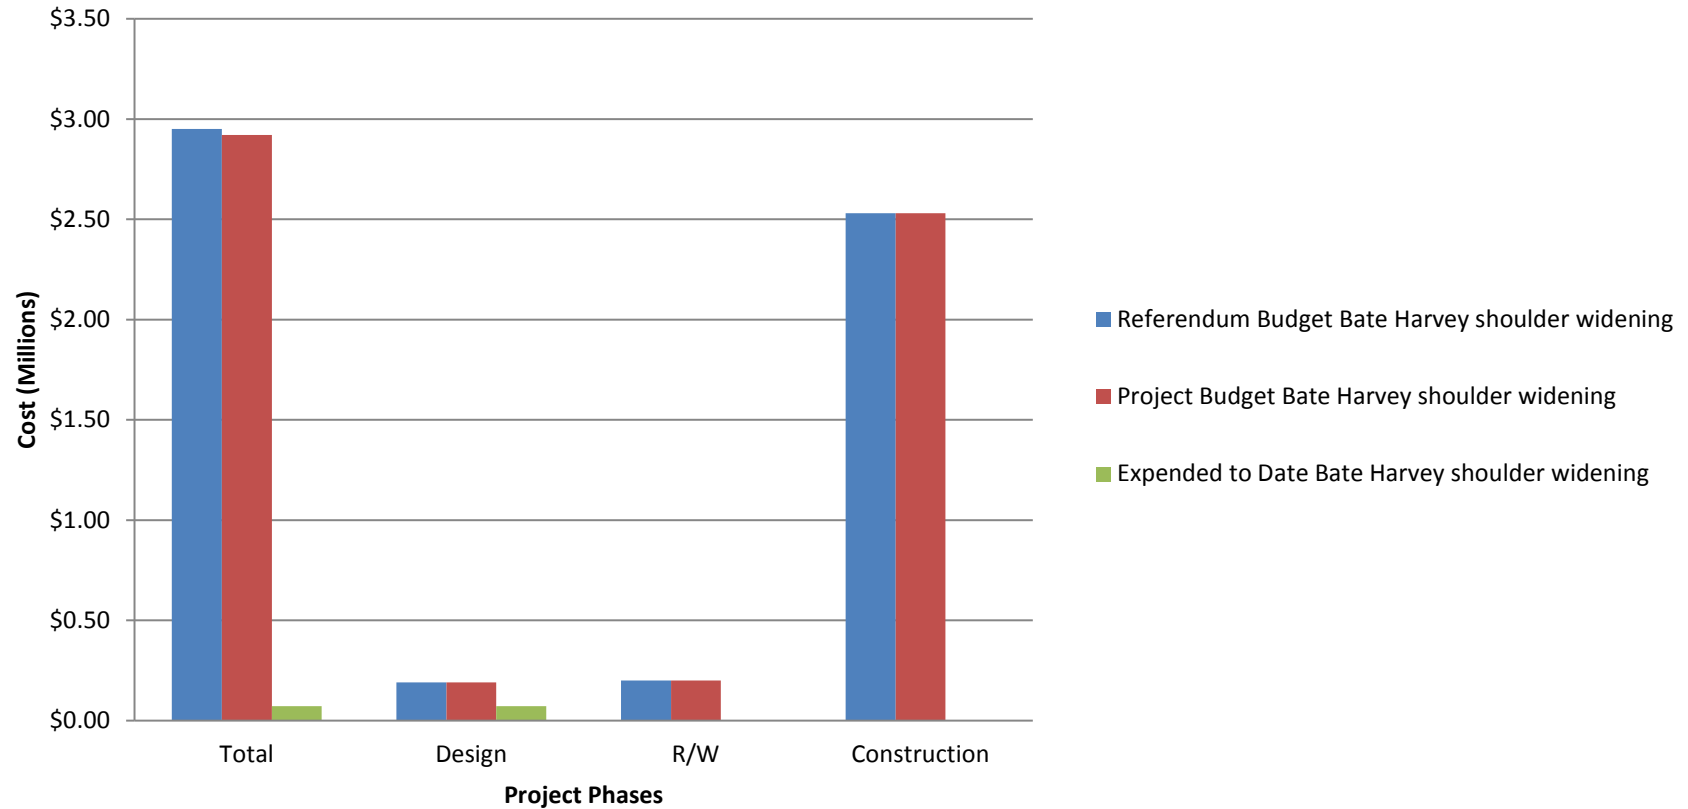

Project Status: 70% plans

Expenses are updated through: May 10, 2019


## US 21 Springfield Parkway to Highway 160

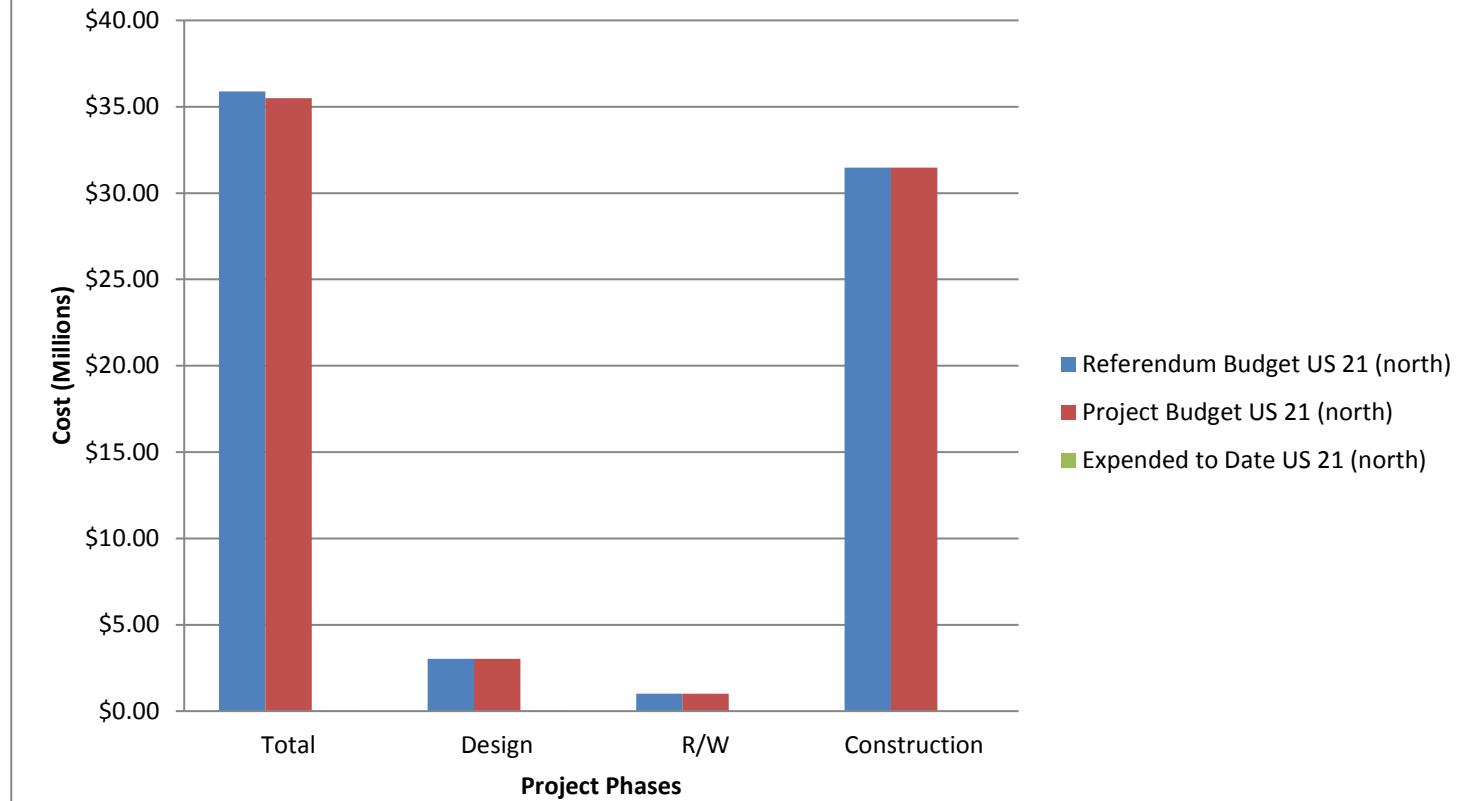

Project Status: Preliminary design  
Expenses are updated through: May 10, 2019

# Neely Road

## Robertson Road to Crawford Road

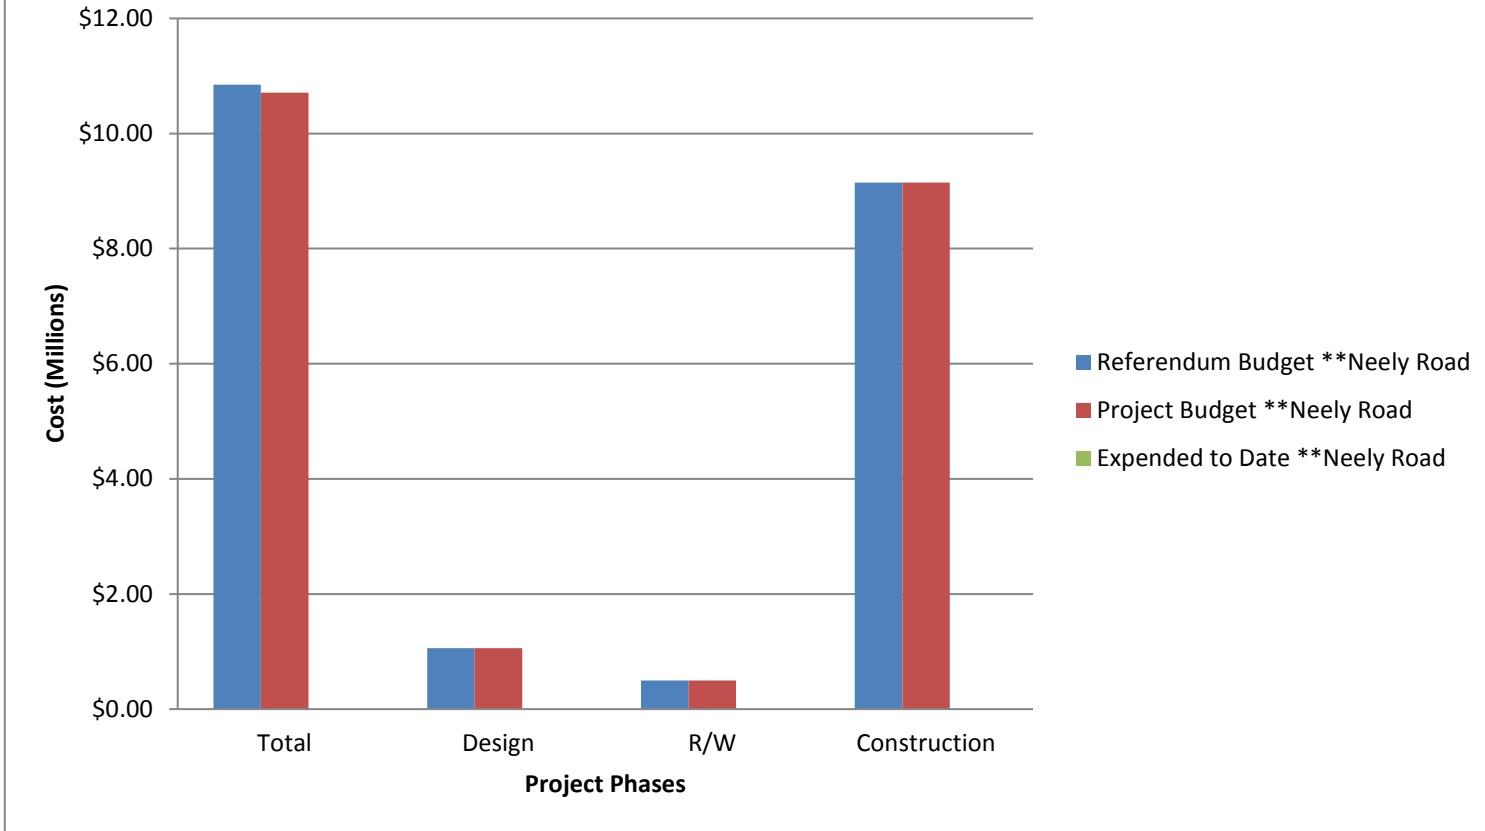

Project Status: On hold  
Expenses are updated through: May 10, 2019
