




Pennies for Progress


Pennies 2

Prepared for Council Meeting on
February 15, 2021

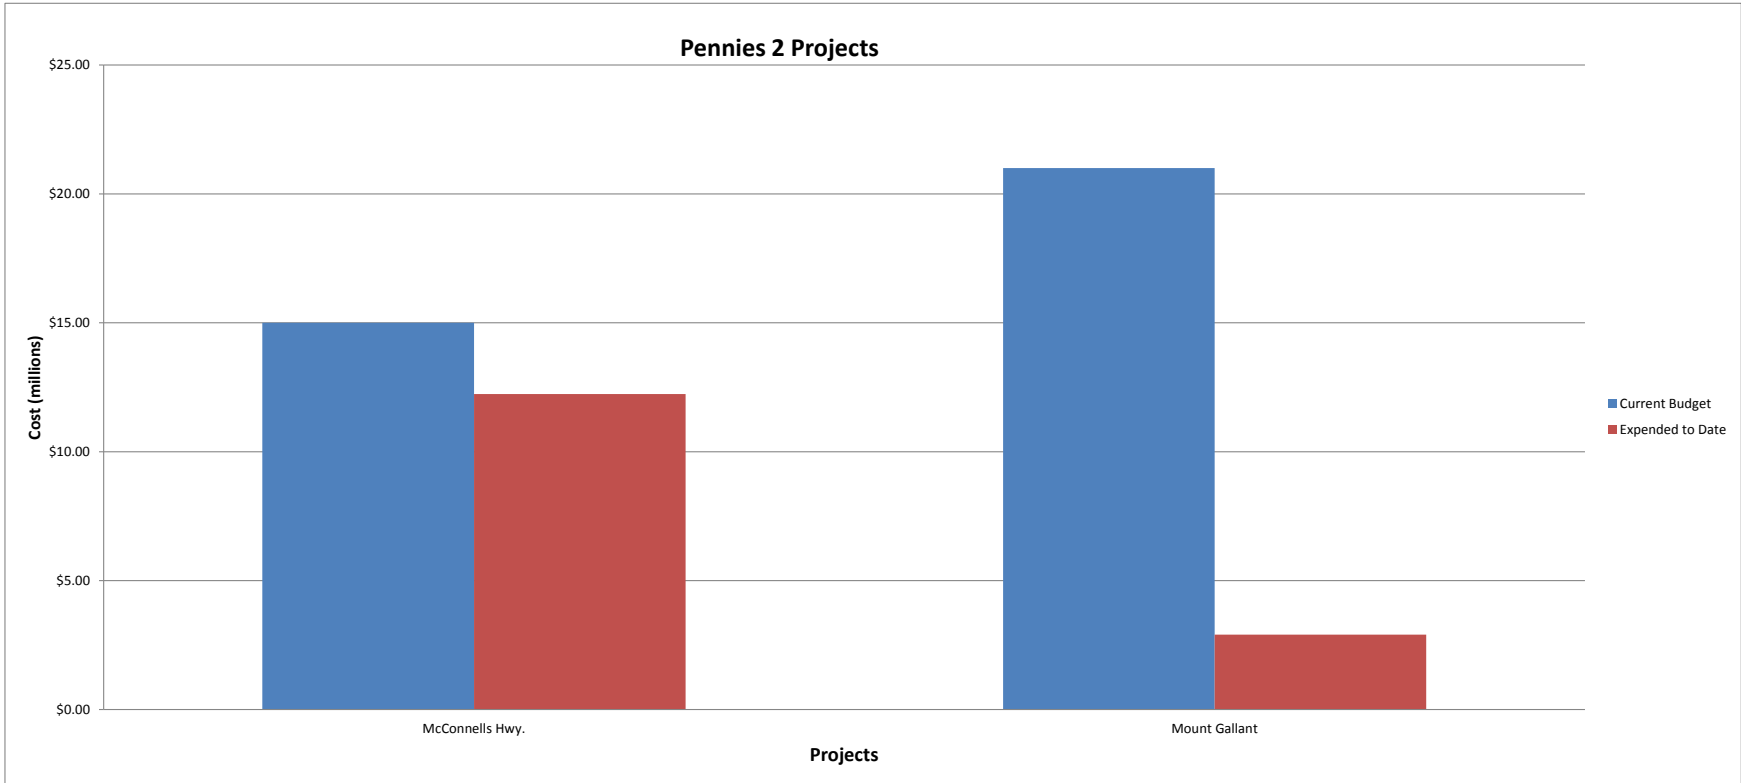

Project	Current Budget	Expended to Date	Status
McConnells Hwy.	\$15.00	\$12.24	Project Closeout
Mount Gallant	\$21.00	\$2.90	Project turned over to Panthers


Remaining Pennies 2 funds will be used on SC 557 5 lane widening project. See Pennies 4 report.

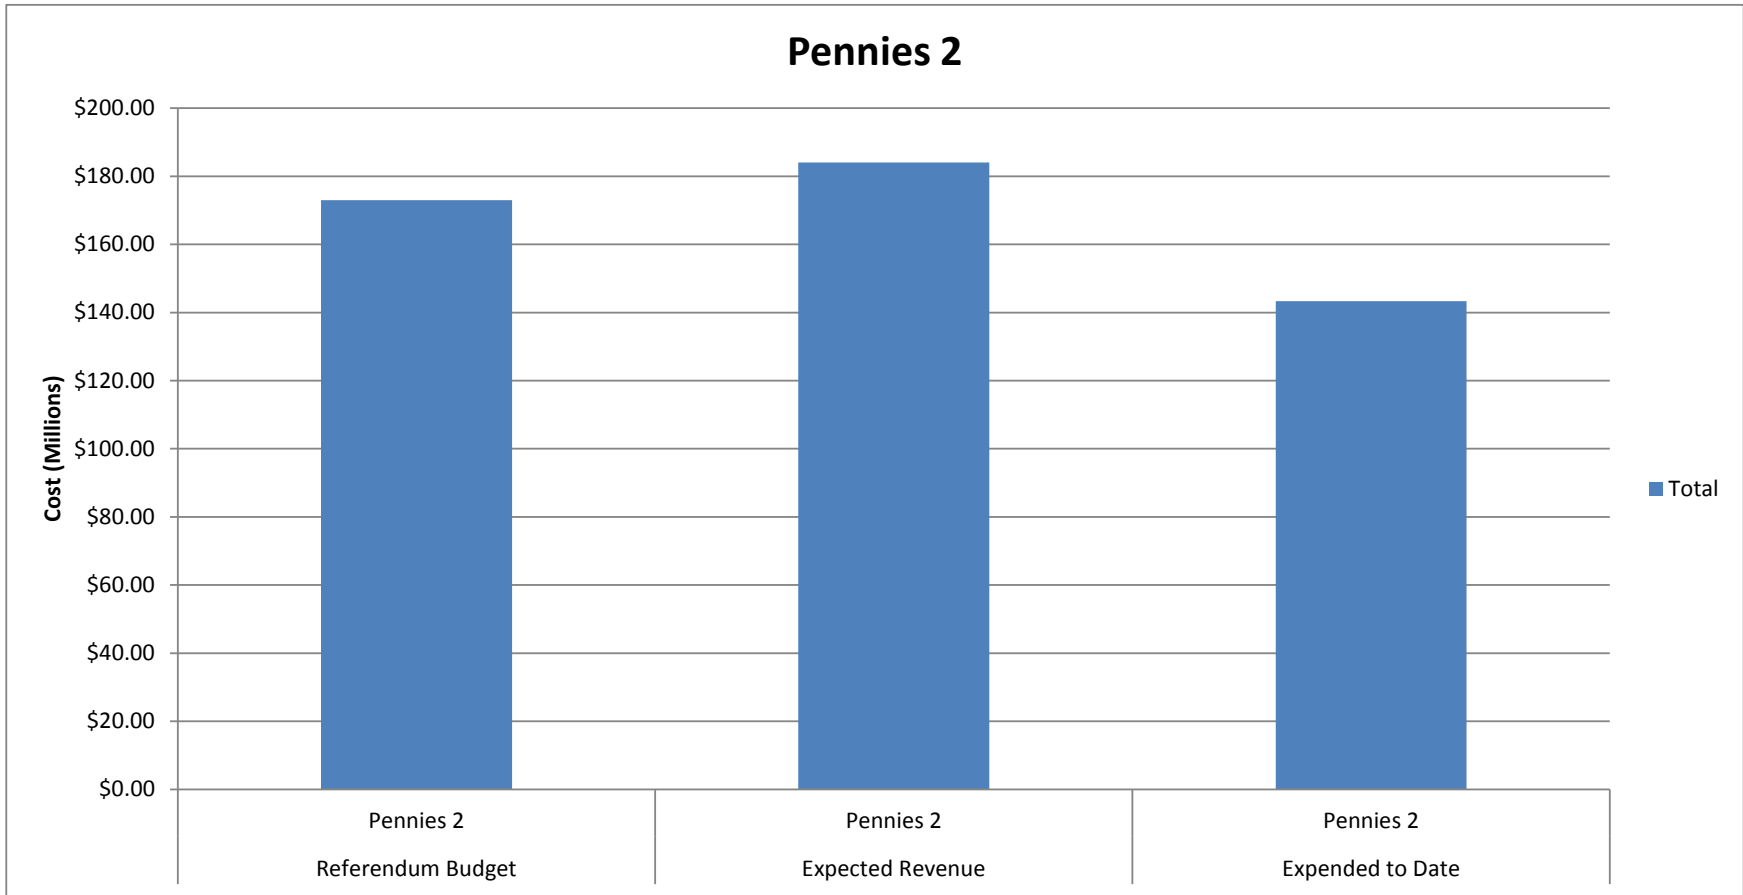

		Total
Referendum Budget	Pennies 2	\$173.00
Expected Revenue	Pennies 2	\$184.00
Expended to Date	Pennies 2	\$143.37


* Dollars are in millions

McConnells Highway Highway 901 to Eastview Road

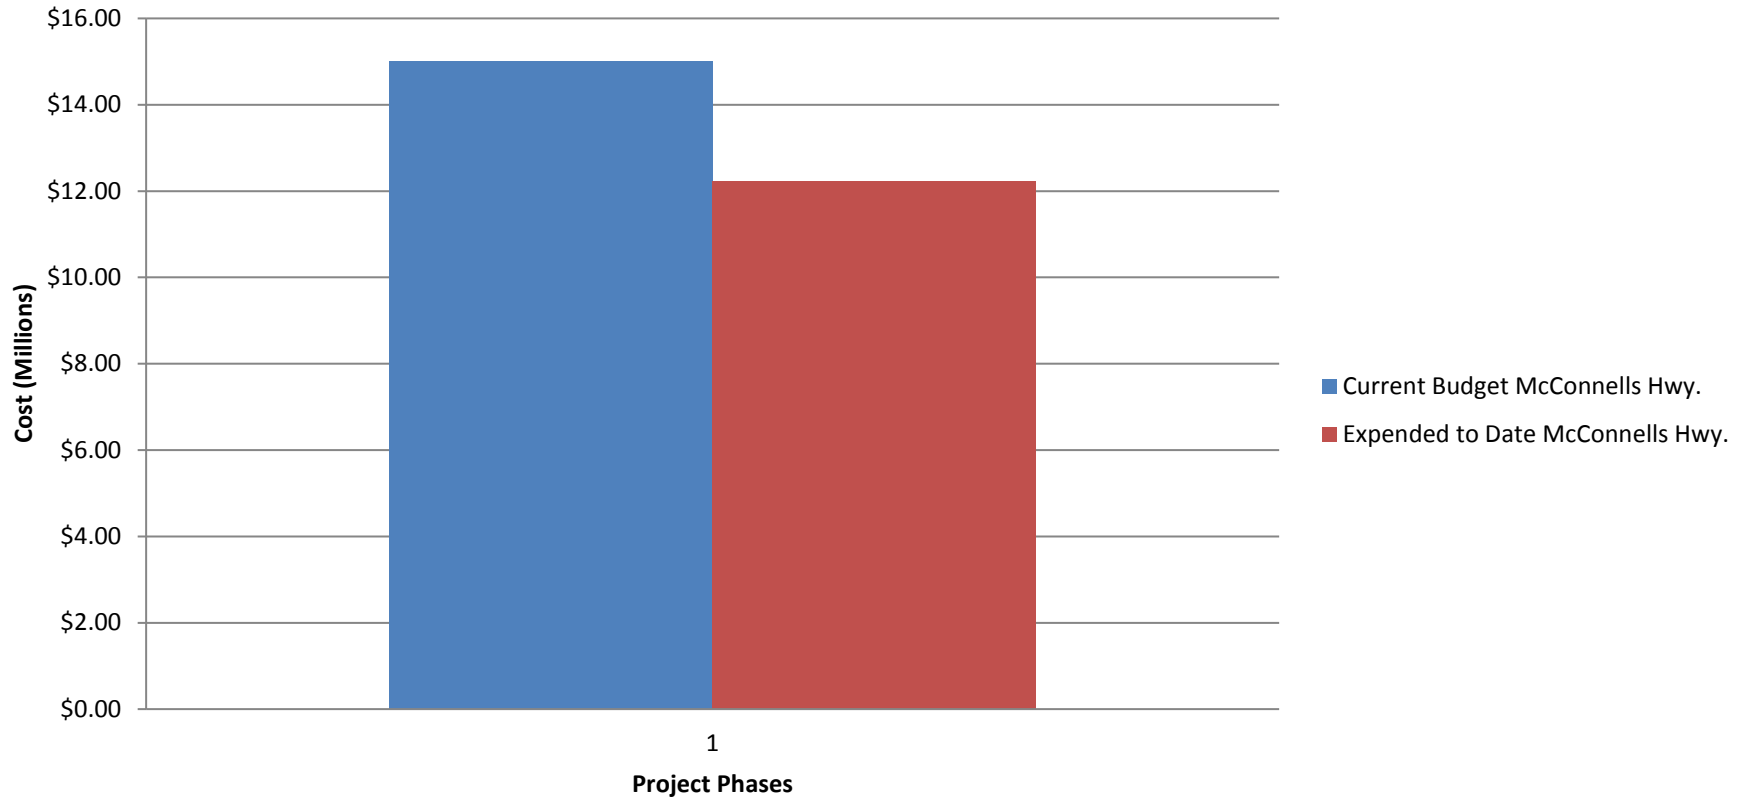

Project Status: Project Closeout
Expenses are updated through: December 31, 2020

Mount Gallant Anderson Road to Dave Lyle Blvd

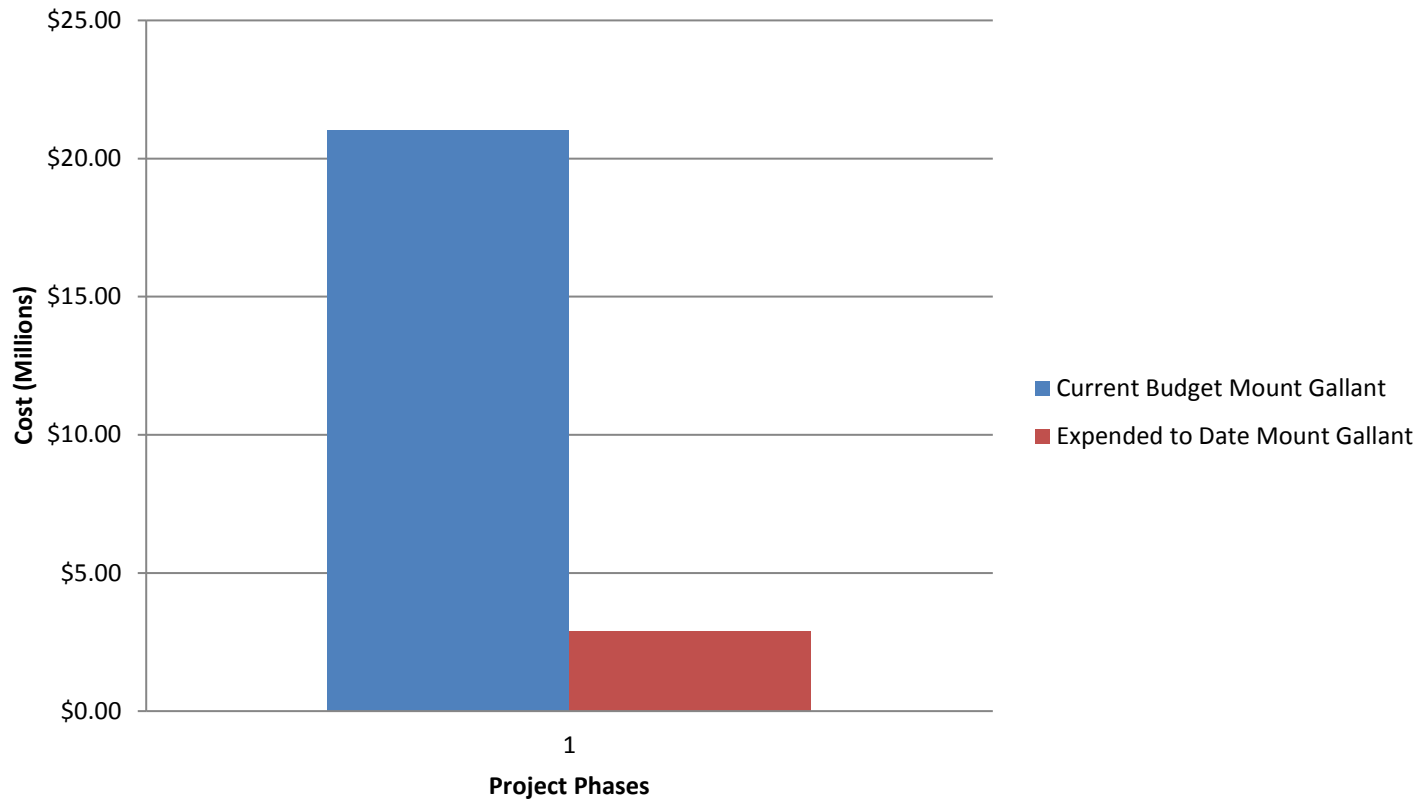

Project Status: Project turned over to Panthers
Expenses are updated through: December 31, 2020


*Budget increased due to final plans and agreement with Panthers.




Pennies for Progress

Pennies 3

Prepared for Council Meeting on
February 15, 2021

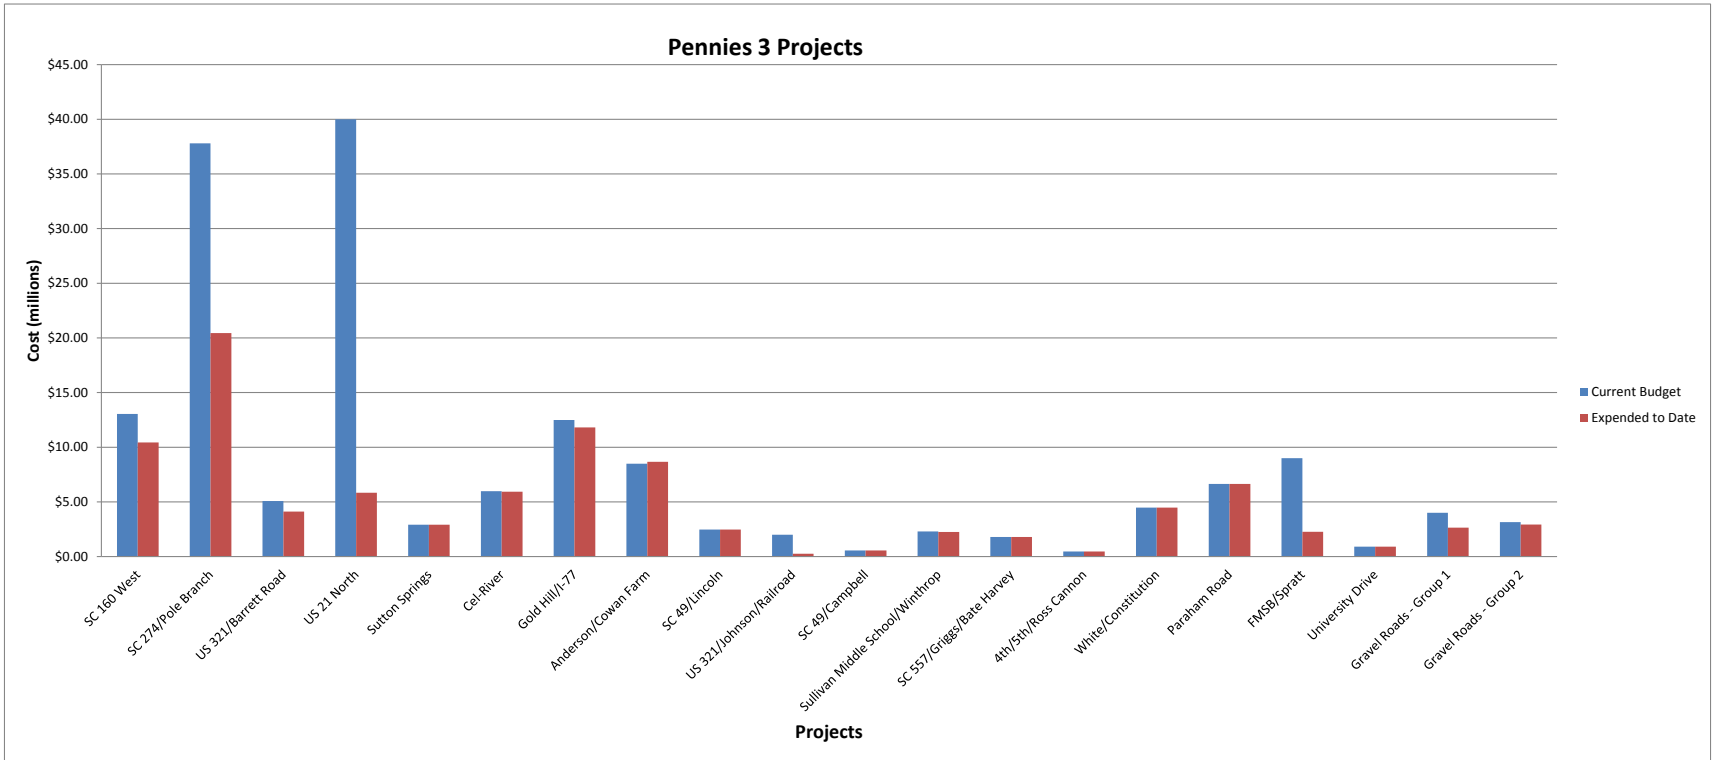

Project	Current Budget	Expended to Date	Status
SC 160 West	\$13.05	\$10.43	Project Closeout
SC 274/Pole Branch	\$37.80	\$20.44	Under construction
US 321/Barrett Road	\$5.08	\$4.11	Project Closeout
US 21 North	\$40.00	\$5.84	Acquiring Right-of-Way
Sutton Springs	\$2.91	\$2.91	Complete
Cel-River	\$5.98	\$5.93	Complete
Gold Hill/I-77	\$12.50	\$11.81	Under construction
Anderson/Cowan Farm	\$8.50	\$8.67	Complete
SC 49/Lincoln	\$2.46	\$2.46	Complete
US 321/Johnson/Railroad	\$2.00	\$0.26	Acquiring Right-of-Way/Final Plans
SC 49/Campbell	\$0.56	\$0.56	Complete
Sullivan Middle School/Winthrop	\$2.30	\$2.25	Complete
SC 557/Griggs/Bate Harvey	\$1.80	\$1.80	Complete
4th/5th/Ross Cannon	\$0.46	\$0.46	Complete
White/Constitution	\$4.48	\$4.48	Complete
Paraham Road	\$6.65	\$6.65	Complete
FMSB/Spratt	\$9.00	\$2.27	Bid Phase
University Drive	\$0.91	\$0.91	Complete
Gravel Roads - Group 1	\$4.00	\$2.65	Ongoing
Gravel Roads - Group 2	\$3.15	\$2.93	Ongoing

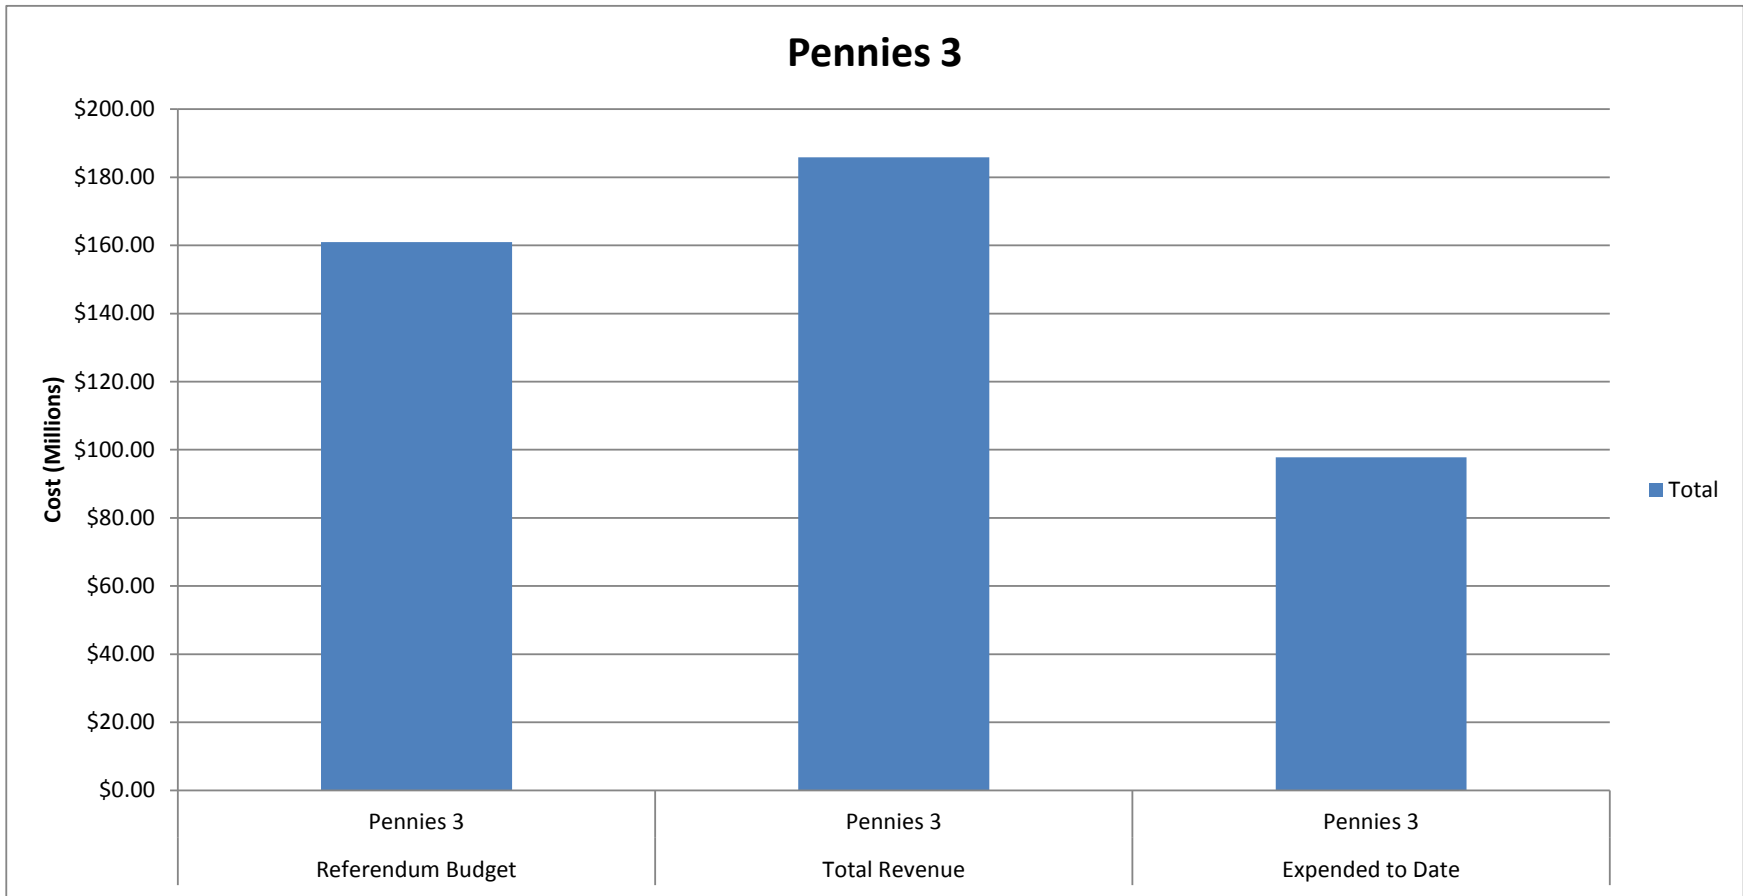


		Total
Referendum Budget	Pennies 3	\$161.00
Total Revenue	Pennies 3	\$185.88
Expended to Date	Pennies 3	\$97.82

* Dollars are in millions

SC 160 West


Gold Hill Road to NC State Line

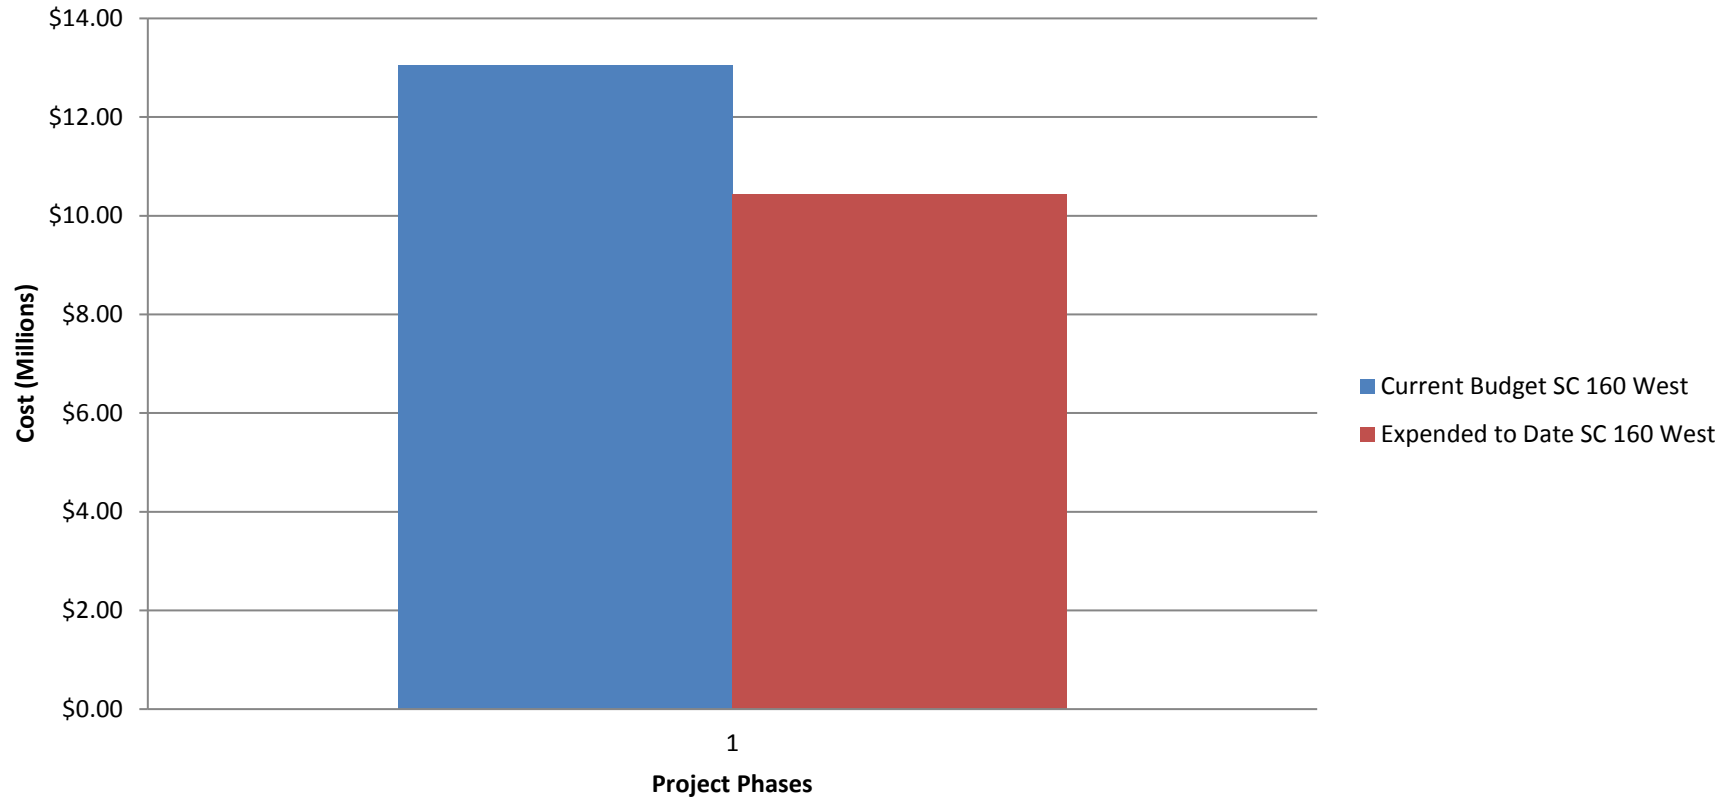

Project Status: Project Closeout
Expenses are updated through: December 31, 2020


274 Pole Branch

Hwy 274: Highway 49 to Pole Branch Road
Pole Branch: Highway 274 to NC State Line

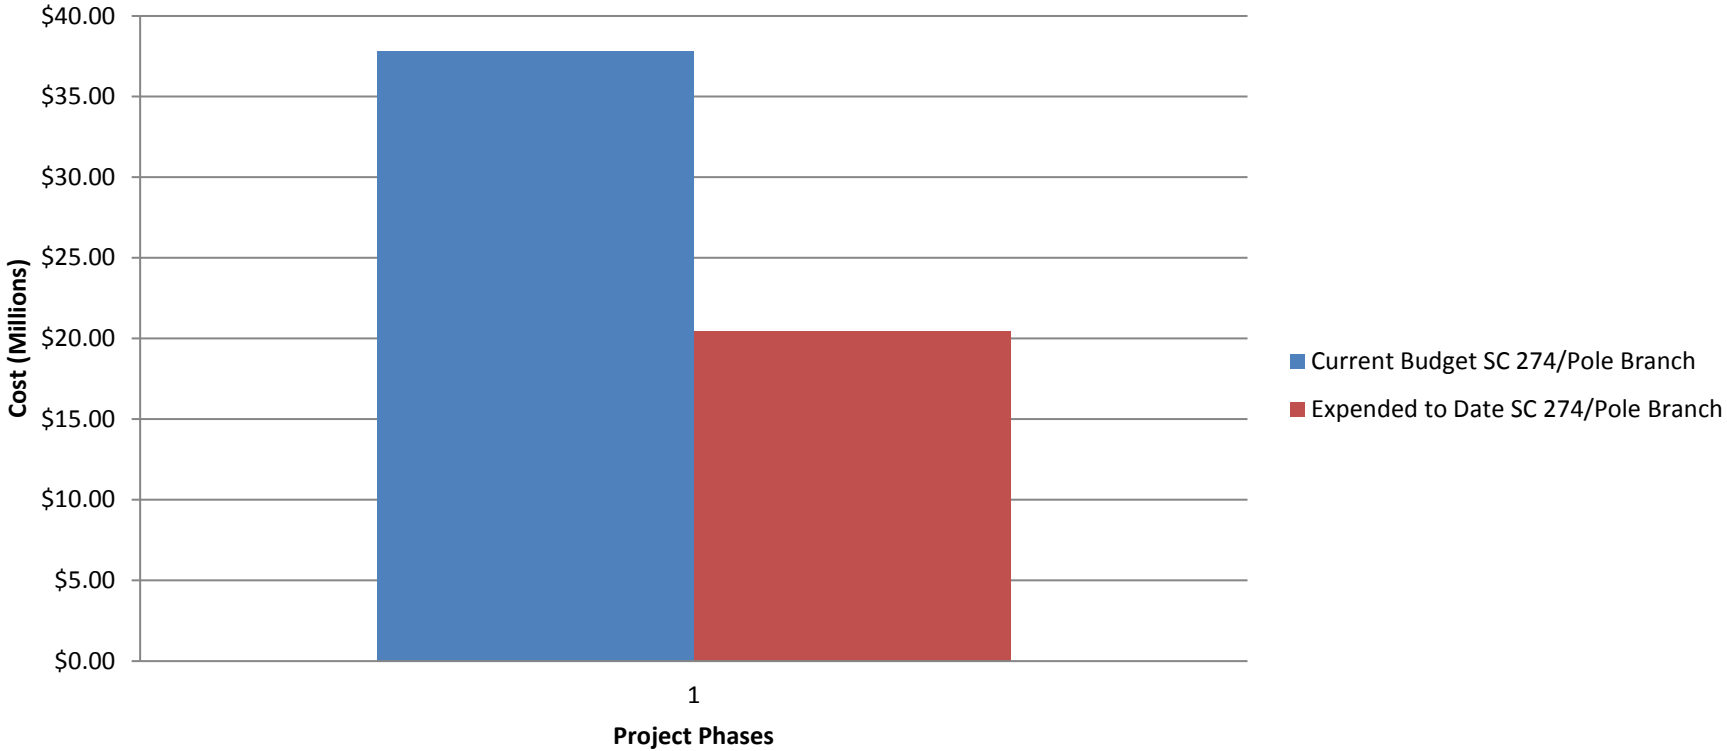


Project Status: Under construction
Expenses are updated through: December 31, 2020

US 321 - Barrett Connector Road

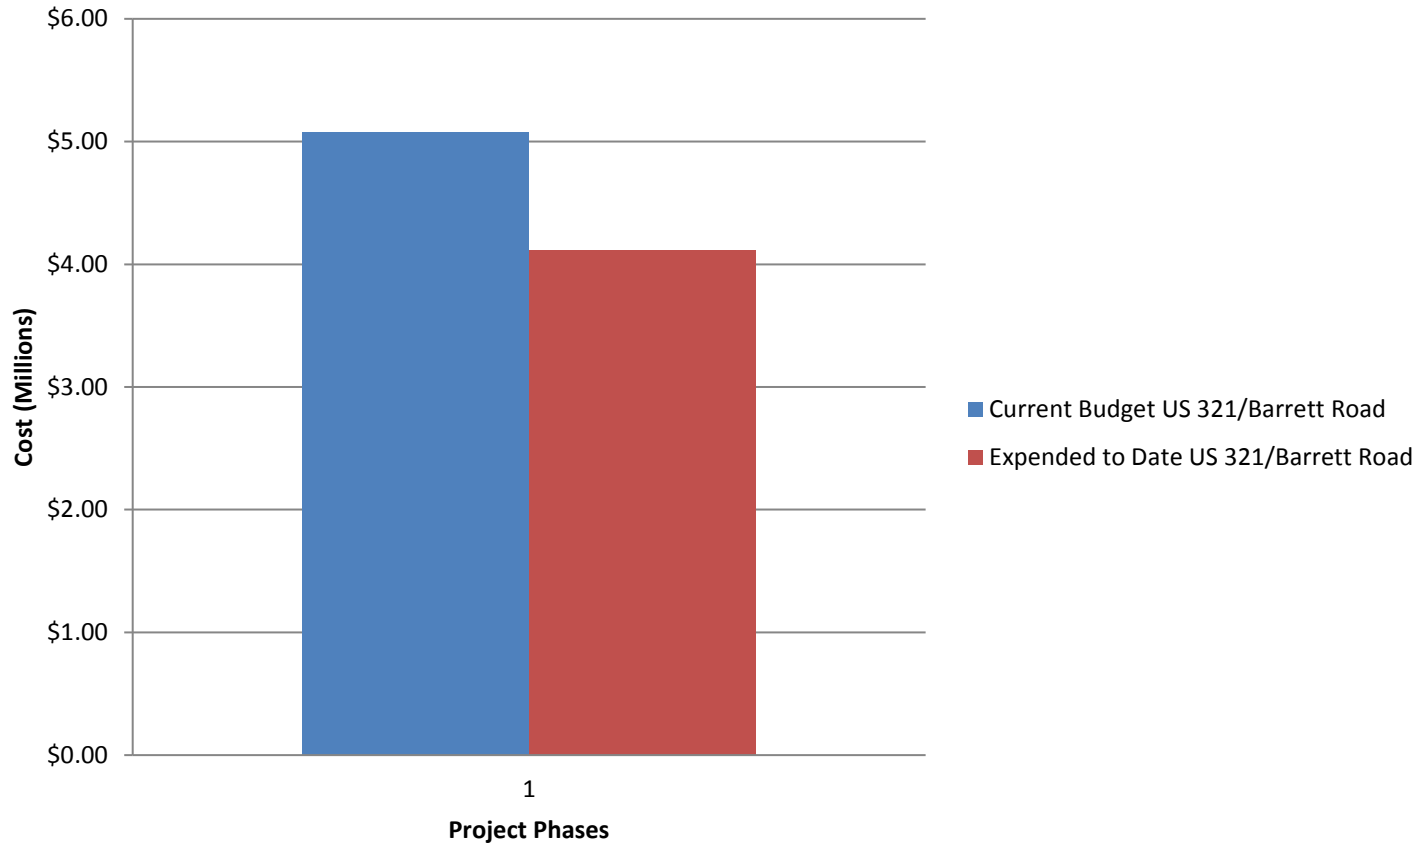


Project Status: Project Closeout
Expenses are updated through: December 31, 2020

US 21 North/Highway 51
US 21: Springfield Parkway to Springhill Farm Road
Hwy 51: US 21 to NC State Line

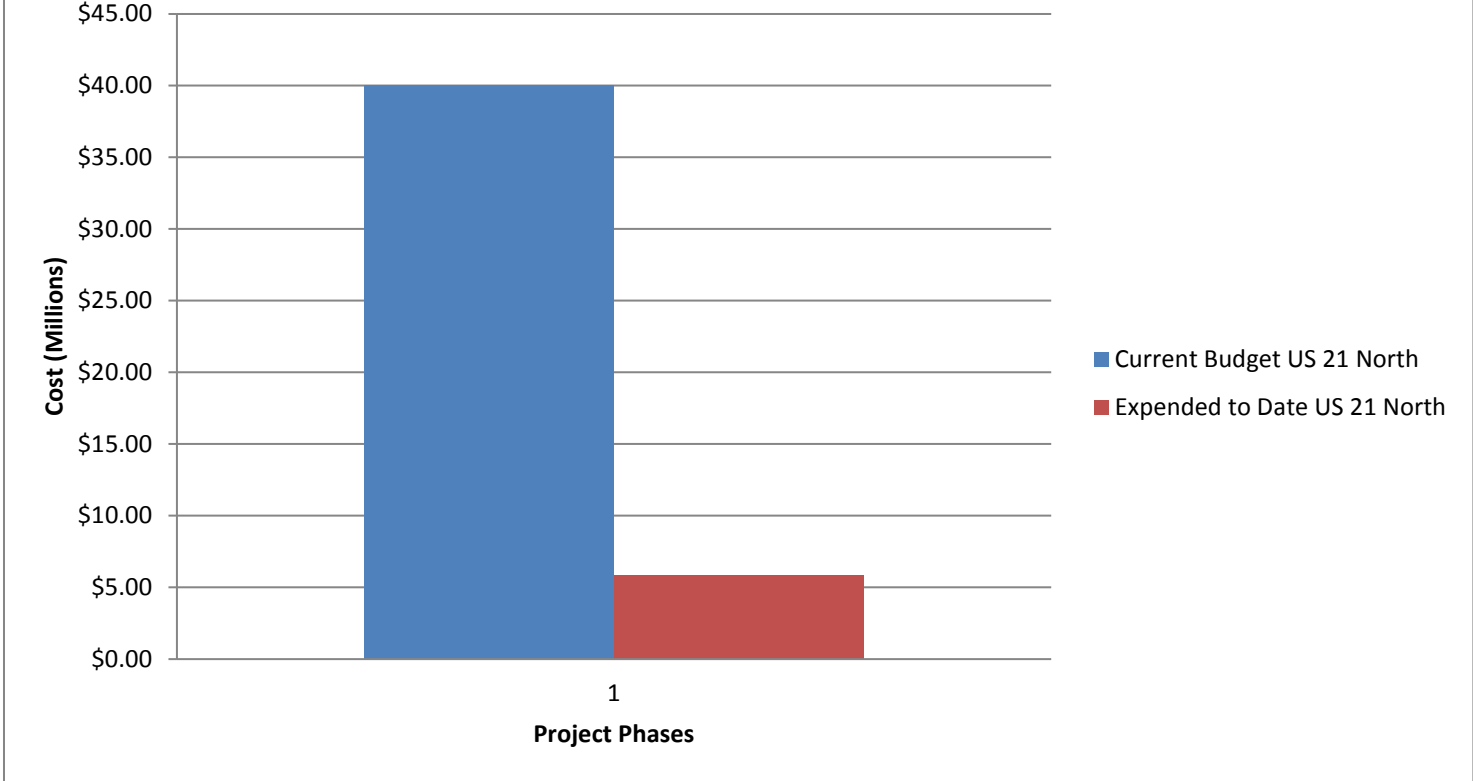

Project Status: Acquiring Right-of-Way
Expenses are updated through: December 31, 2020


Sutton Springs

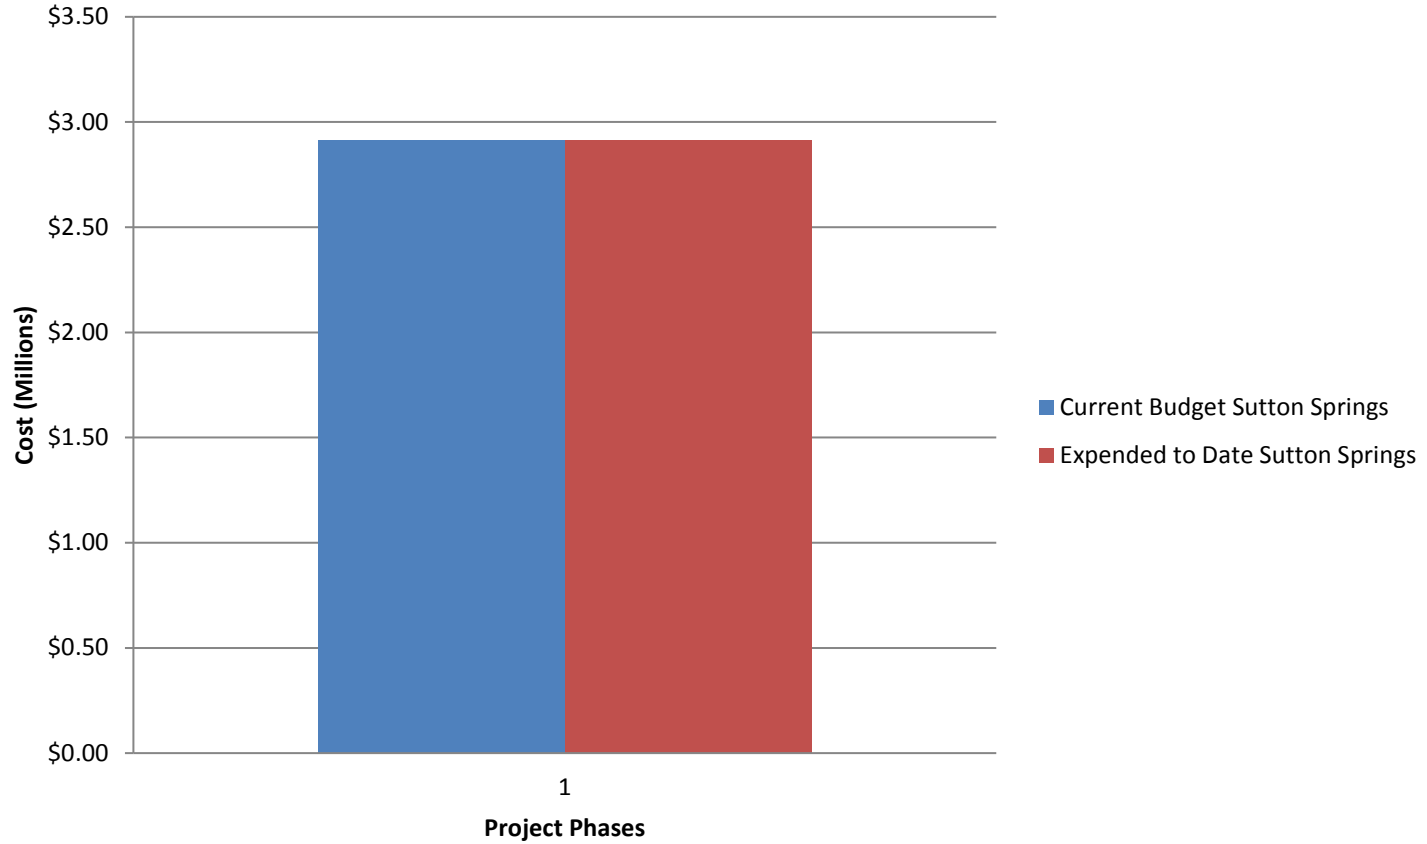


Project Status: Complete
Expenses are updated through: December 31, 2020

Cel-River

Cherry Road to Cherry Street

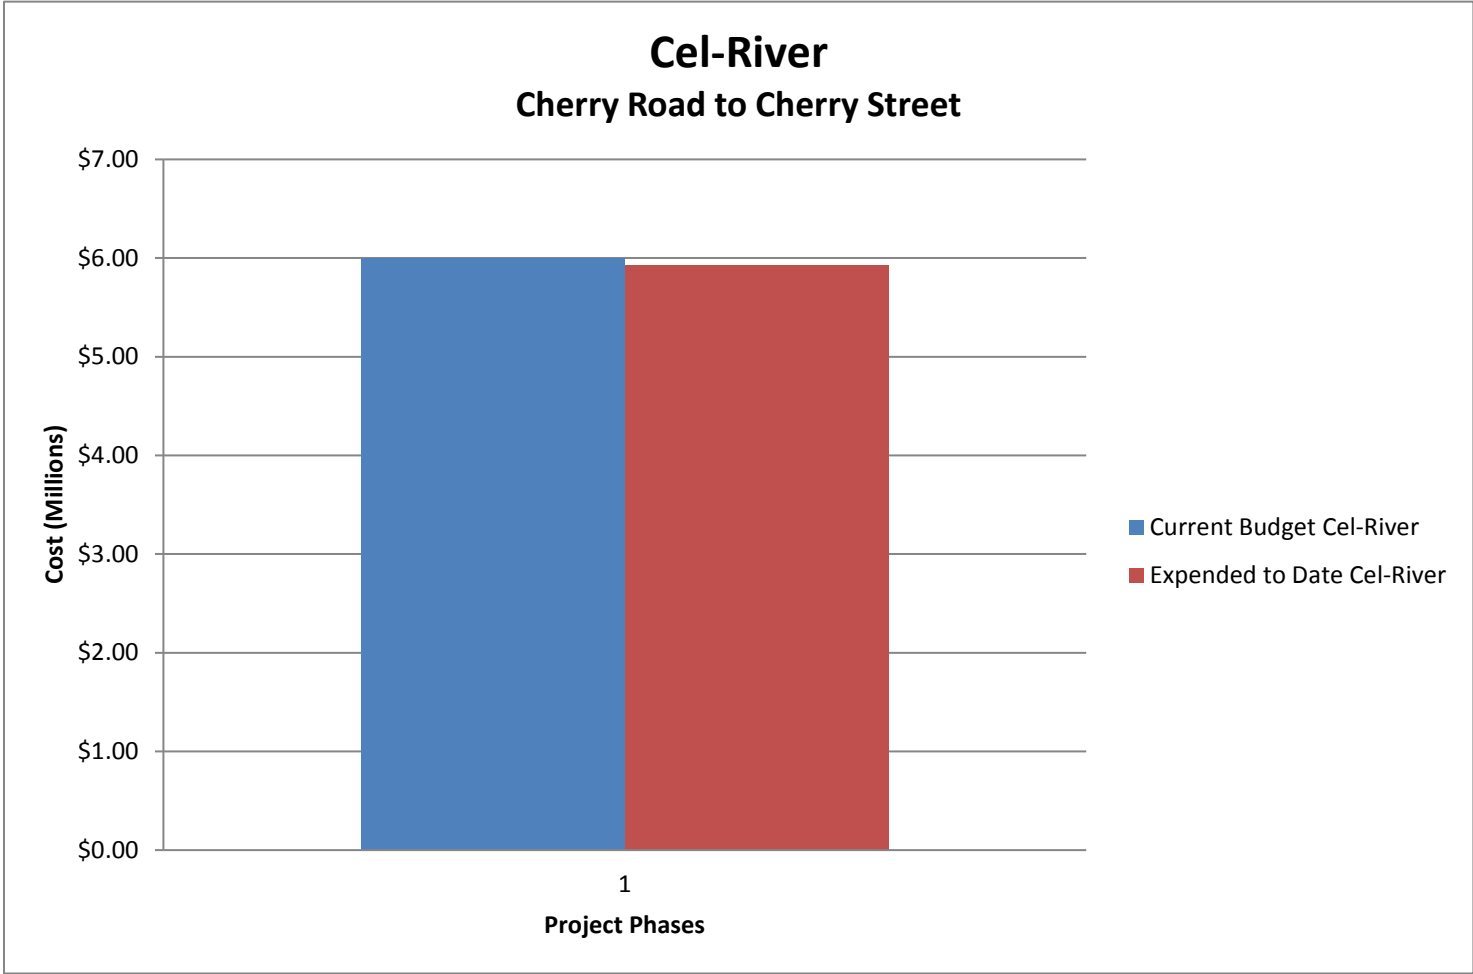


Project Status: Complete
Expenses are updated through: December 31, 2020

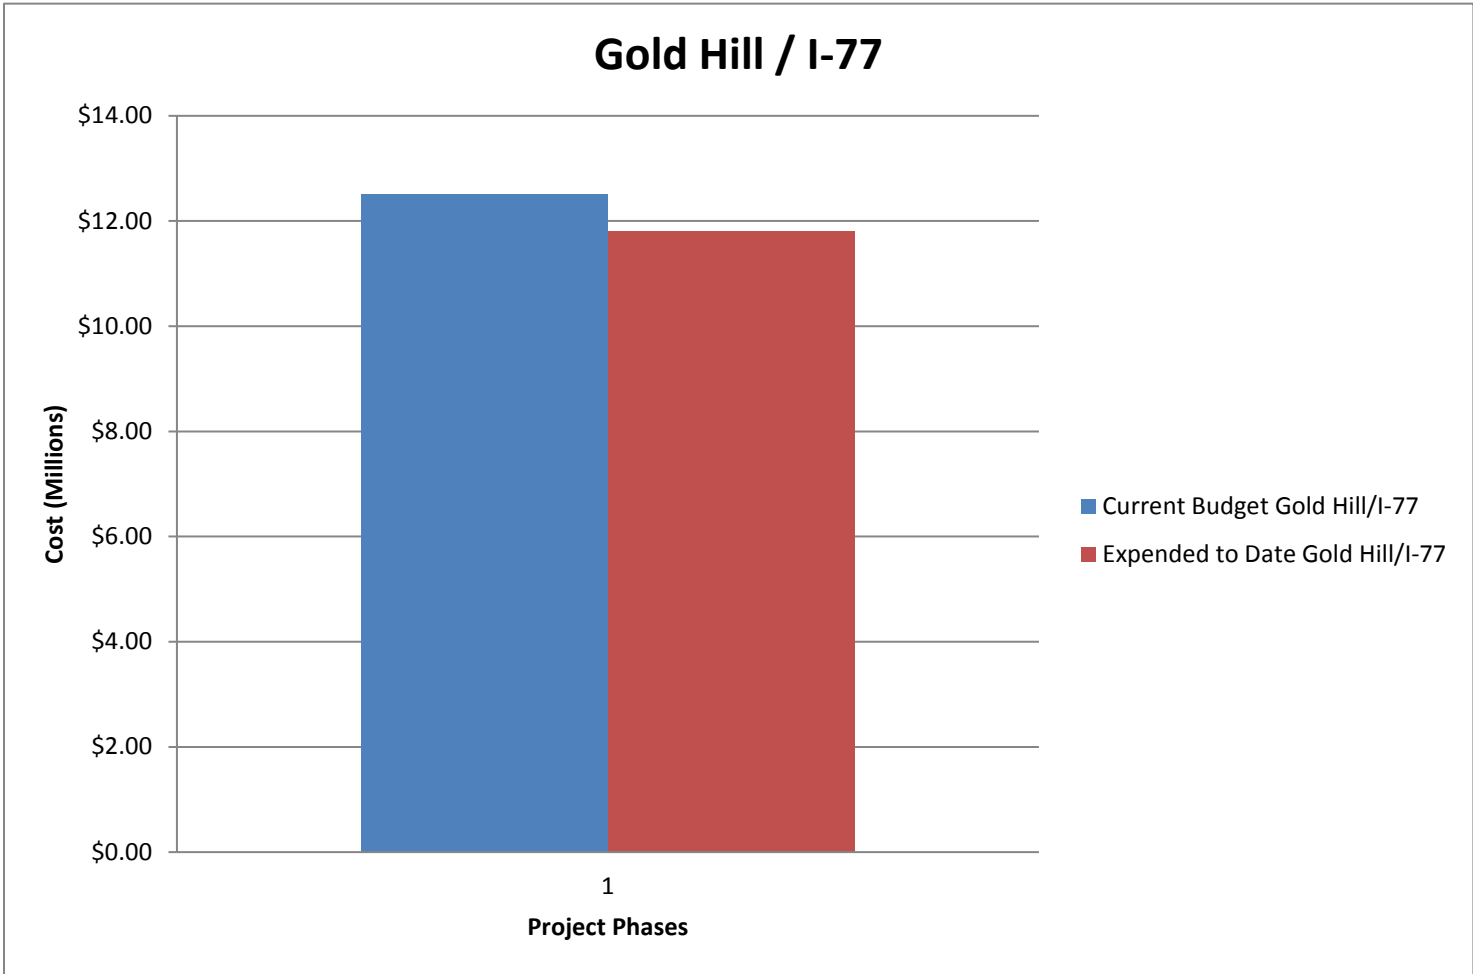

Project Status: Under construction
Expenses are updated through: December 31, 2020

* Managed by SCDOT. Funds have already been submitted to SCDOT.

Anderson / Cowan Farm

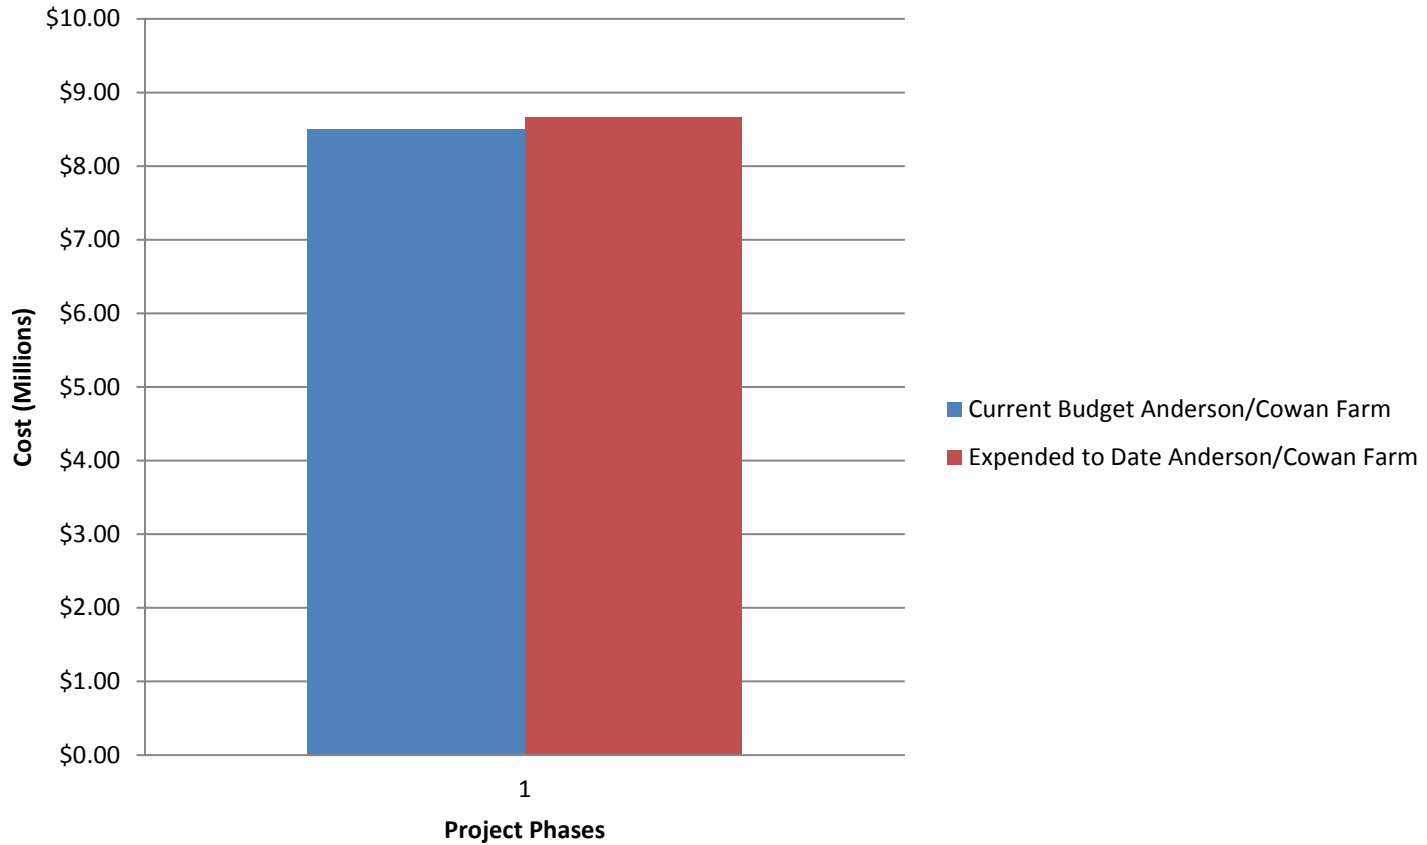


Project Status: Complete

Expenses are updated through: December 31, 2020

* Managed by SCDOT. Funds have already been submitted to SCDOT.

* Will receive a reimbursement of remaining funds from SCDOT when project is completed.


SC 49 / Lincoln

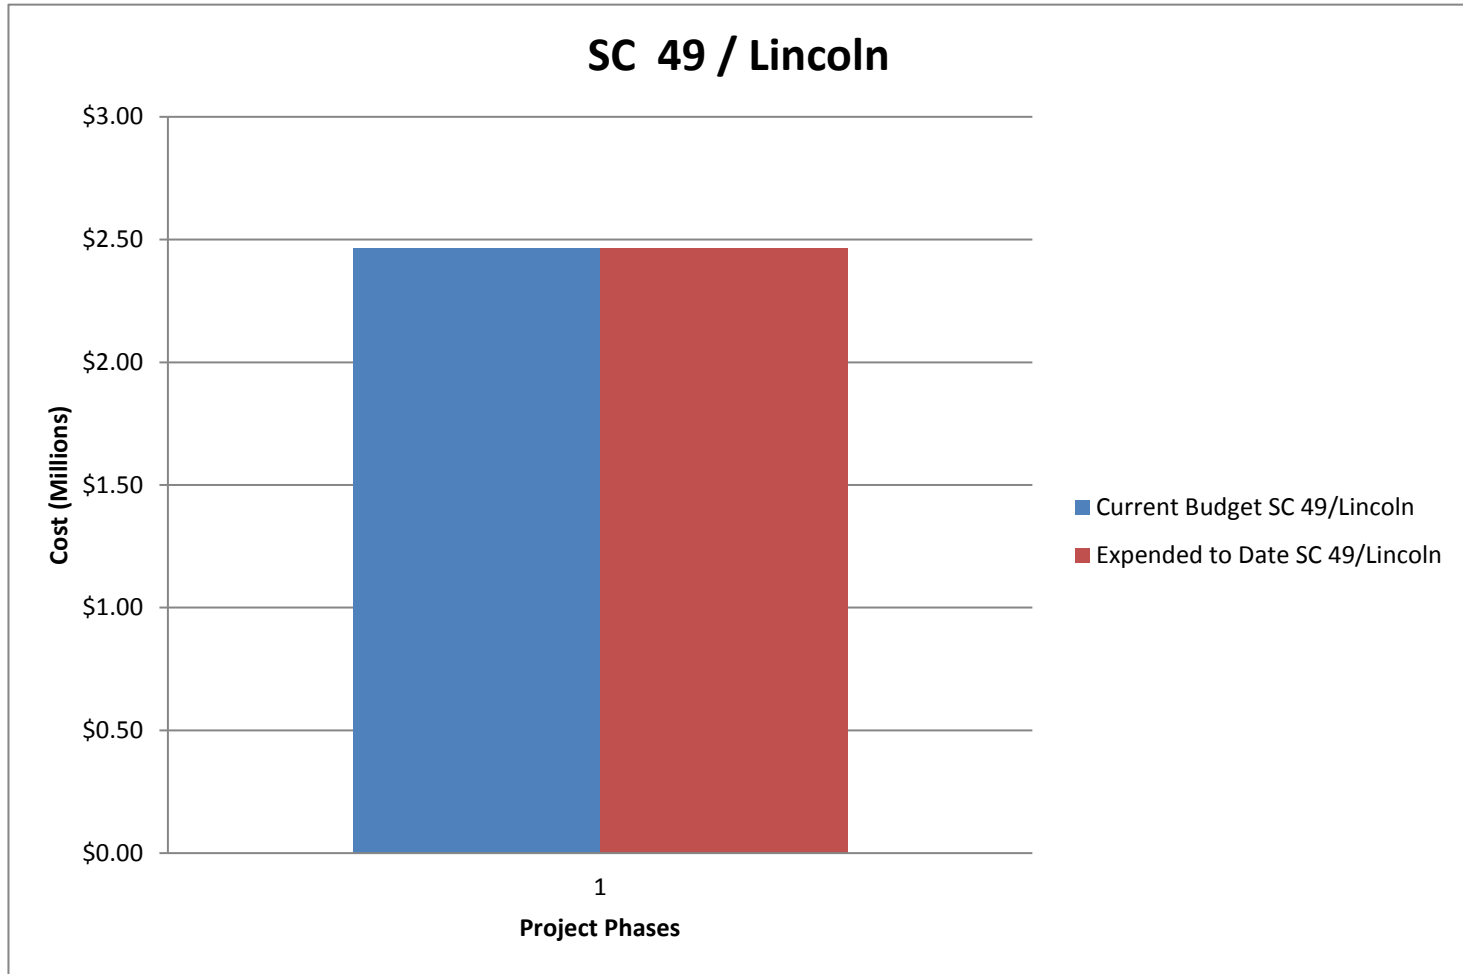

Project Status: Complete


Expenses are updated through: December 31, 2020

US 321 / Johnson / Railroad

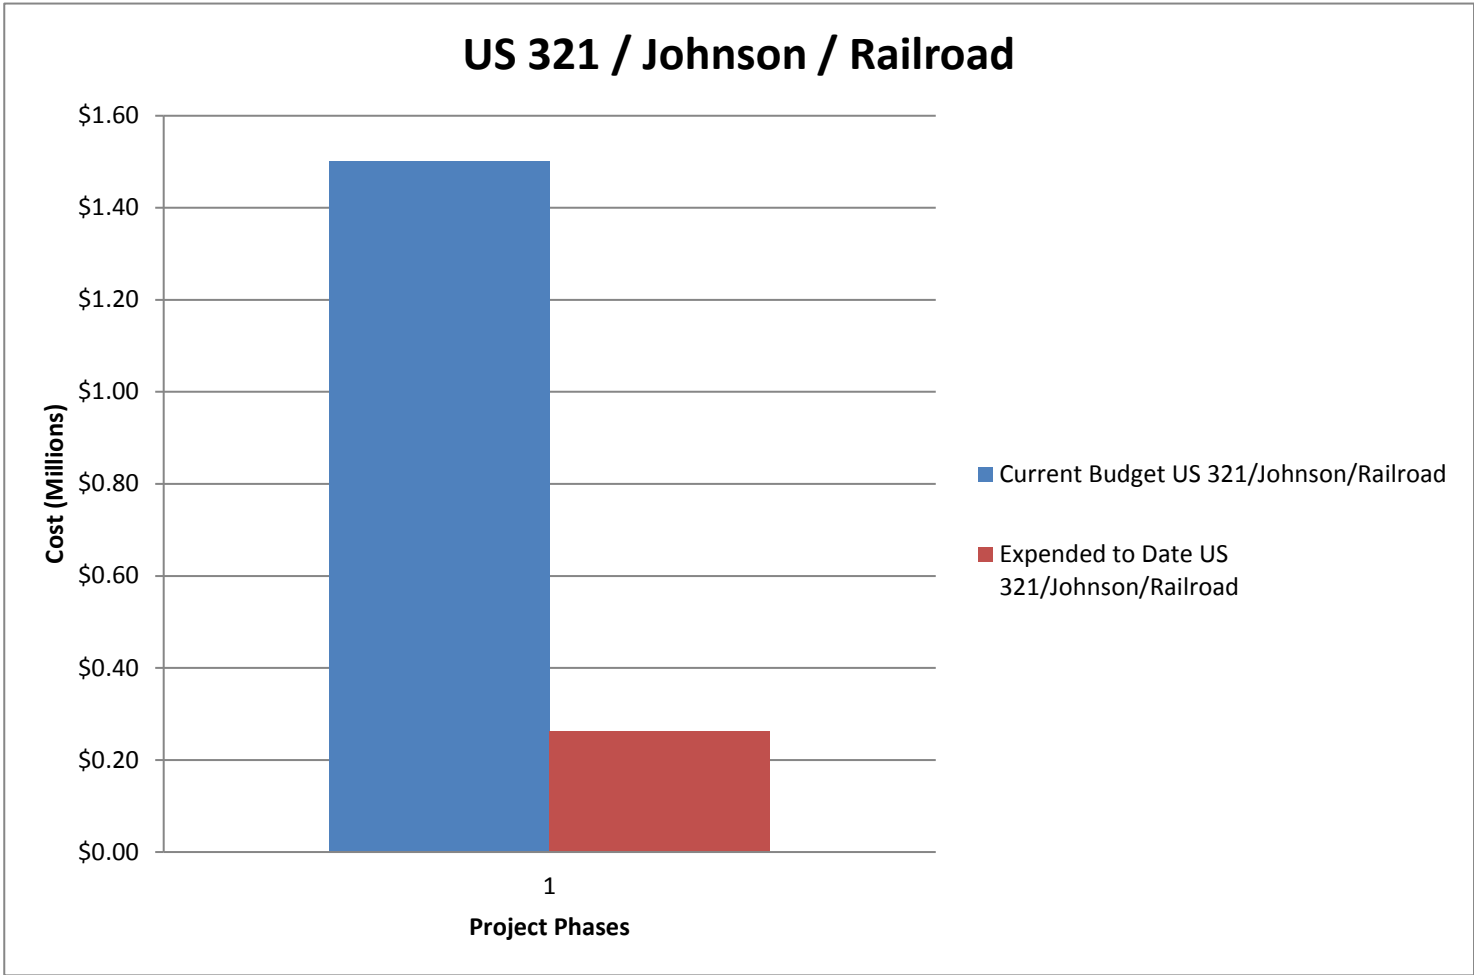

Project Status: Acquiring Right-of-Way/Final Plans
Expenses are updated through: December 31, 2020


SC 49 / Campbell

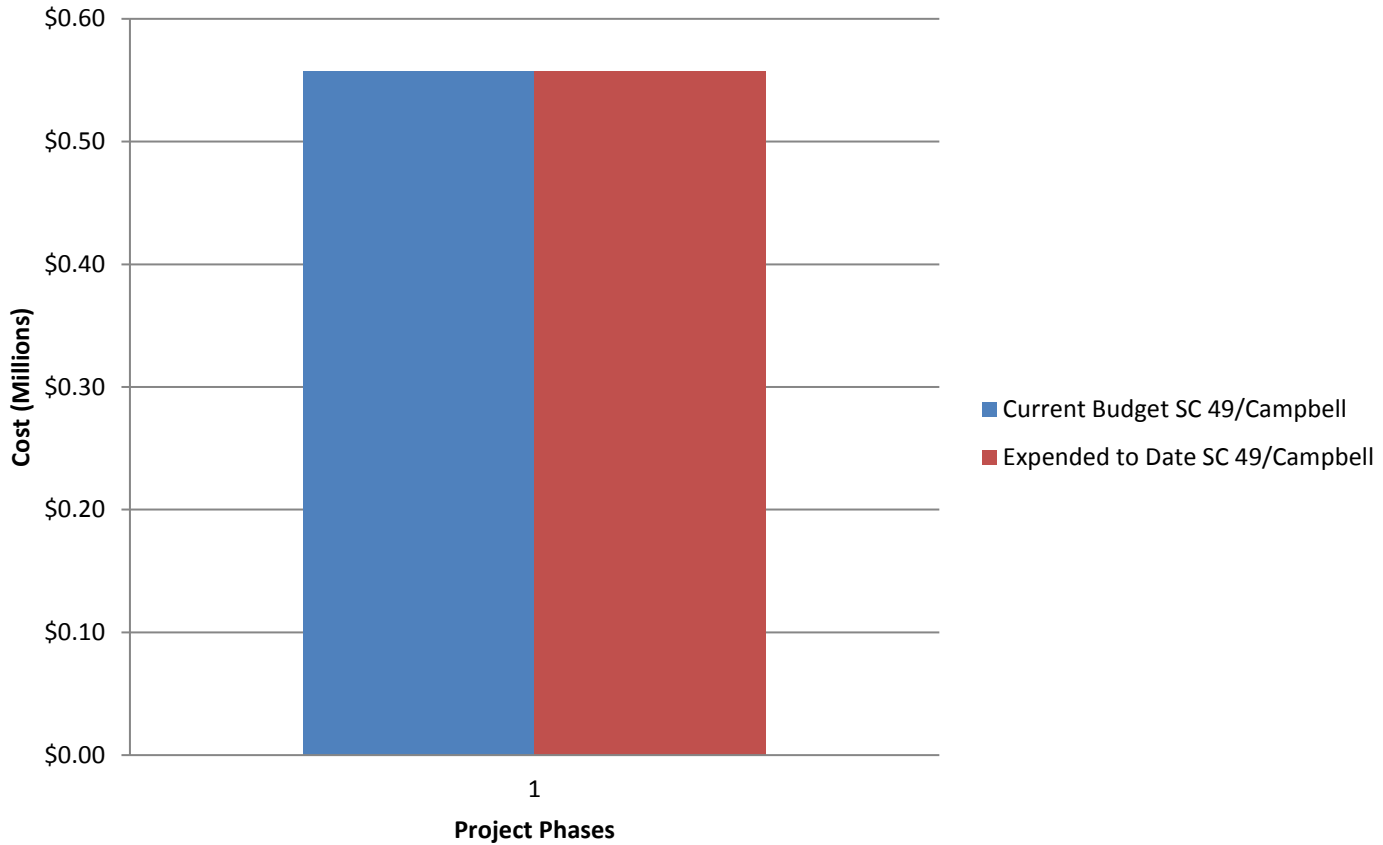

Project Status: Complete

Expenses are updated through:


December 31, 2020

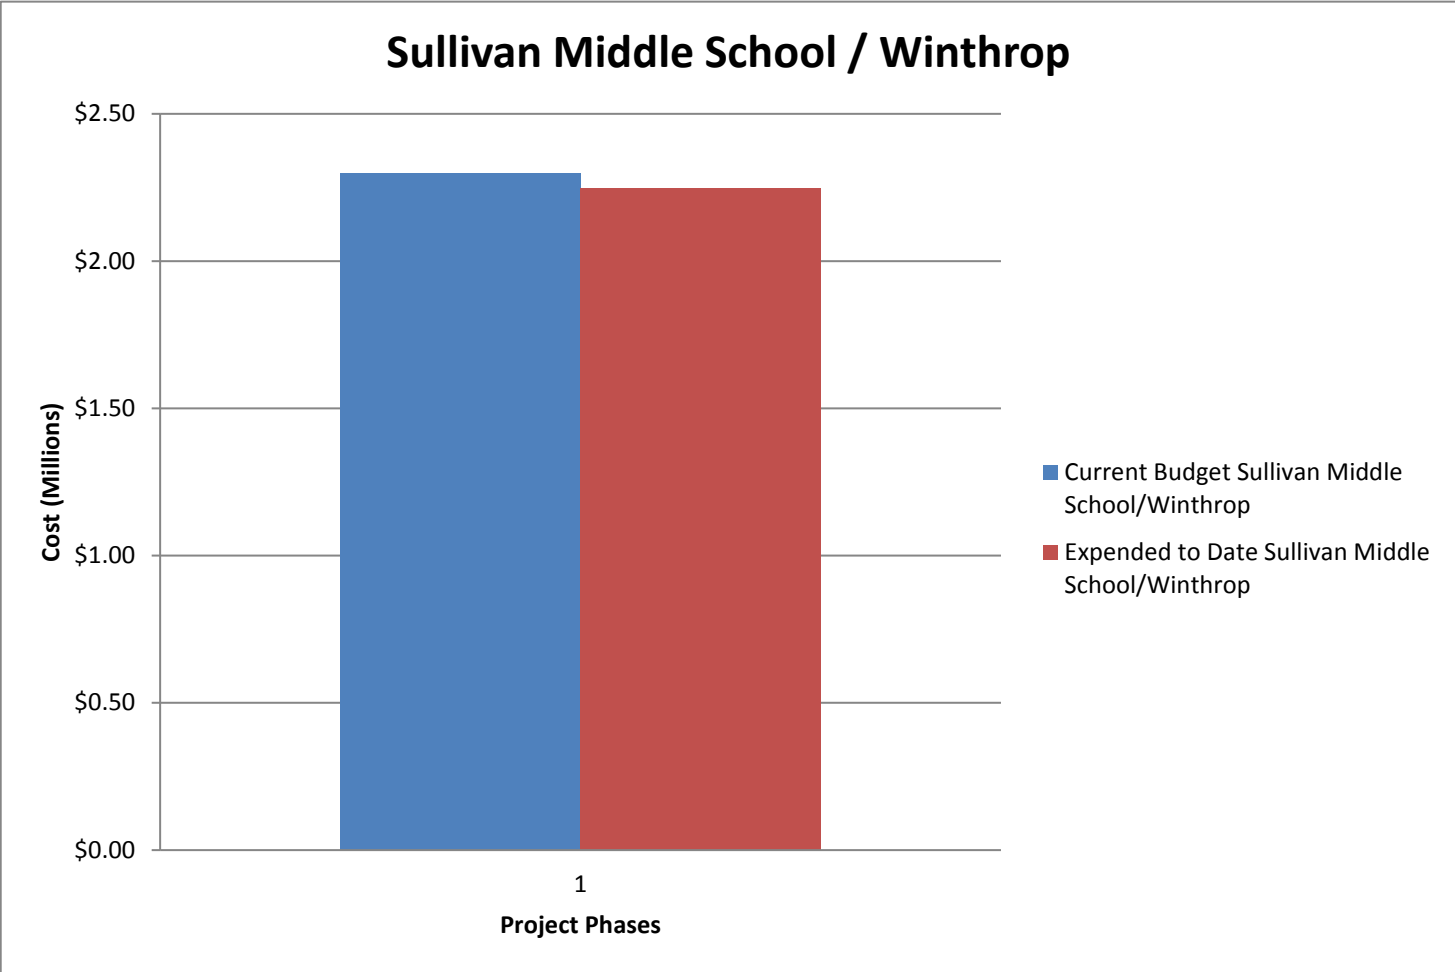

Project Status: Complete
Expenses are updated through: December 31, 2020

* Managed by SCDOT. Funds have already been submitted to SCDOT.


SC 557 / Griggs / Bate Harvey

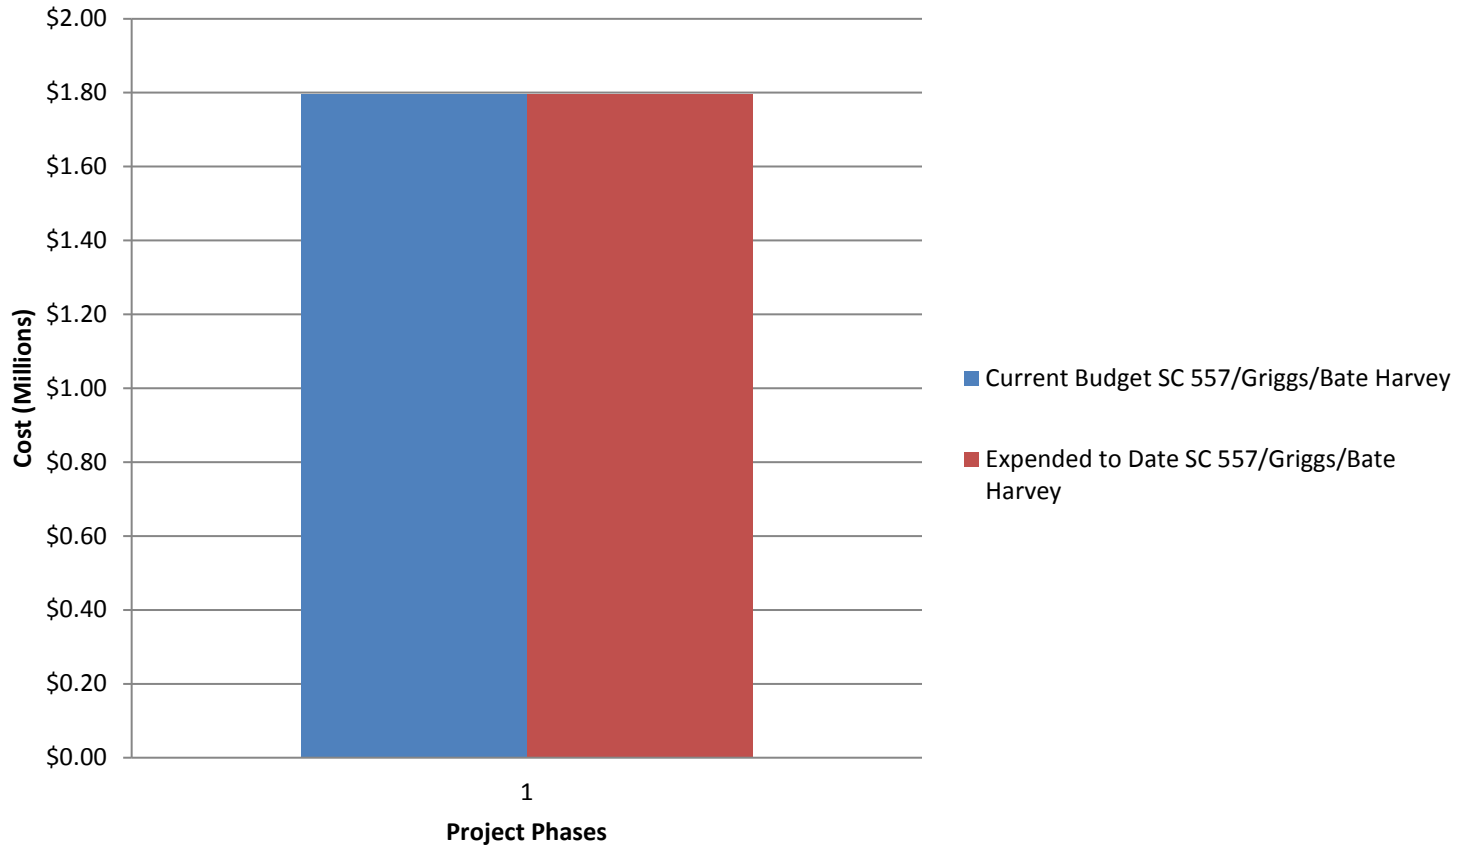

Project Status: Complete

Expenses are updated through: December 31, 2020


4th / 5th / Ross Cannon

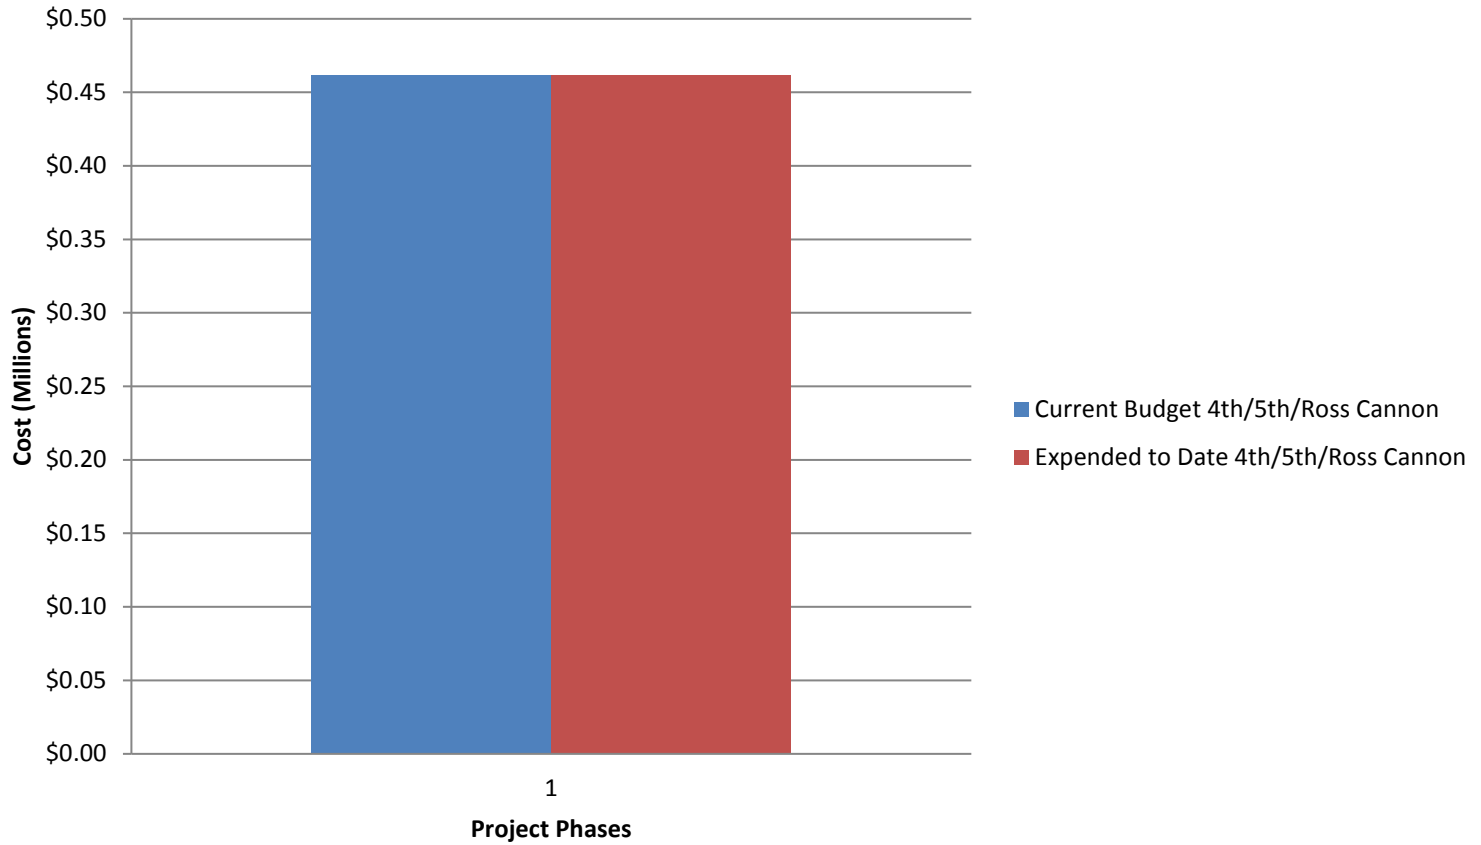

Project Status: Complete


Expenses are updated through: December 31, 2020

White / Constitution

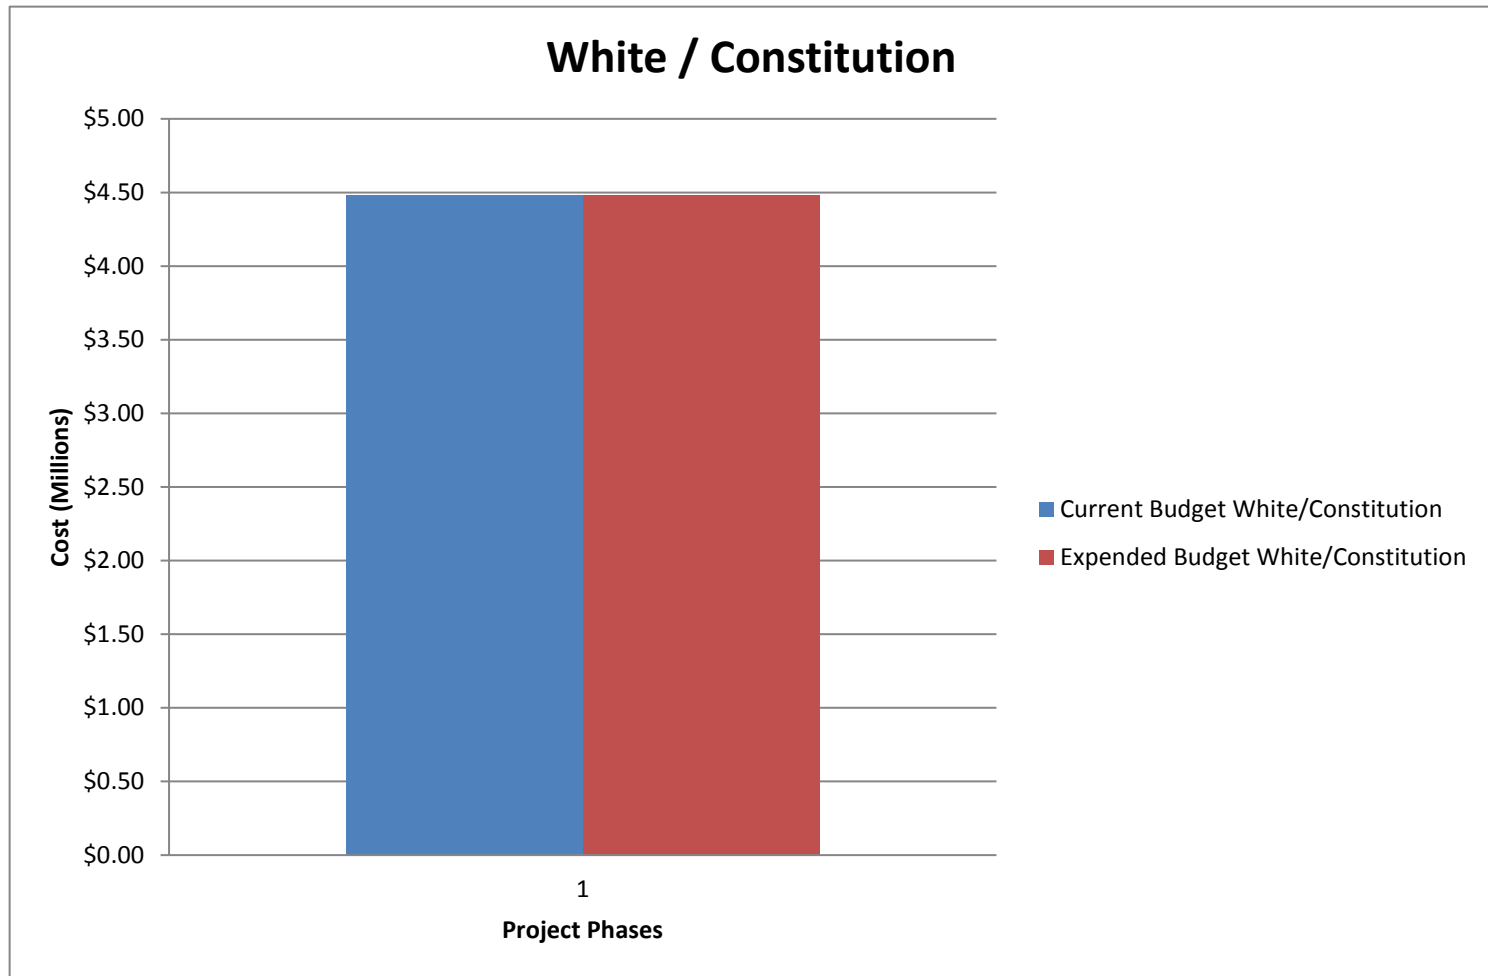

Project Status: Complete


Expenses are updated through: December 31, 2020

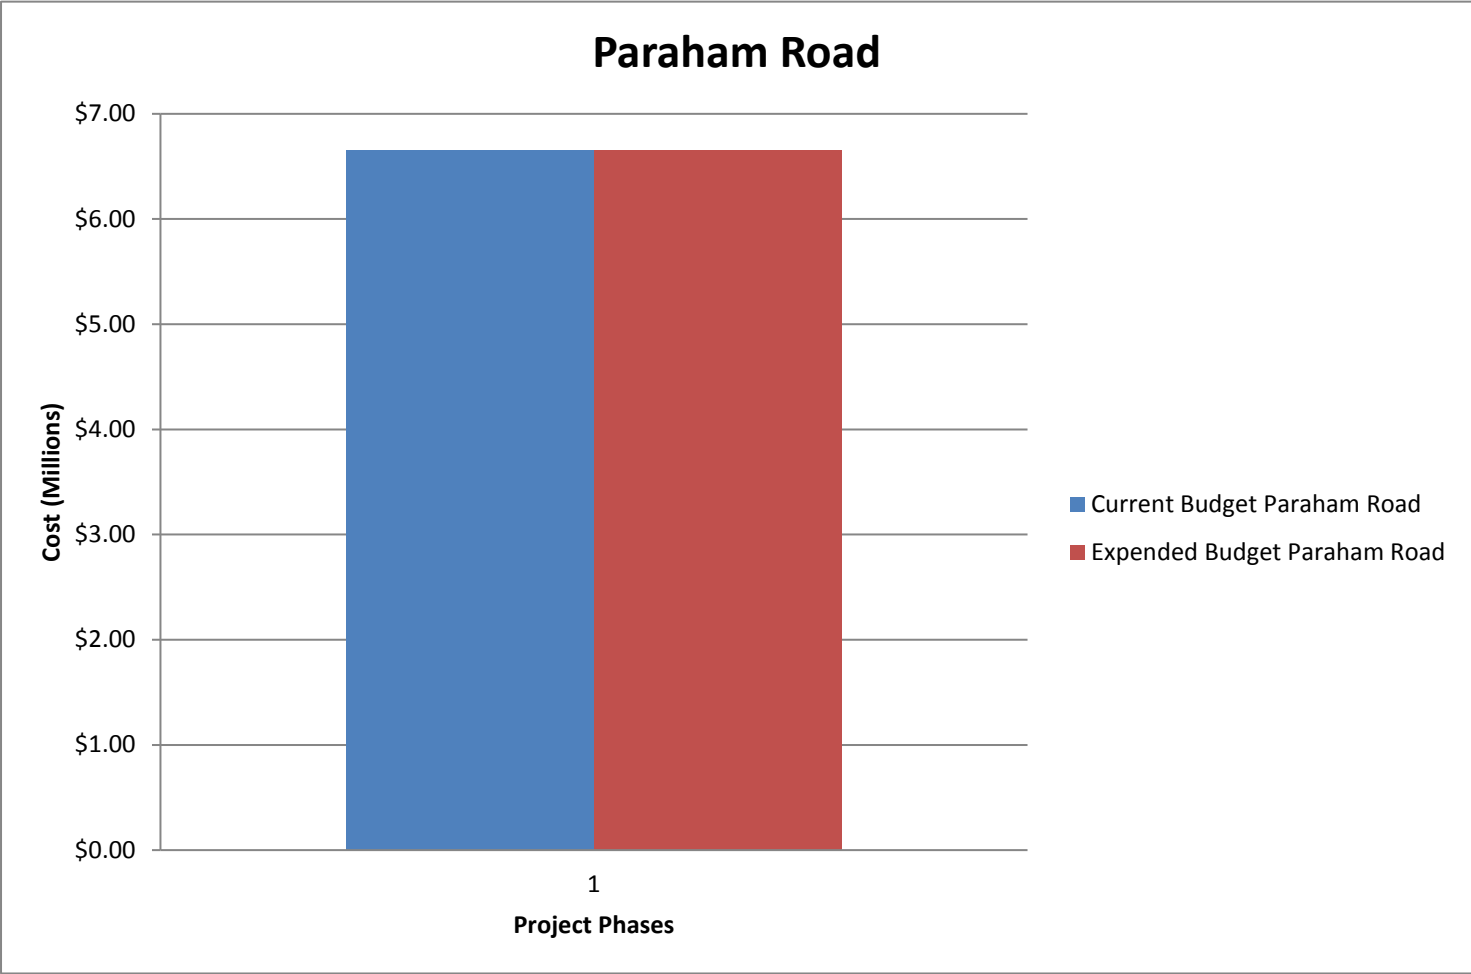

Project Status: Complete


Expenses are updated through: December 31, 2020

FMSB / Spratt

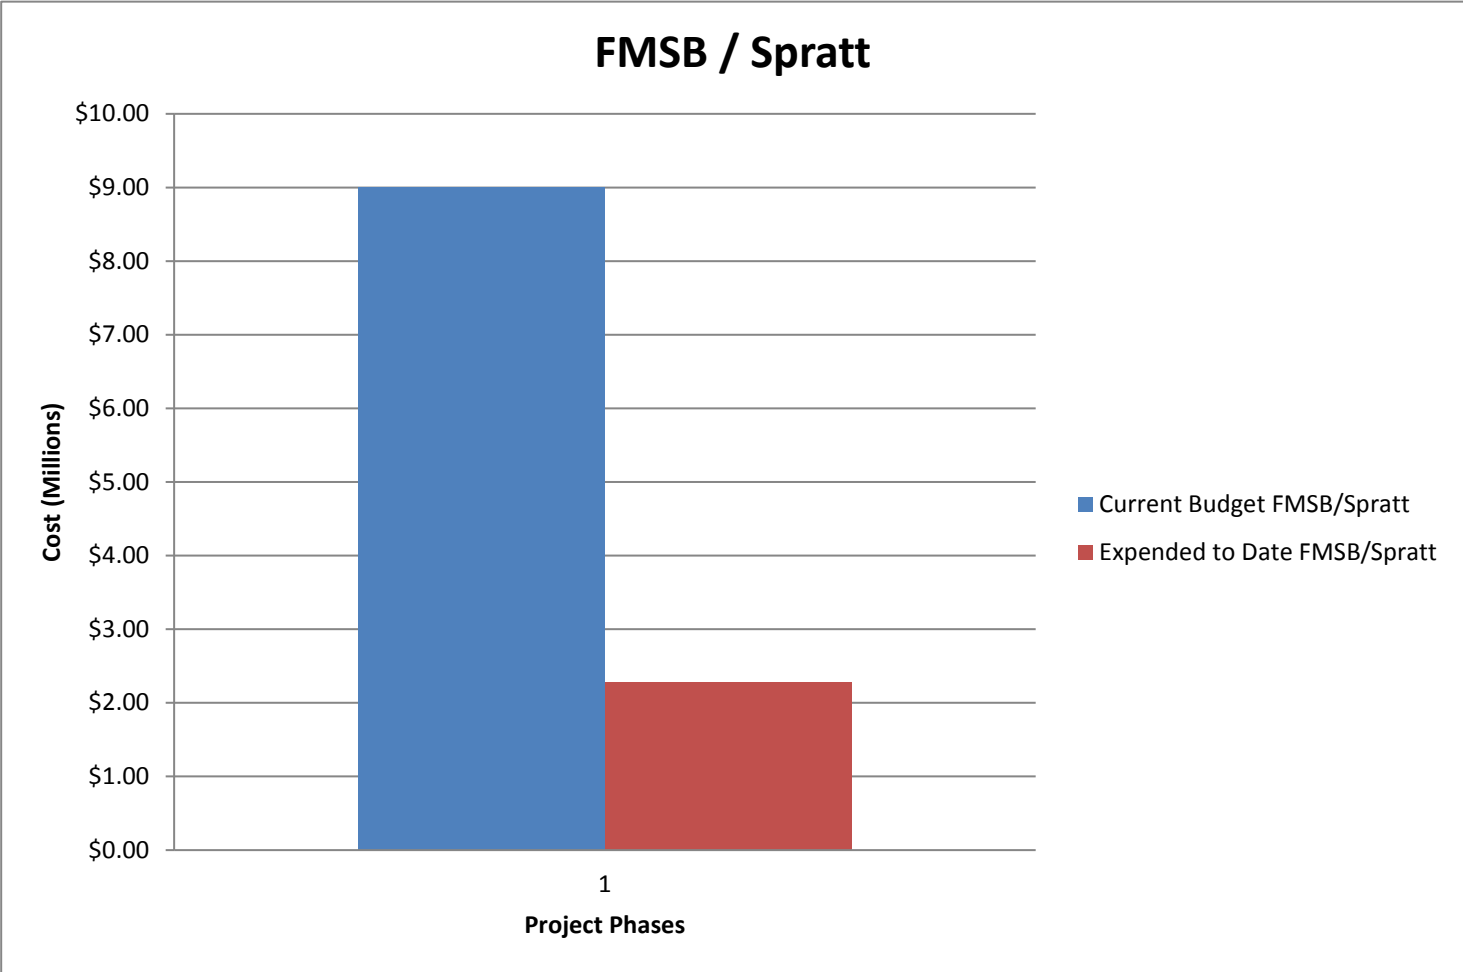


Project Status: Bid Phase
Expenses are updated through: December 31, 2020


University Drive

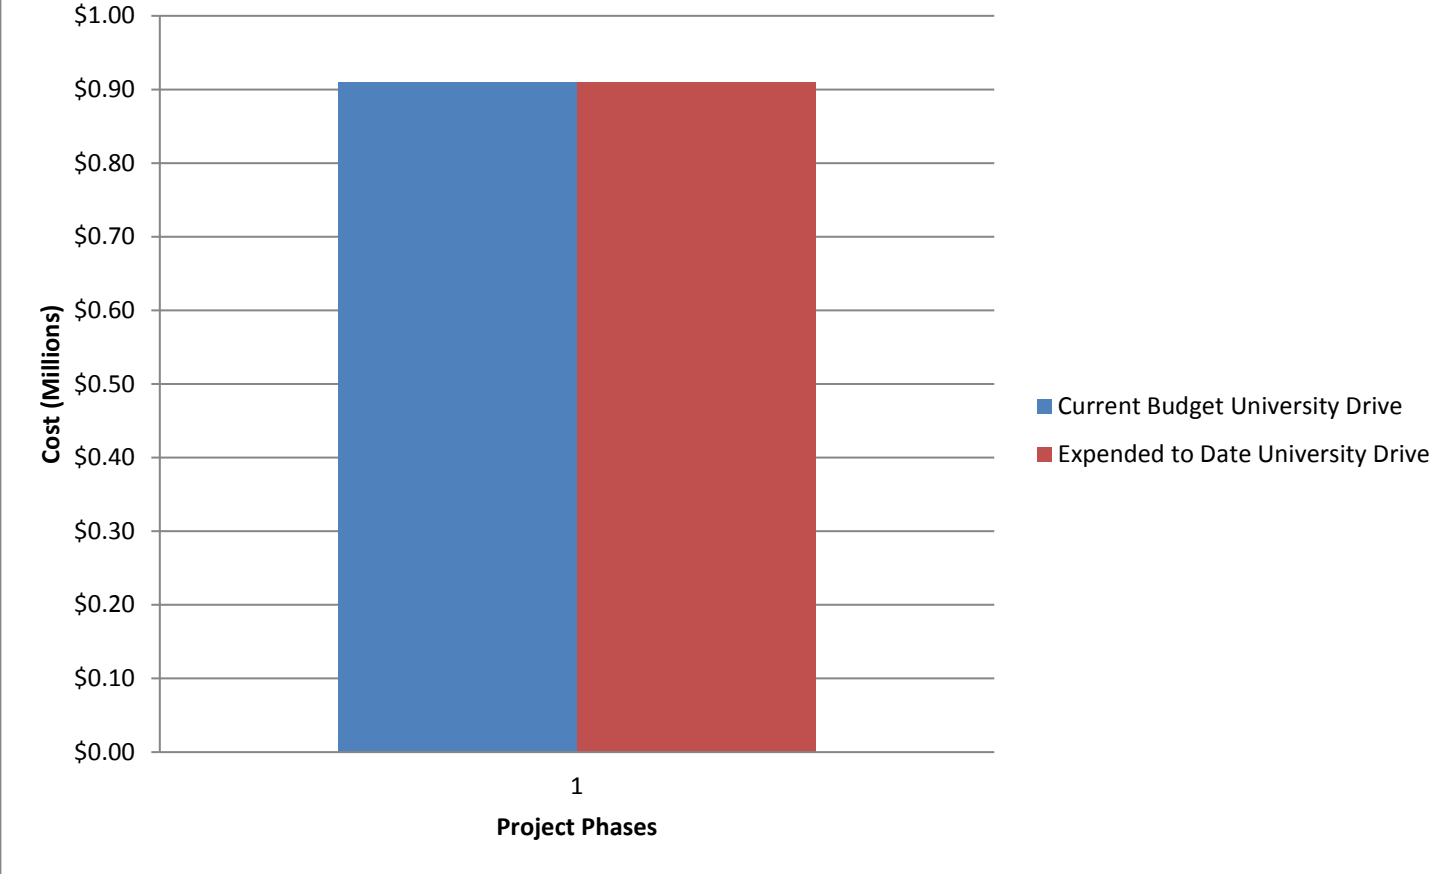

Project Status: Complete
Expenses are updated through: December 31, 2020

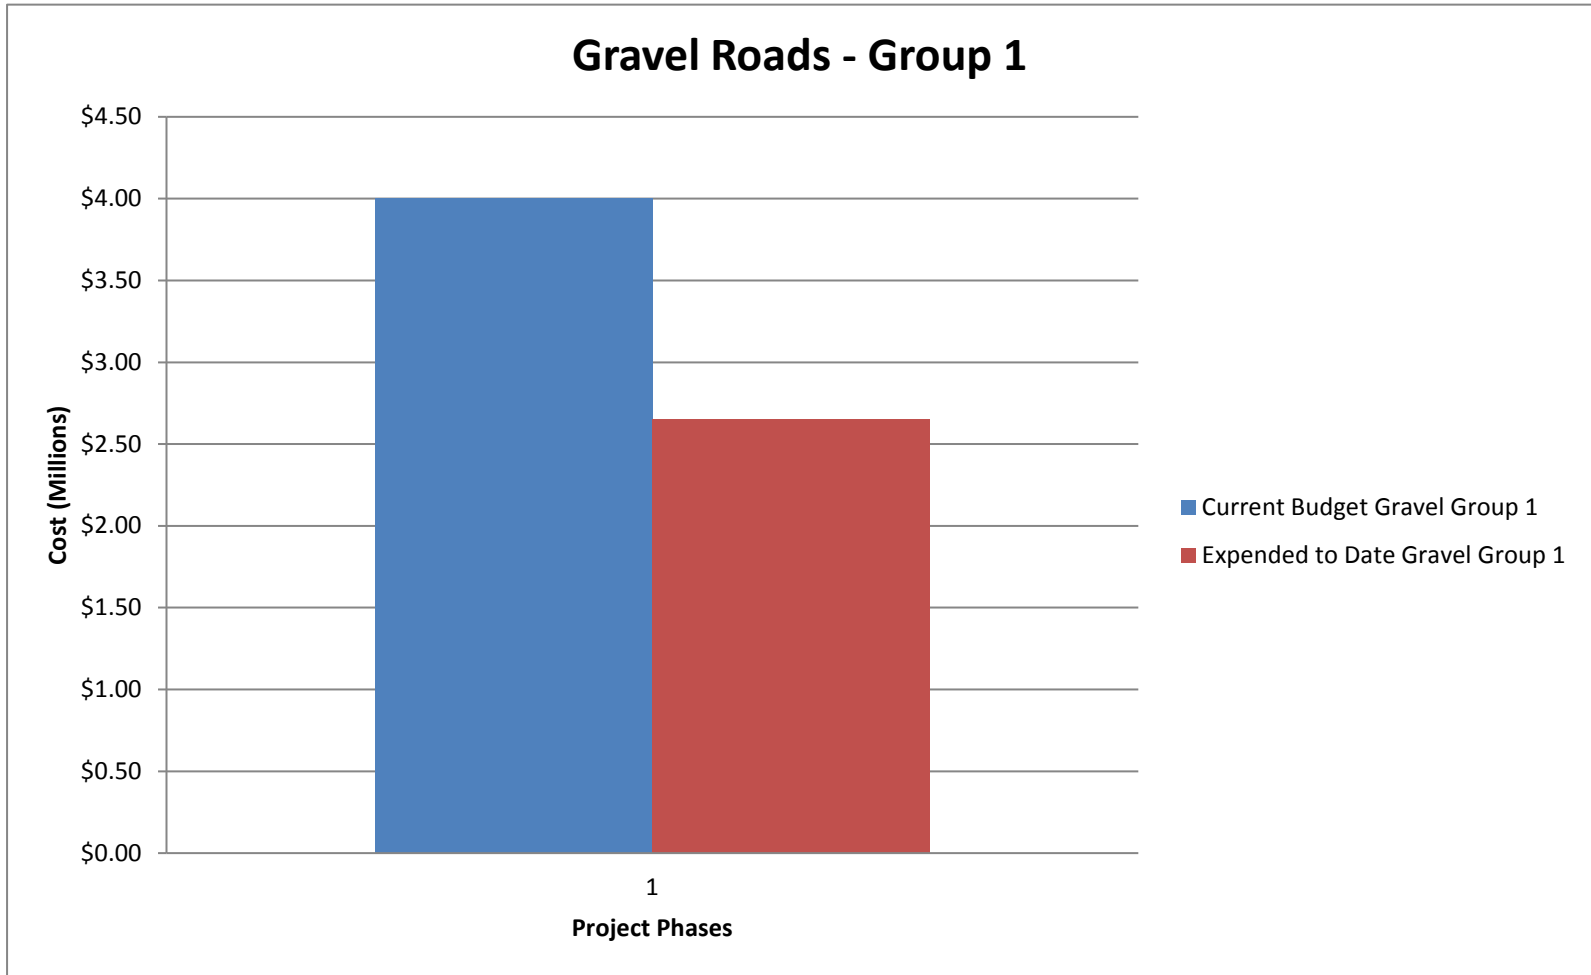

Project Status: Ongoing
Expenses are updated through: December 31, 2020

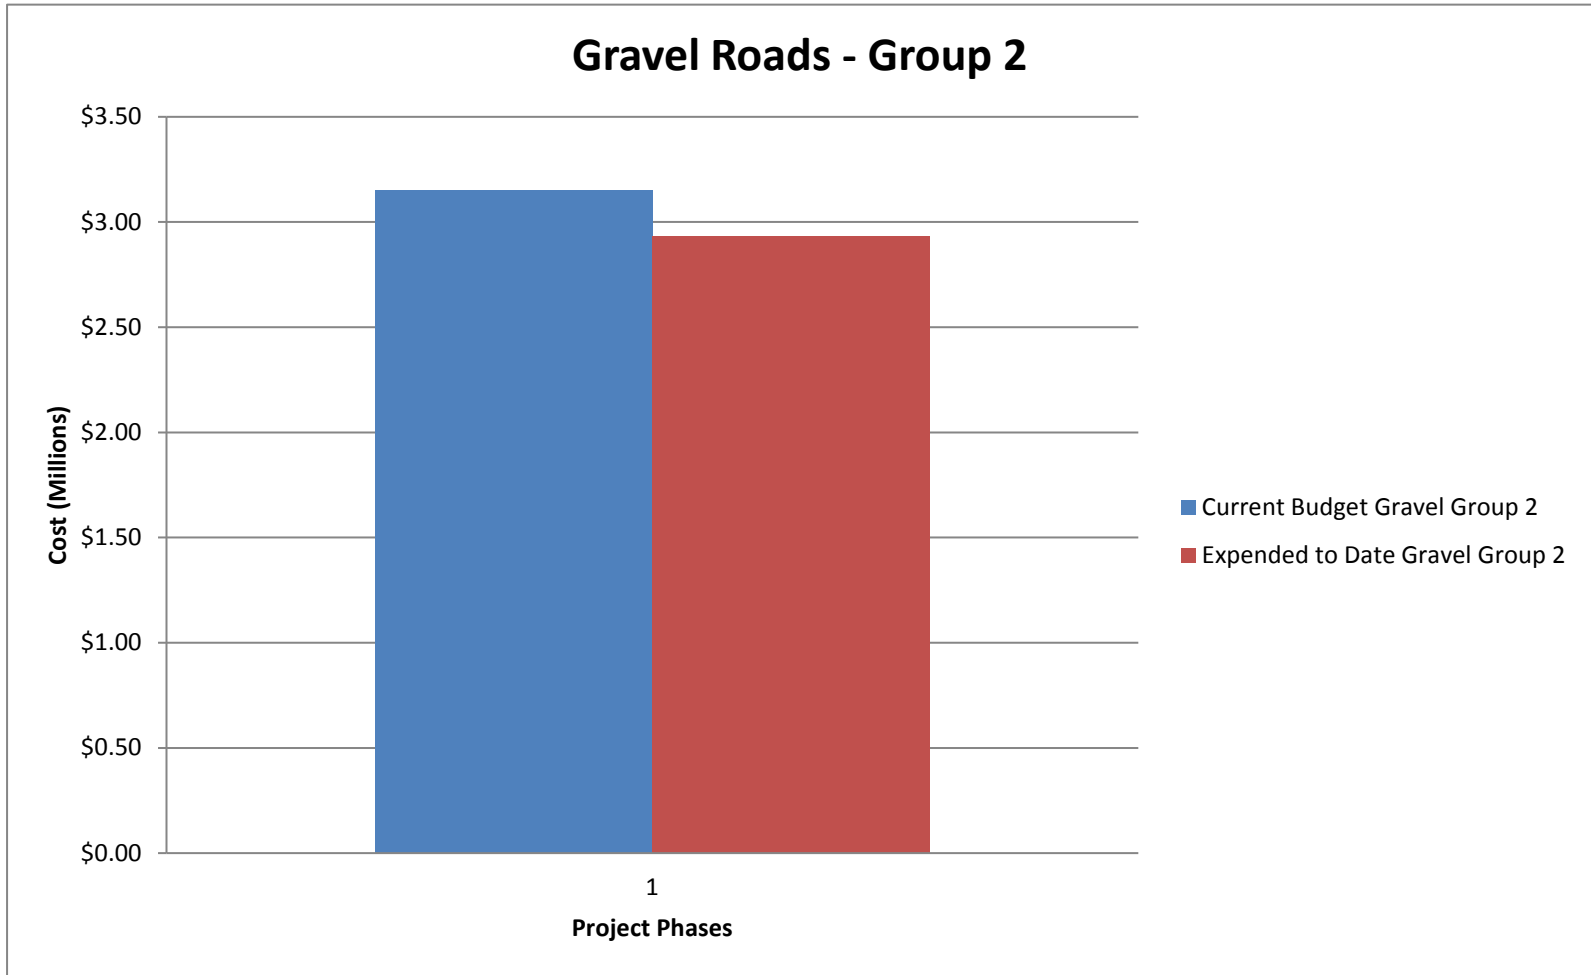

Project Status: Ongoing
Expenses are updated through: December 31, 2020




Pennies for Progress

Pennies 4

Prepared for Council Meeting on
February 15, 2021


Pennies 4 Projects

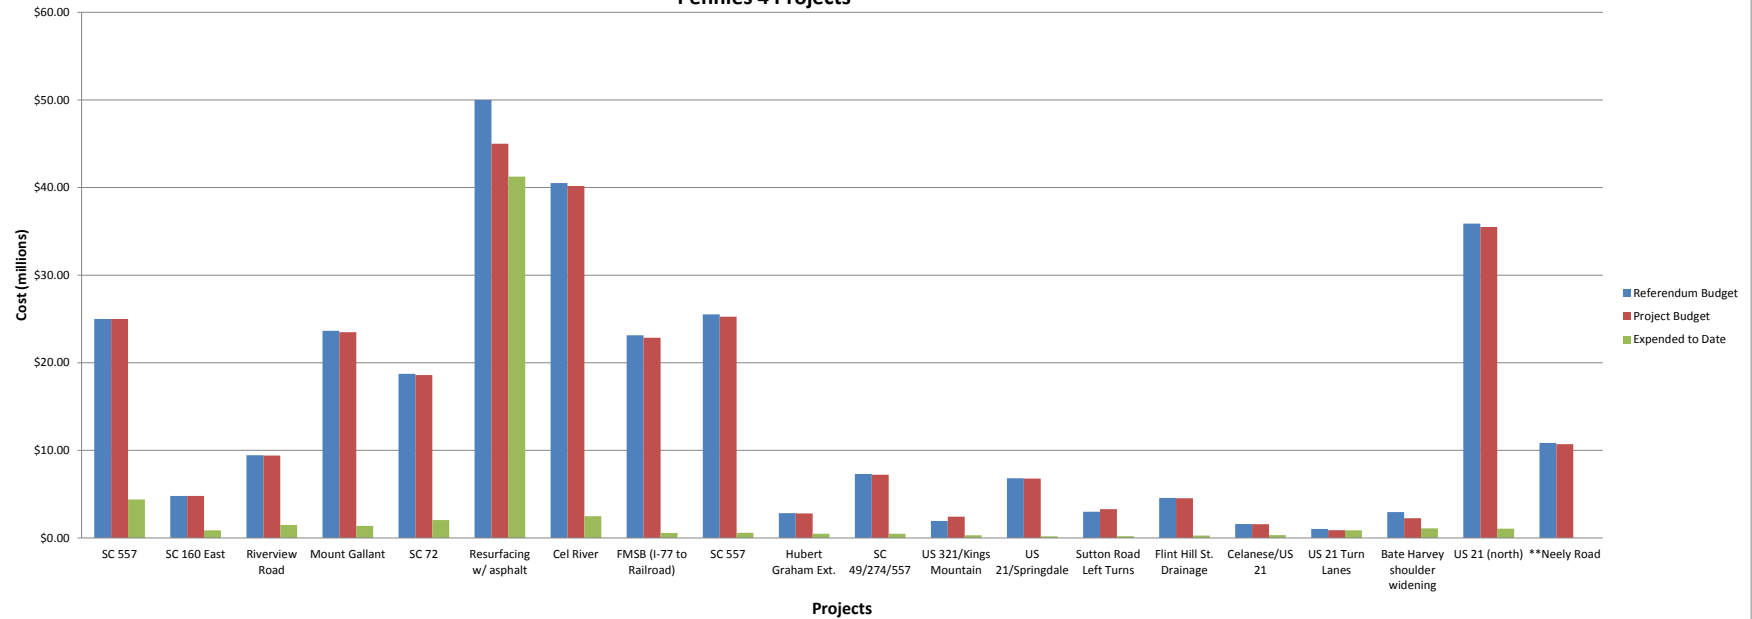


Project	Referendum Budget	Program Management	Project Budget	Expended to Date	Status
SC 557	\$25.00	\$0.00	\$25.00	\$4.40	Final Plans
SC 160 East	\$4.80	\$0.00	\$4.80	\$0.87	Final Plans
Riverview Road	\$9.45	\$0.05	\$9.40	\$1.49	Acquiring Right-of-Way
Mount Gallant	\$23.65	\$0.16	\$23.49	\$1.37	70% plans
SC 72	\$18.74	\$0.14	\$18.60	\$2.04	Acquiring Right-of-Way
Resurfacing w/ asphalt	\$50.00	\$0.00	\$45.00	\$41.24	Ongoing
Cel River	\$40.51	\$0.34	\$40.17	\$2.48	70% plans
FMSB (I-77 to Railroad)	\$23.13	\$0.27	\$22.86	\$0.58	30% plans
SC 557	\$25.52	\$0.26	\$25.26	\$0.59	30% plans
Hubert Graham Ext.	\$2.83	\$0.04	\$2.79	\$0.49	Acquiring Right-of-Way
SC 49/274/557	\$7.30	\$0.08	\$7.22	\$0.48	70% plans
US 321/Kings Mountain	\$1.94	\$0.02	\$2.43	\$0.31	Bid Phase
US 21/Springdale	\$6.82	\$0.04	\$6.78	\$0.18	30% plans
Sutton Road Left Turns	\$3.00	\$0.05	\$3.29	\$0.20	70% plans
Flint Hill St. Drainage	\$4.57	\$0.03	\$4.54	\$0.27	Working towards 70% plans
Celanese/US 21	\$1.59	\$0.02	\$1.57	\$0.32	70% plans
US 21 Turn Lanes	\$1.03	\$0.01	\$0.88	\$0.87	Complete
Bate Harvey shoulder widening	\$2.95	\$0.03	\$2.25	\$1.09	Project Closeout
US 21 (north)	\$35.88	\$0.38	\$35.50	\$1.07	30% plans
**Neely Road	\$10.85	\$0.14	\$10.71	\$0.00	On hold

Project budget is Referendum budget subtracting the Program Management allocation

Pennies 4

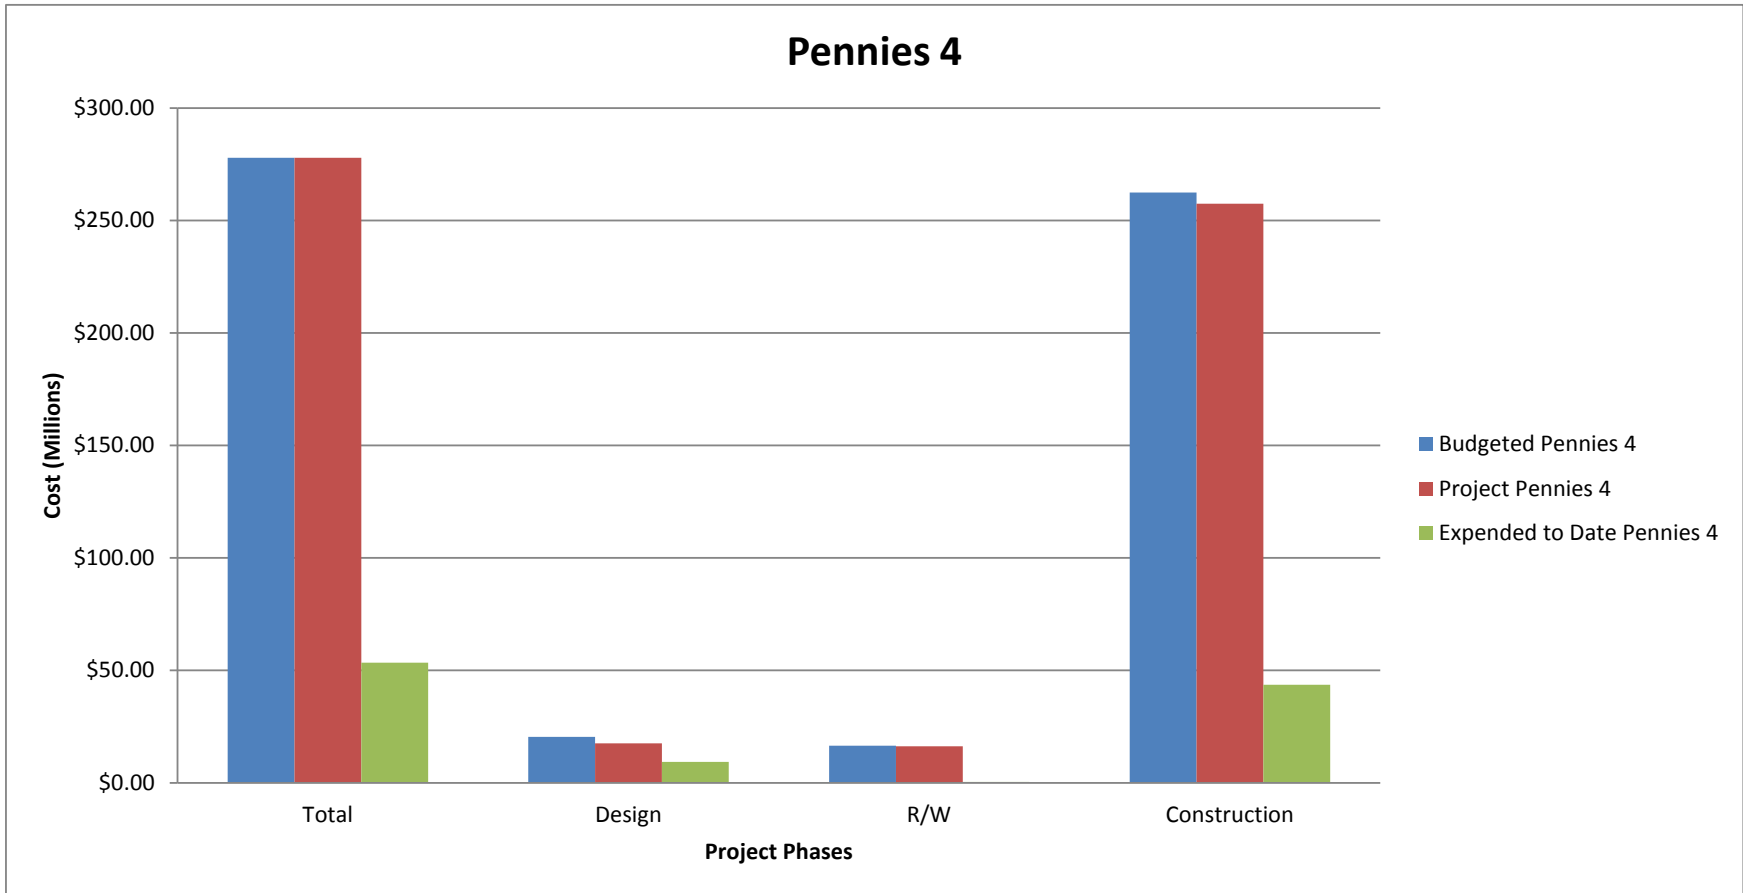

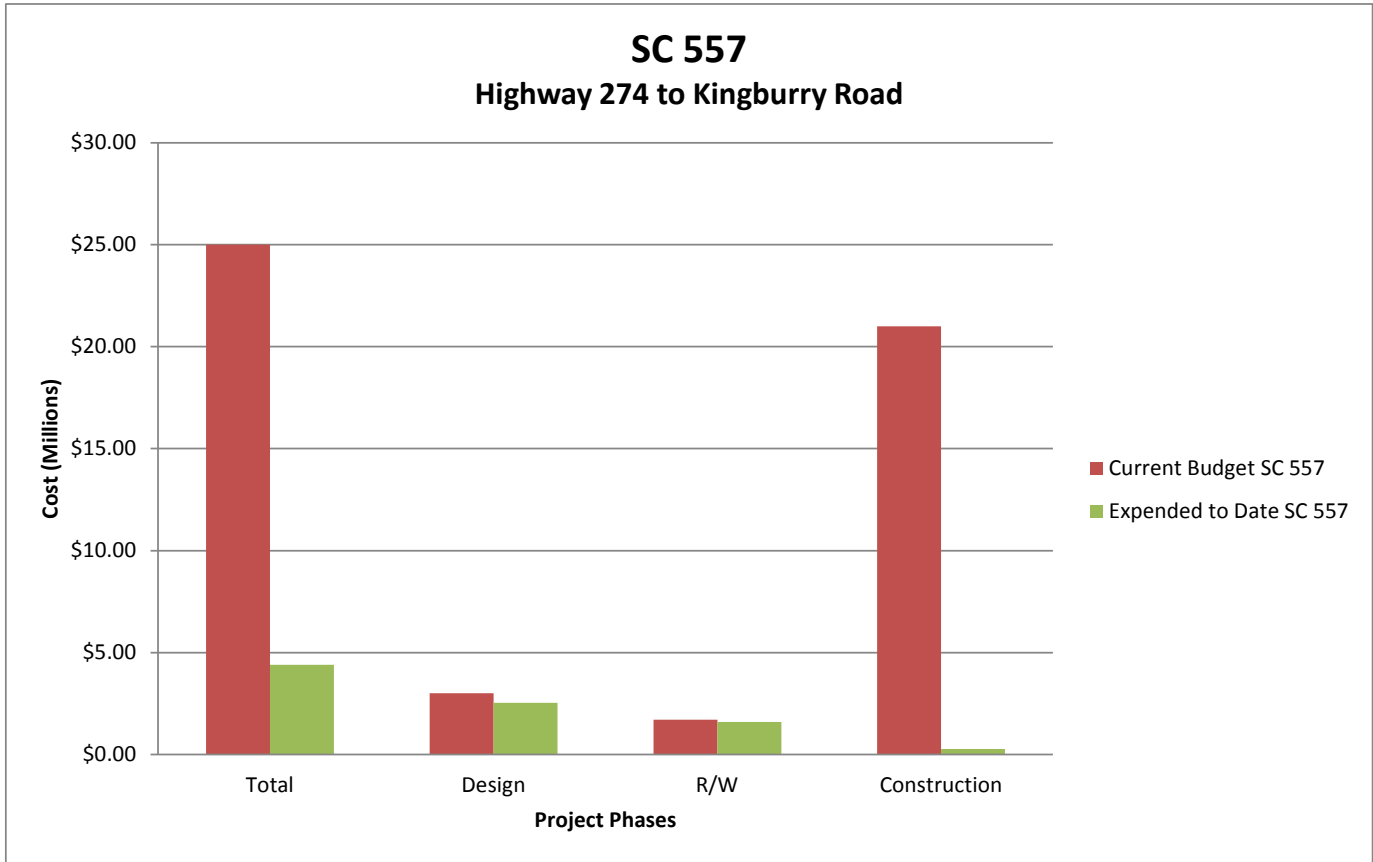


Project Status: Final Plans
 Expenses are updated through: December 31, 2020

	<u>Budget</u>	<u>Spent to Date</u>
Pennies 2	\$20.00	\$3.33
Pennies 3	\$1.50	\$1.07
Pennies 4	\$3.50	\$0.00
Total	\$25.00	\$4.40

* Staff Anticipates there will be additional funding available from other Pennies 2 projects, thus reducing the amount needed from Pennies 4 from \$8.0 million to \$3.5 million.


SC 160 East FMSB to Lancaster County Line

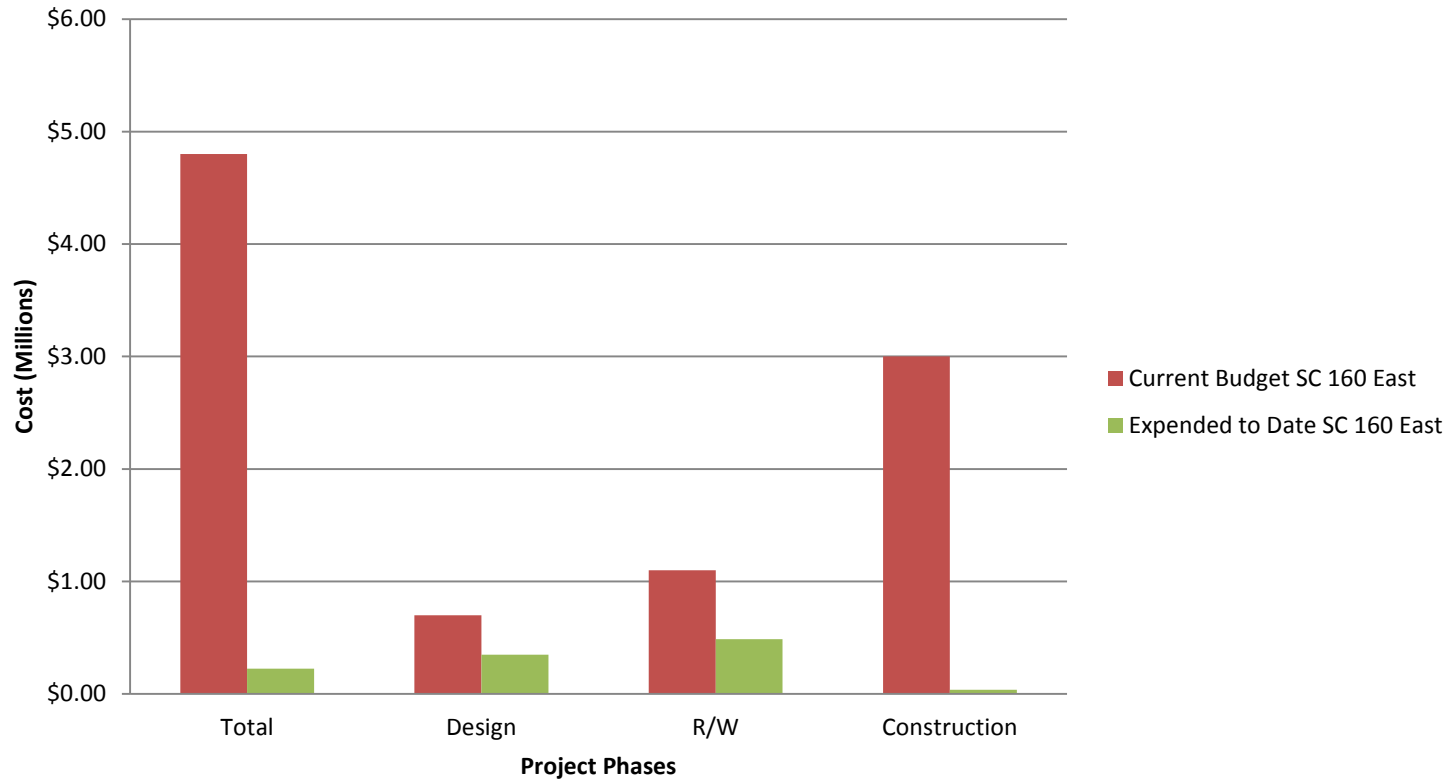

Project Status: Final Plans
 Expenses are updated through: December 31, 2020

	<u>Budget</u>	<u>Spent to Date</u>
Pennies 3	\$1.50	\$0.87
Pennies 4	\$3.30	\$0.00
Total	\$4.80	\$0.87


Riverview Road Celanese Road to Eden Terrace Road

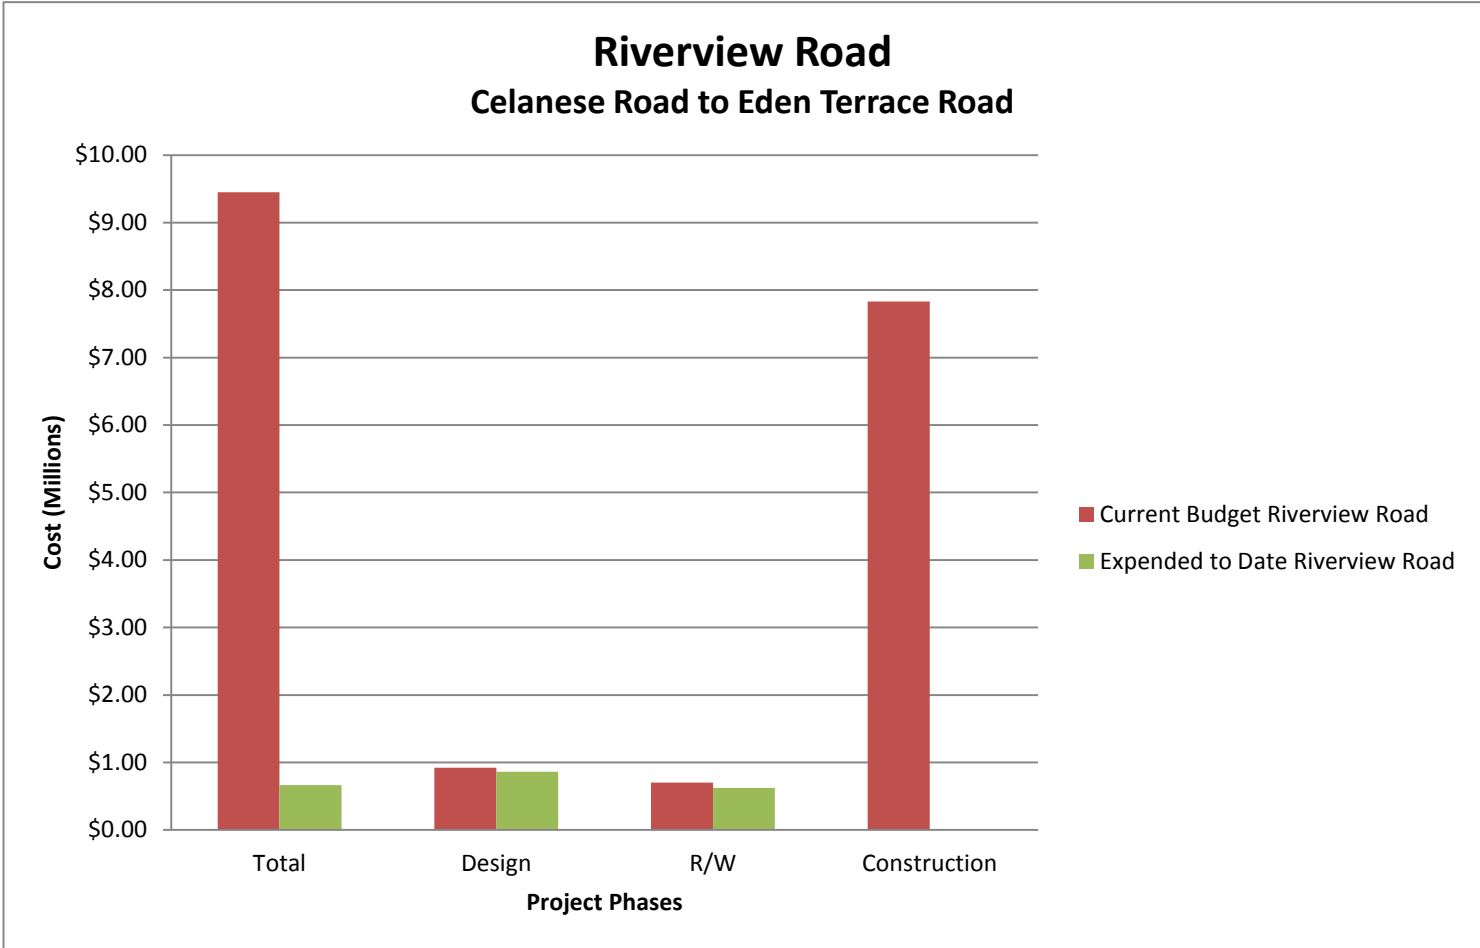

Project Status: Acquiring Right-of-Way
 Expenses are updated through: December 31, 2020

	<u>Budget</u>	<u>Spent to Date</u>
Pennies 3	\$3.49	\$1.49
Pennies 4	\$6.01	\$0.00
Total	\$9.50	\$1.49


Mt Gallant Celanese Road to Twin Lakes Road

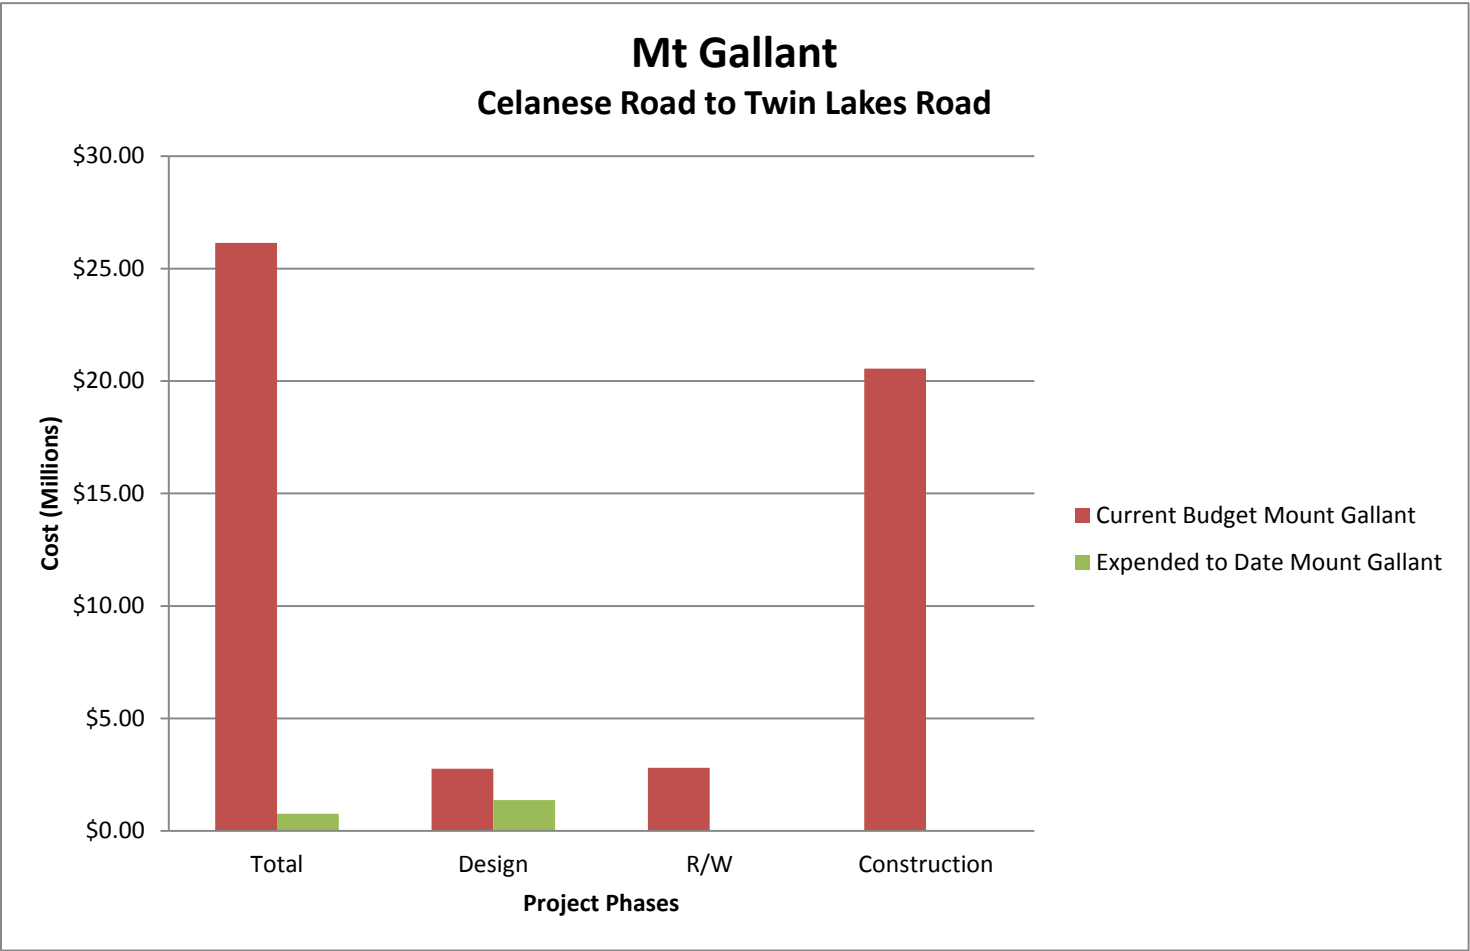

Project Status: 70% plans
 Expenses are updated through: December 31, 2020

	<u>Budget</u>	<u>Spent to Date</u>
Pennies 3	\$2.49	\$1.37
Pennies 4	\$23.81	\$0.00
Total	\$26.30	\$1.37


SC 72 Highway 901 to Rambo Road

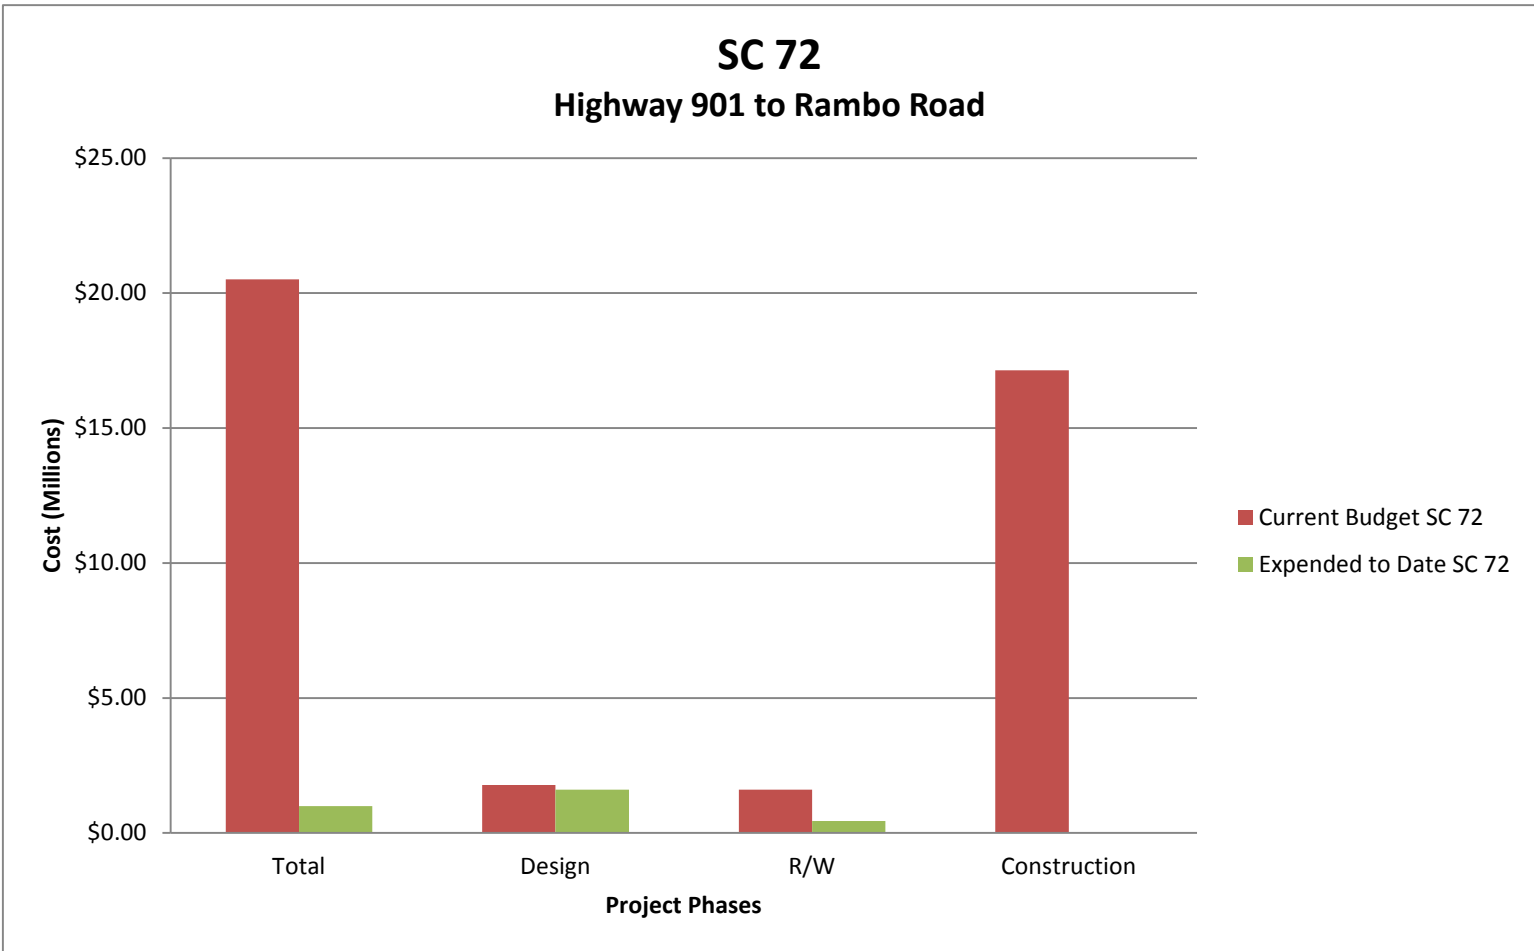

Project Status: Acquiring Right-of-Way
 Expenses are updated through: December 31, 2020

	<u>Budget</u>	<u>Spent to Date</u>
Pennies 3	\$1.77	\$1.60
Pennies 4	\$18.88	\$0.44
Total	\$20.65	\$2.04

Resurfacing w/ Asphalt

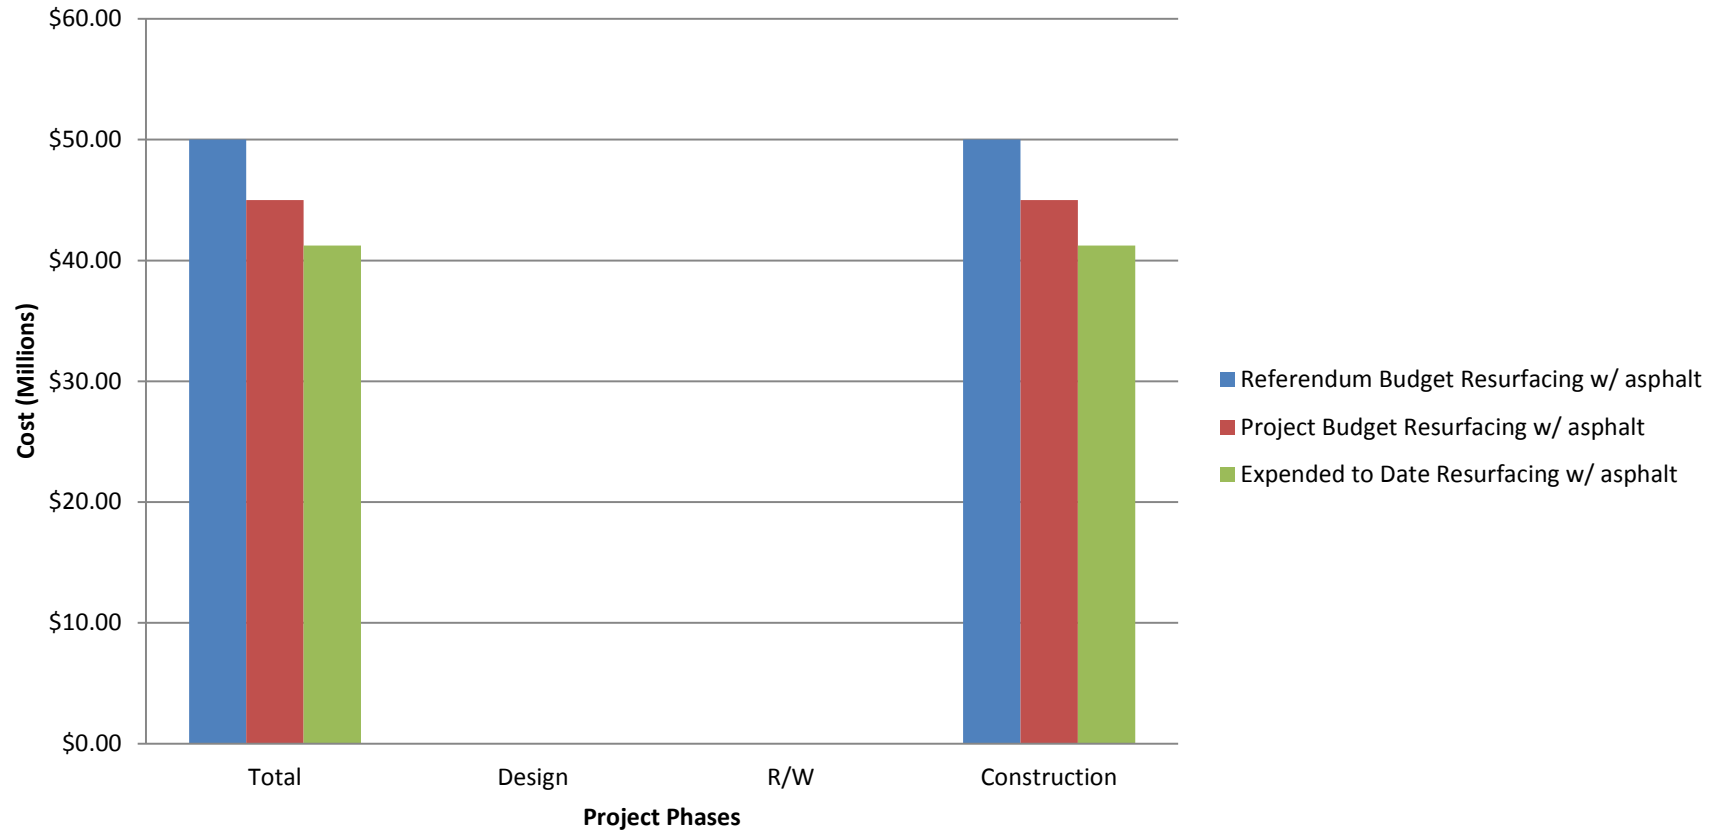


Project Status: Ongoing

Expenses are updated through: December 31, 2020

*Budget reduced due to bids being received.


Cel River Cherry Street to Dave Lyle Blvd

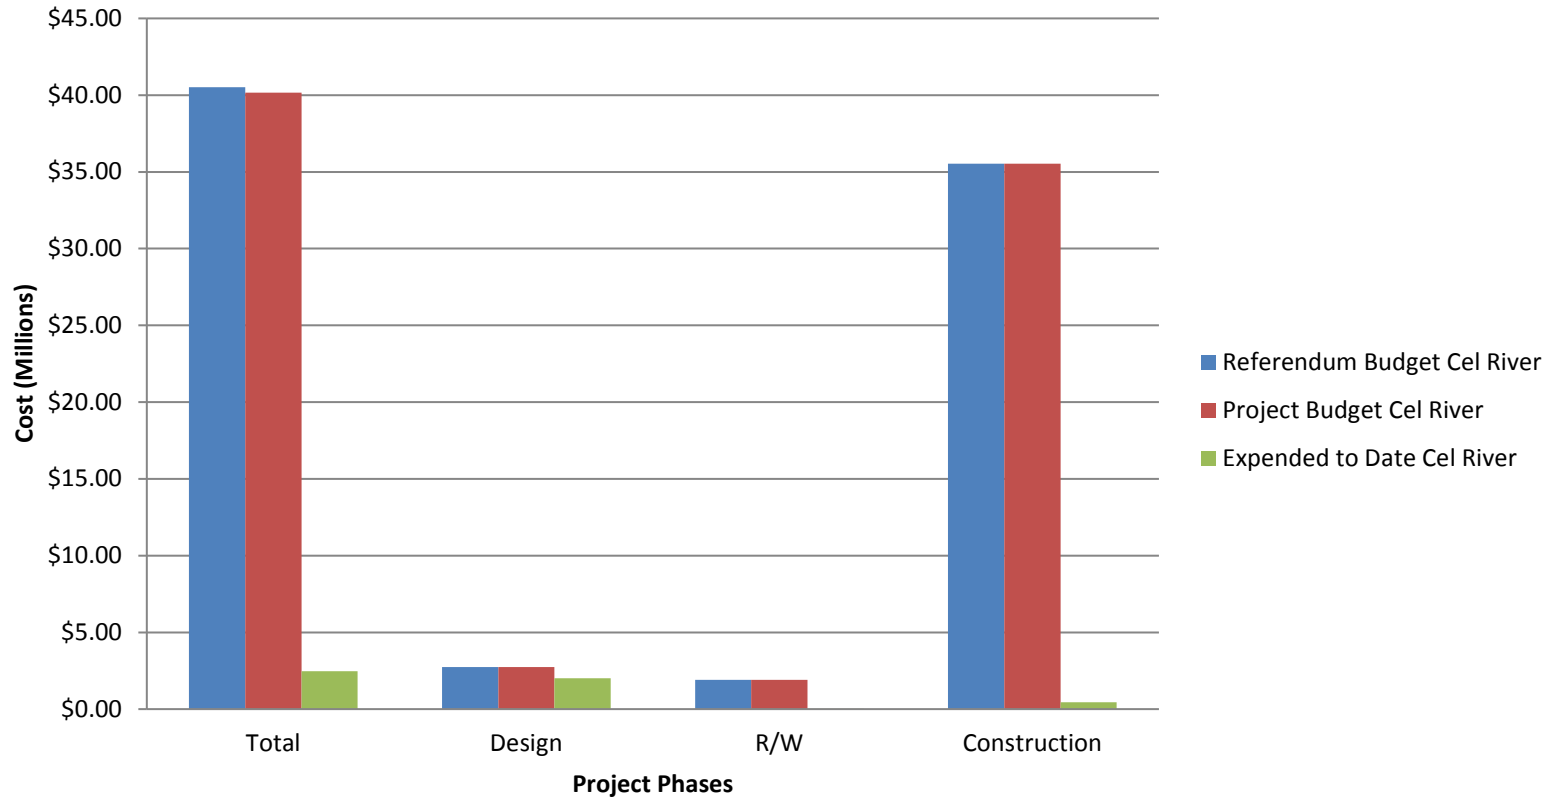

Project Status: 70% plans
 Expenses are updated through: December 31, 2020

Galleria Blvd. extension is in final plans stage and is expected to begin construction in Spring 2021.


FMSB I-77 to Railroad Bridge

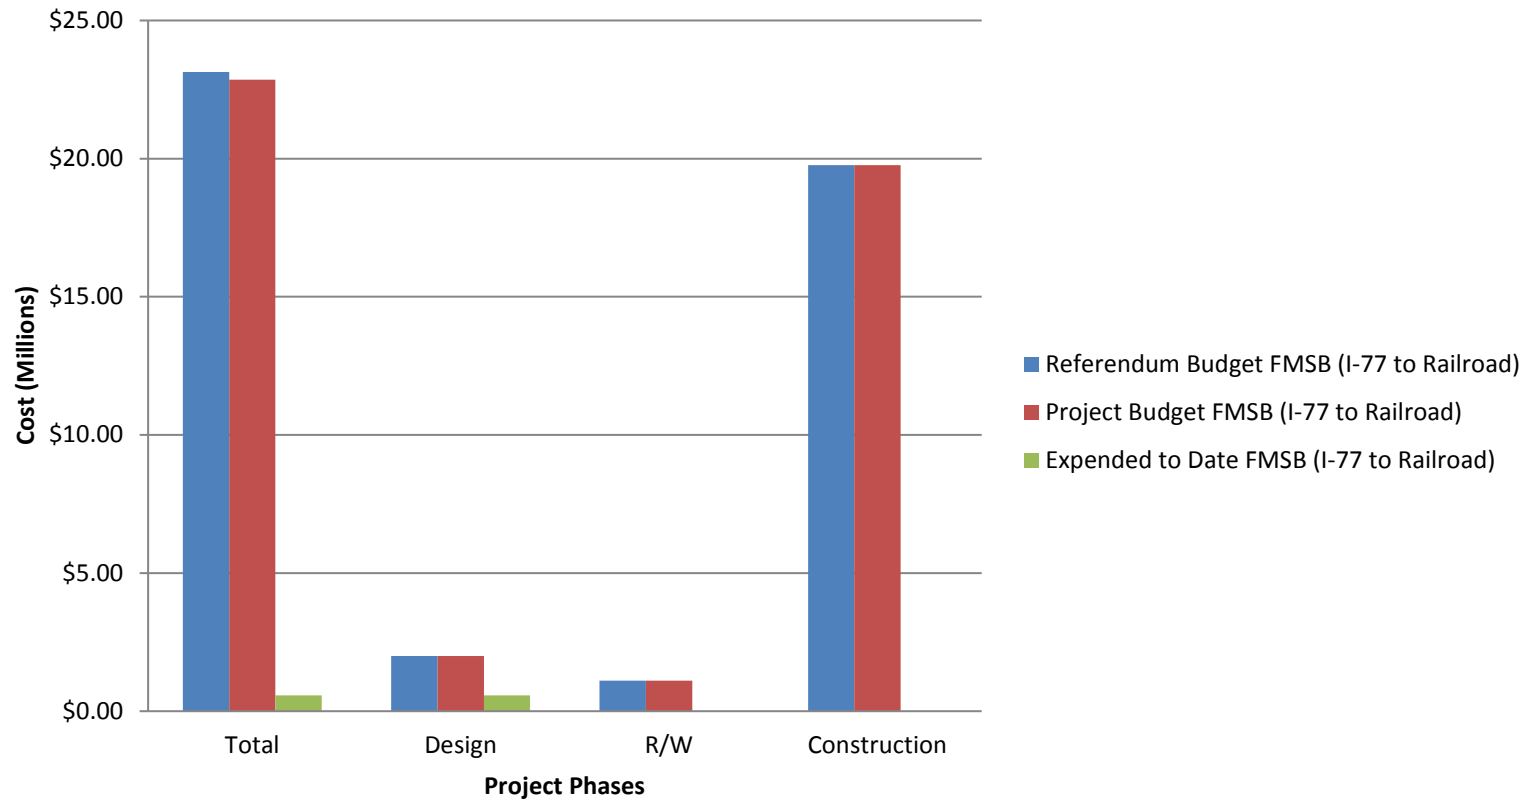

Project Status: 30% plans


Expenses are updated through: December 31, 2020

SC 557 Kingsburry Road to Highway 55

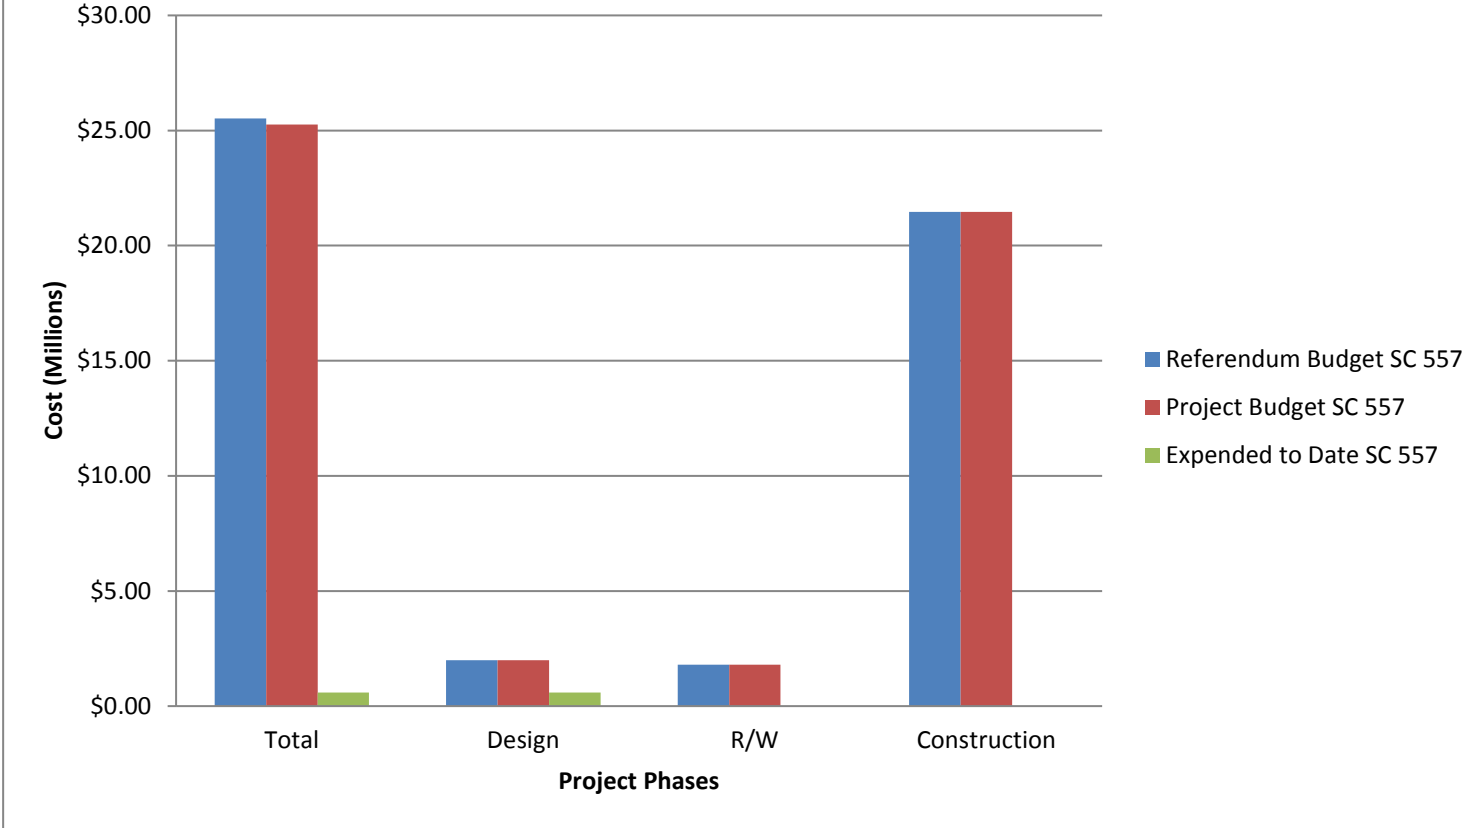


Project Status: 30% plans
Expenses are updated through: December 31, 2020

Hubert Graham Ext. Windhaven Development to Dry Run Road

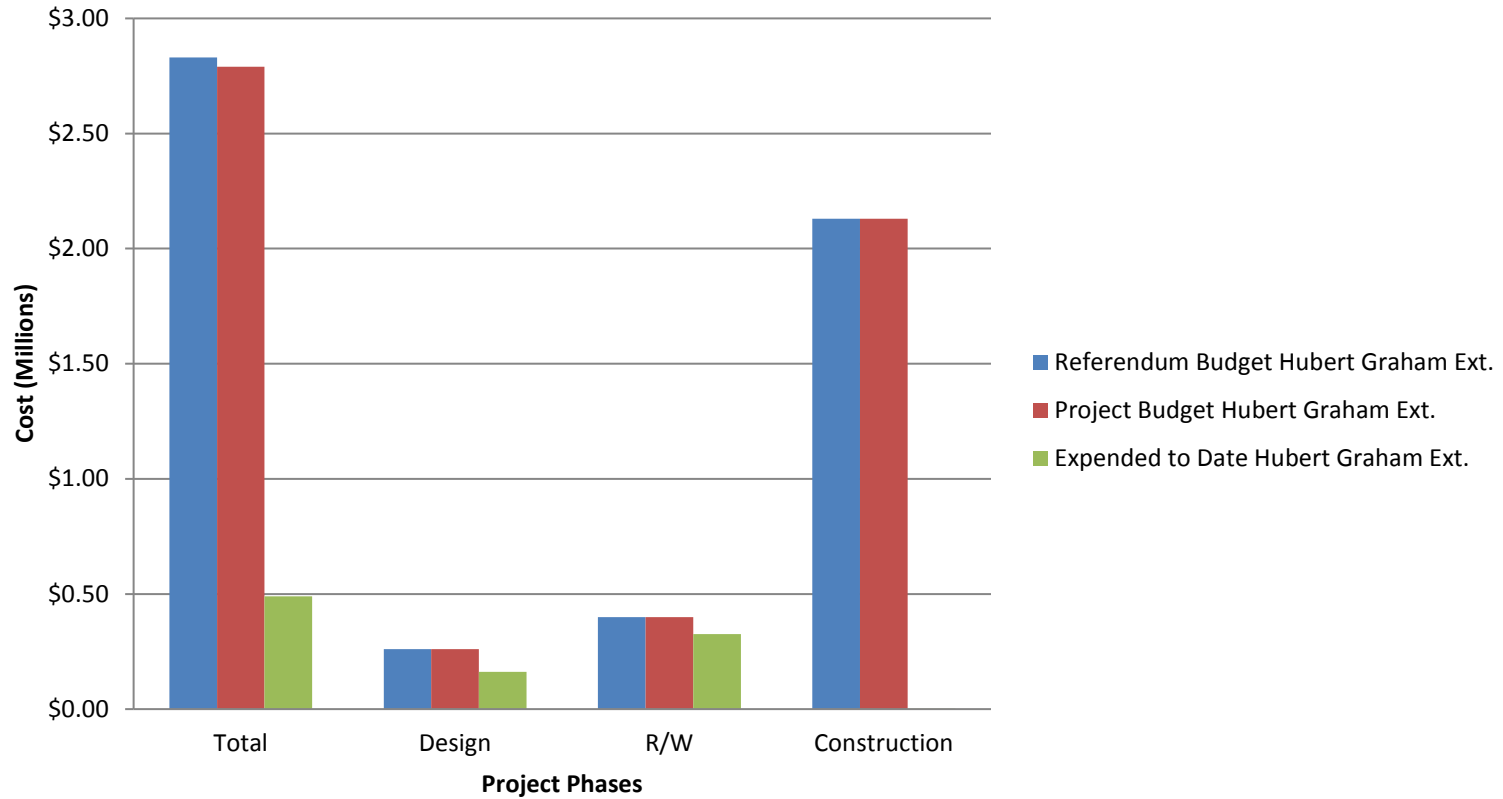

Project Status: Acquiring Right-of-Way
 Expenses are updated through: December 31, 2020


SC 49 / 274 / 557

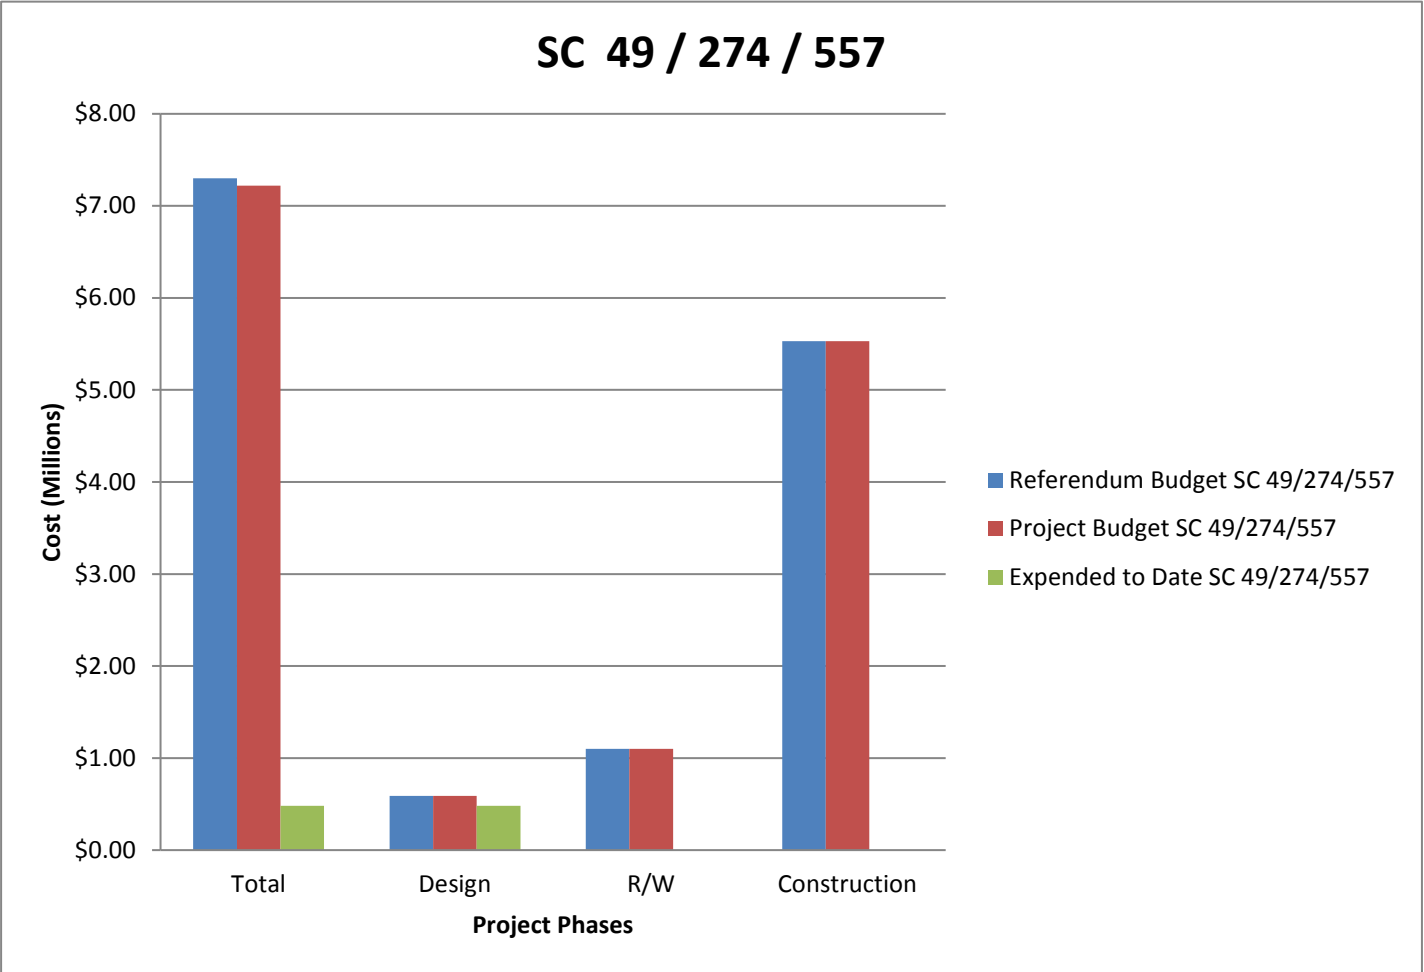

Project Status: 70% plans

Expenses are updated through: December 31, 2020

US 321 / Kings Mountain

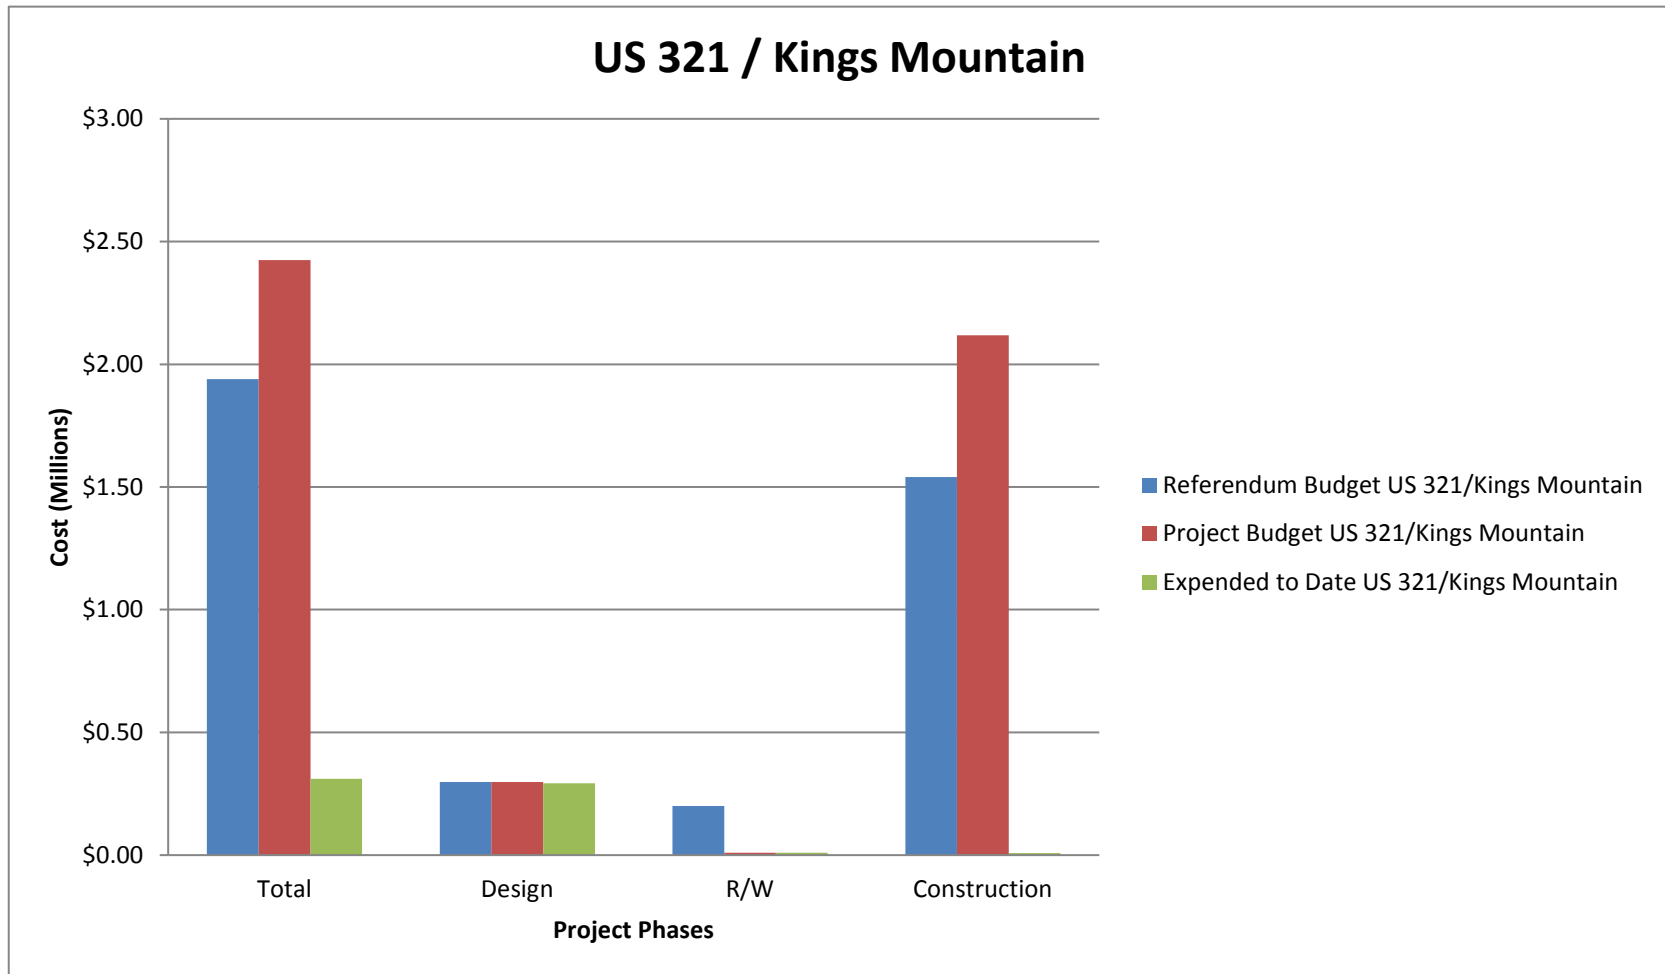


Project Status: Bid Phase

Expenses are updated through: December 31, 2020

Right-of-Way Budget reduced due to no acquisitions.

Project budget increased based on final design

US 21 / Springdale

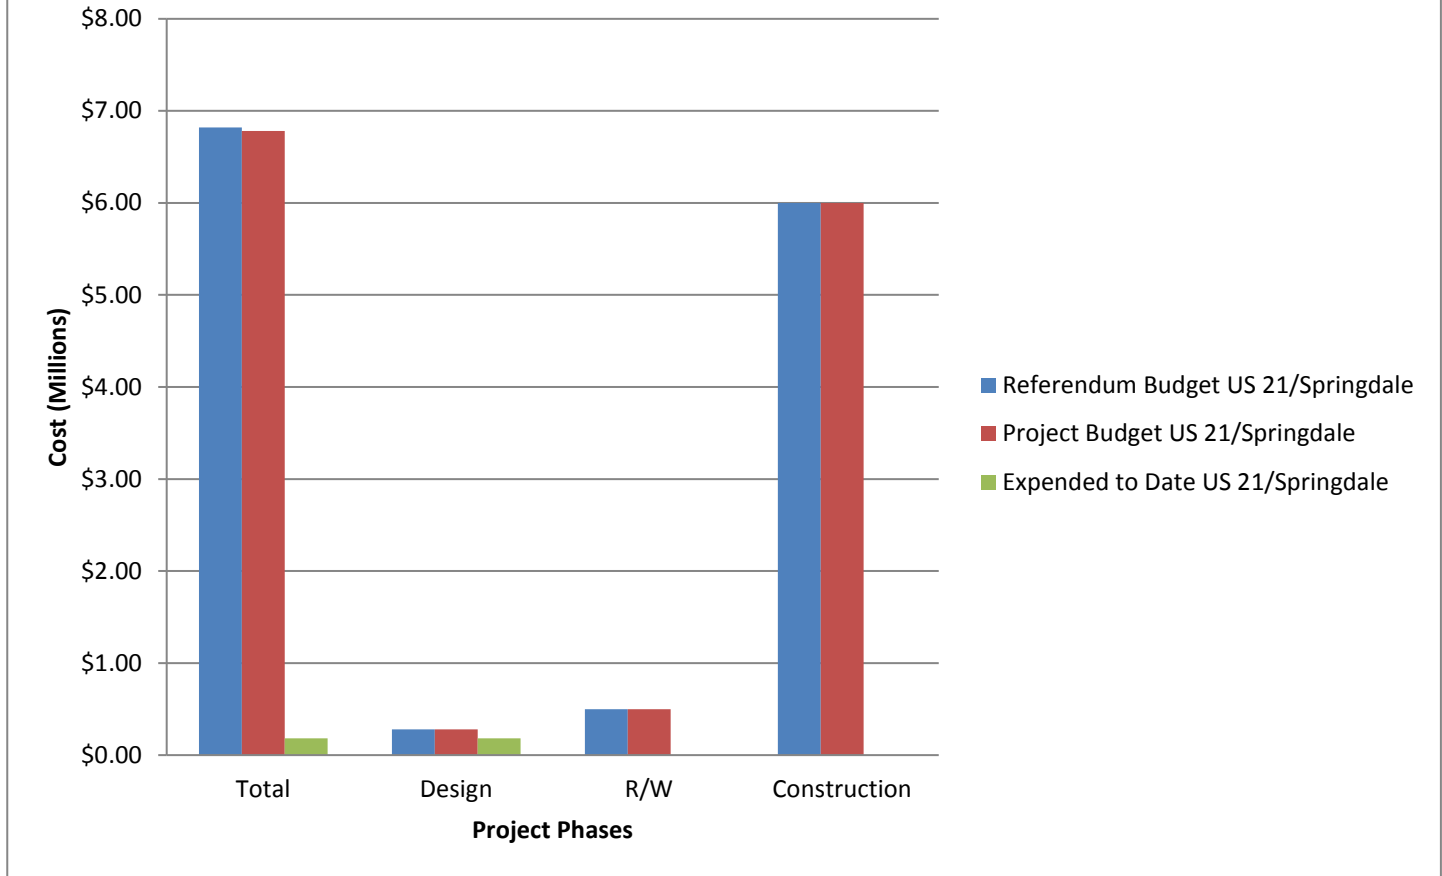


Project Status: 30% plans

Expenses are updated through: December 31, 2020

Sutton Road Left Turns

New Gray Rock Road, Sam Smith Road, Harris Road

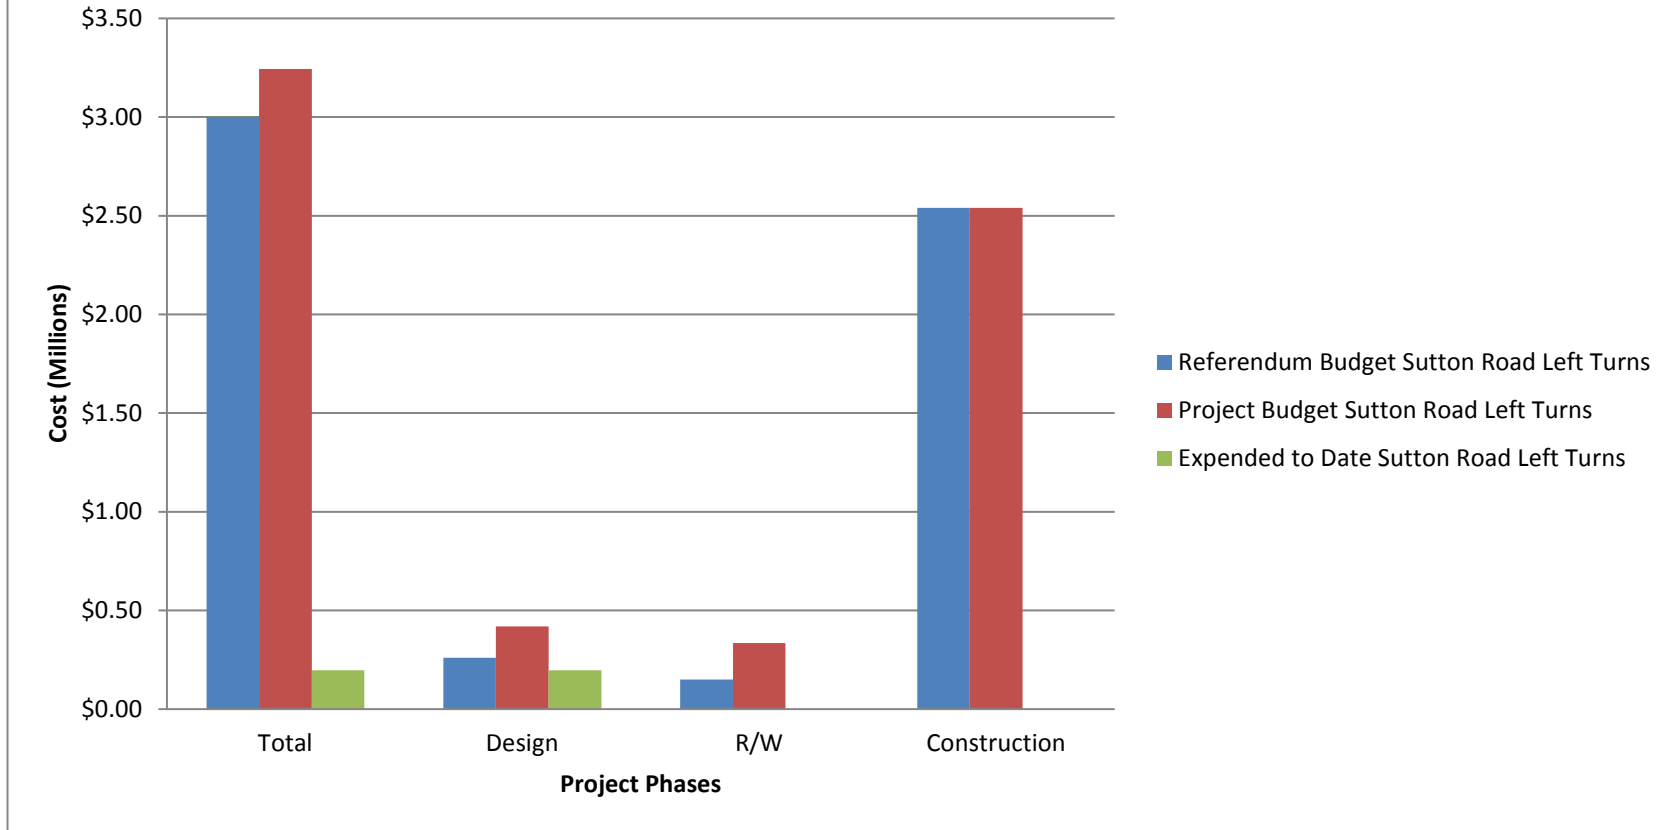


Project Status: 70% plans

Expenses are updated through: December 31, 2020

Budget increased due to design change based on feedback at public meeting.


Flint Hill Street Community Drainage

Frank Street, Oates Street, Haynes Street, Russell Street

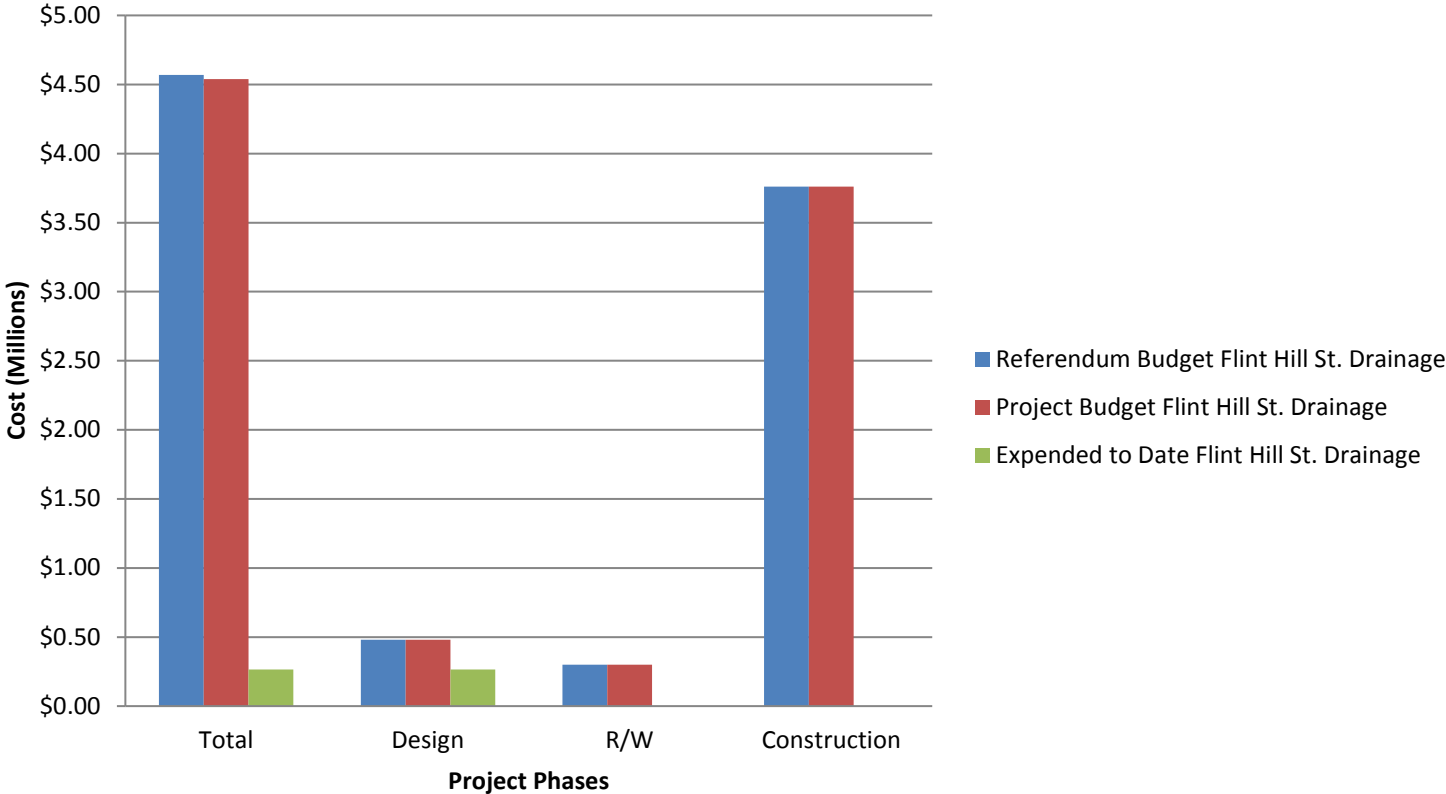

Project Status: Working towards 70% plans
Expenses are updated through: December 31, 2020

Celanese / US 21

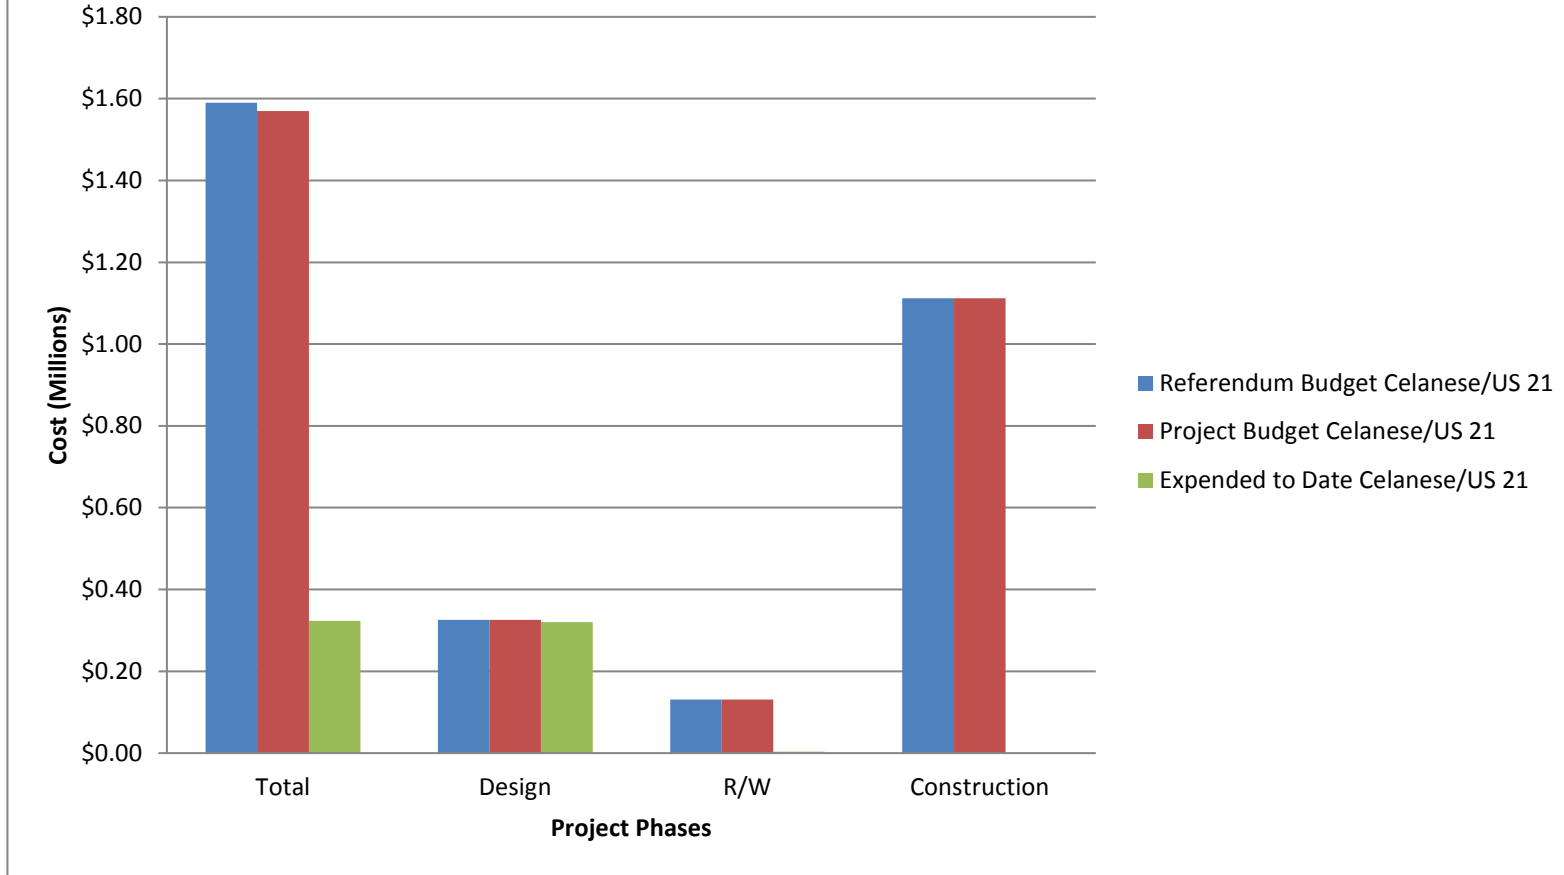


Project Status: 70% plans

Expenses are updated through: December 31, 2020

US 21 Turn Lanes

**Catawba Baptist Church, Hopewell Presbyterian Church, Benson Road,
Cannon Drive, McAllister Road**

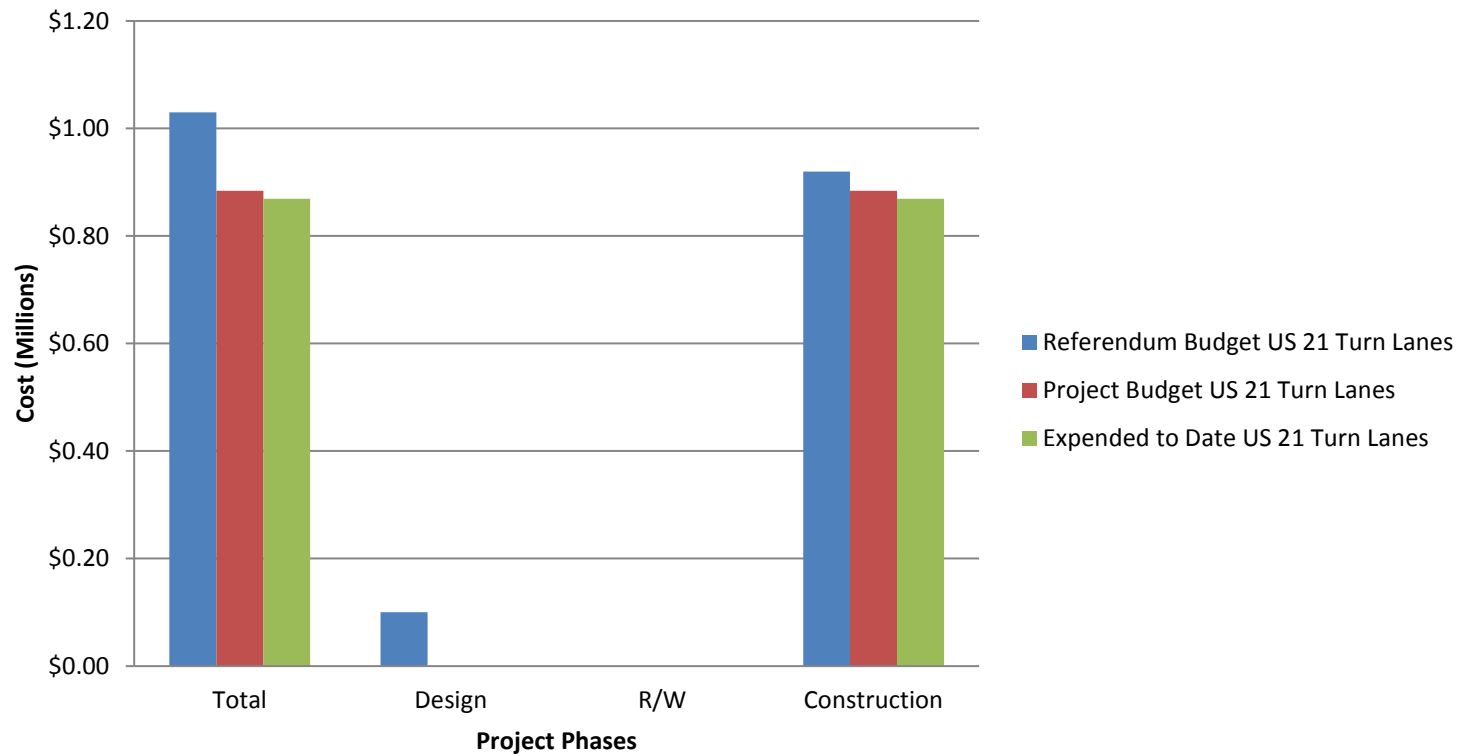


Project Status: Complete

Expenses are updated through: December 31, 2020

Project Budget reduced due to SCDOT designing in-house, and bids being received.


Bate Harvey Shoulder Widening Highway 557 to Green Pond Road

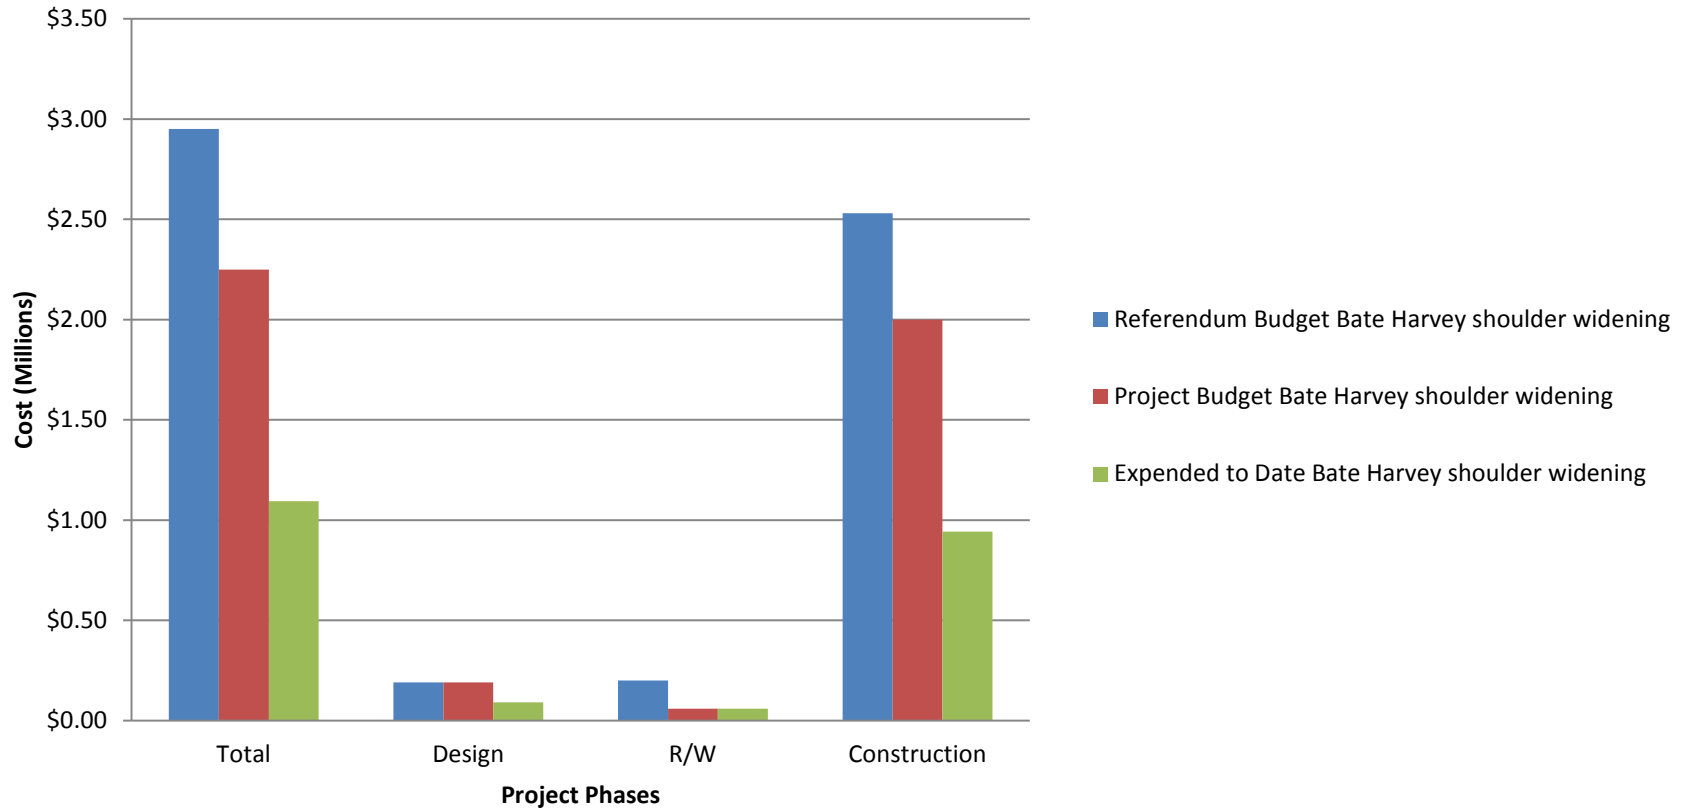

Project Status: Project Closeout
Expenses are updated through: December 31, 2020

*Budget reduced due to bids being received.


US 21 Springfield Parkway to Highway 160

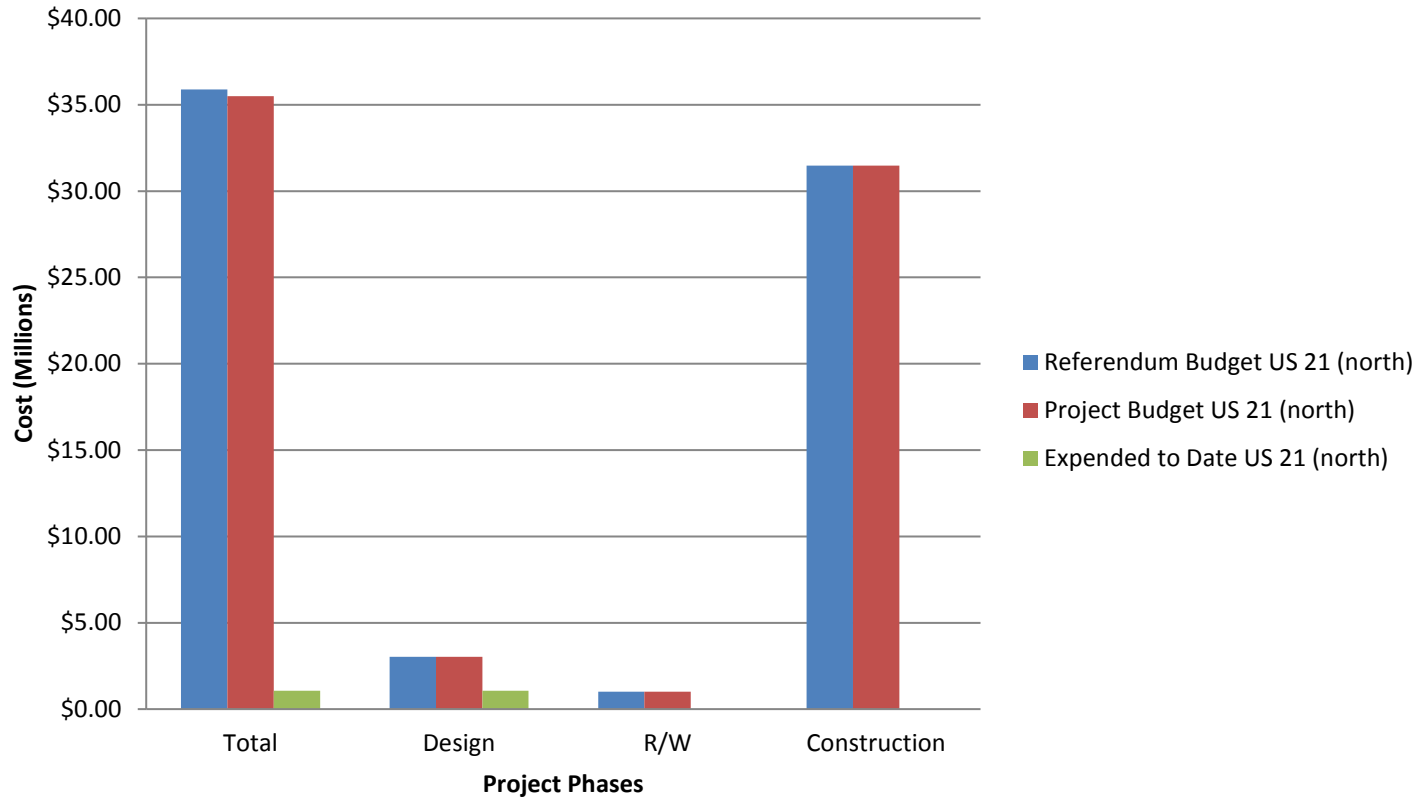

Project Status: 30% plans

Expenses are updated through: December 31, 2020

Neely Road Robertson Road to Crawford Road

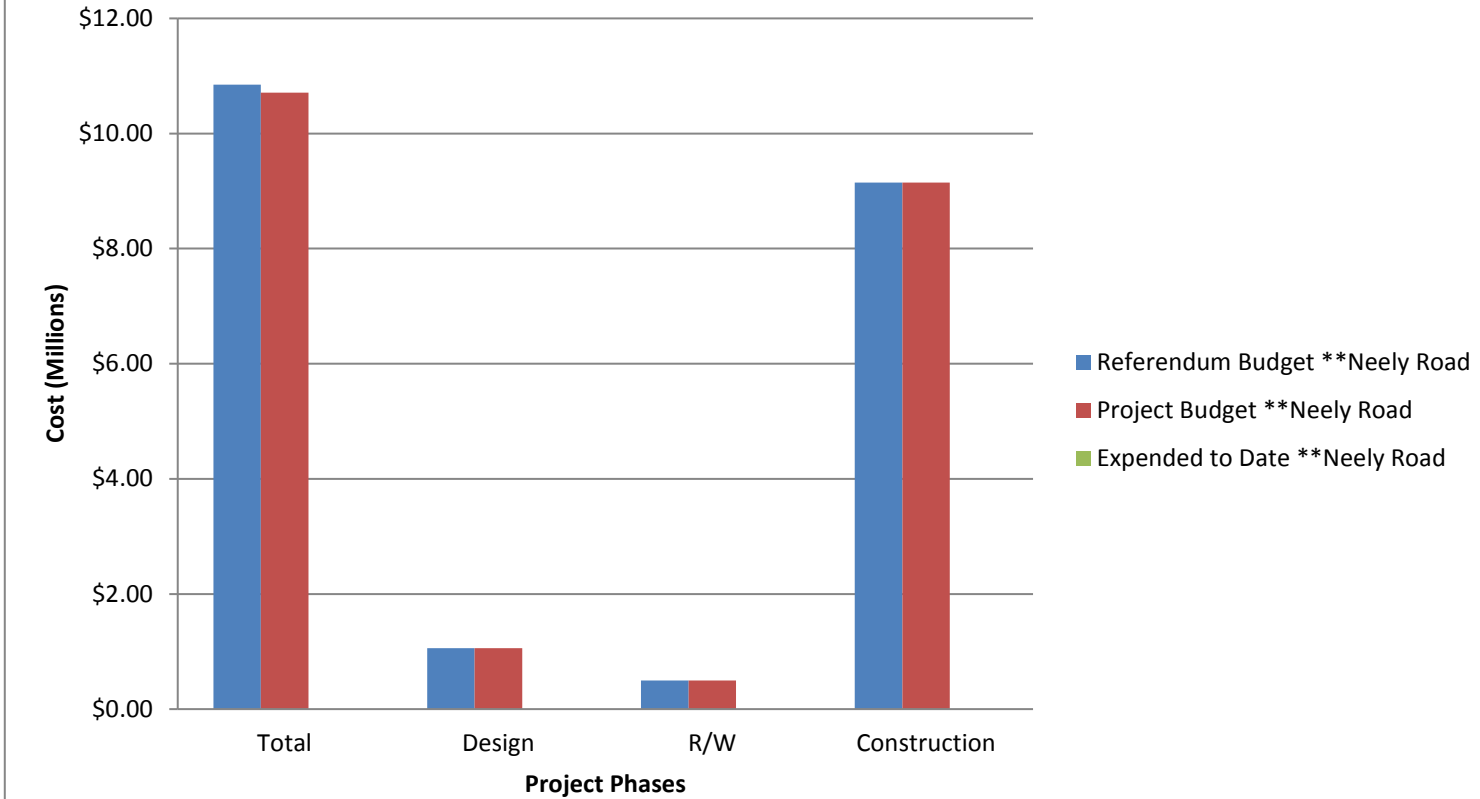

Project Status: On hold

Expenses are updated through: December 31, 2020
